


Job Name: 25-3479 - Phase 24 Wastewater System Improvements Job Location: Columbia, KY Contractor: Cumberland Pipeline LLC	Plant: 100	Tech: J. Horsley - F
	3/23/2026 1:51:21 PM	PC: E. Bradley

**Structure ID: A-3**


**P2 MH048CN36CDARED**

**ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G**

P4) 24" - CASTING HEIGHT - 7"	0 lb	<u>Structure Notes:</u> 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING BY ICAST (HOE MC-375 F/C SANITARY) 5. 8.5" EXTERNAL CHIMNEY SEAL BY ICAST
P3) 24" - GRADE RING w/ConBlock-CDA Red F/F - 4"	270 lb	
P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 36"	2251 lb	REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
P1) 48" - MH BASE w/FLANGE (08F/08EF) w/ConBlock-CDA Red T/n - 36"	5339 lb	
1) ADMIXTURE CONBLOCK CDA RED	0 lb	
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT	1440 lb	
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb	
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb	
1) CASTING - HOE MC-375 F/C Sanitary	271 lb	
1) 48" - Conseal CS-102 1.00"	0 lb	
2) A-Lok - 0285	2 lb	
6) MH Step ML-10-TDS-NCR - 10"	0 lb	
Structure Total:	9573 lb	

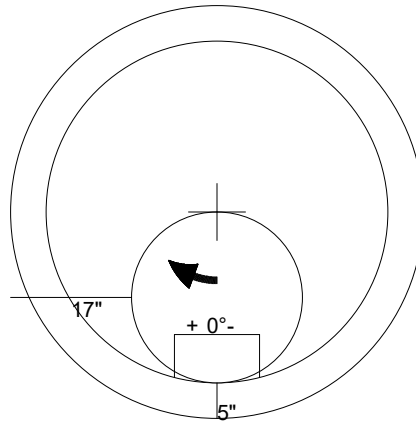

48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 36" - (P2)



Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 2251 lb Volume (Net): 0.57cu.yd
----------------------------------	----------------------------------	--------------------	-------------------	--
