



Structure ID: B1

P2 MH048RS48XS



MH RISER w/XYPEX/NO STEP T/G

P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC XYPEX CONE w/ 24" HOLE-SPECIAL F/G - 24" P2) 48" - MH RISER w/XYPEX/NO STEP T/G - 48" P1) 48" - MH BASE w/XYPEX T/n - 30" 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) JOINT WRAP - 0.065"x12"x50' CONSEAL CS212 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) ADMIXTURE XYPEX C-1000 RED 1) CASTING - HOE MC-375-SS F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 16Y NYLO	0 lb 1740 lb 3353 lb 3255 lb 0 lb 0 lb 1440 lb 0 lb 271 lb 0 lb 16 lb	Structure Notes: STATION: 1+66.98 LN S-1 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 5,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. XYPEX C-1000 ADMIXTURE REQUIRED 5. NO STEPS 6. HOE MC-375 FRAME & SELF-SEAL COVER "SANITARY" SUPPLIED BY ICAST
Structure Total: 10075 lb		


Rim: 453.16' Rim to Invert: 9.13' Slack: 3.56" Sump: 3" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

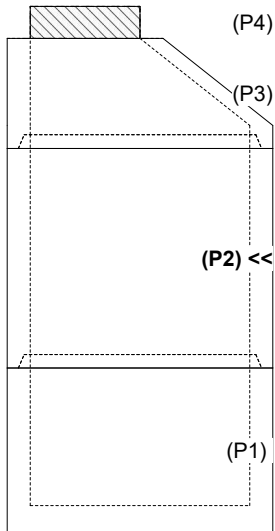

INSIDE WALL DIMENSIONS

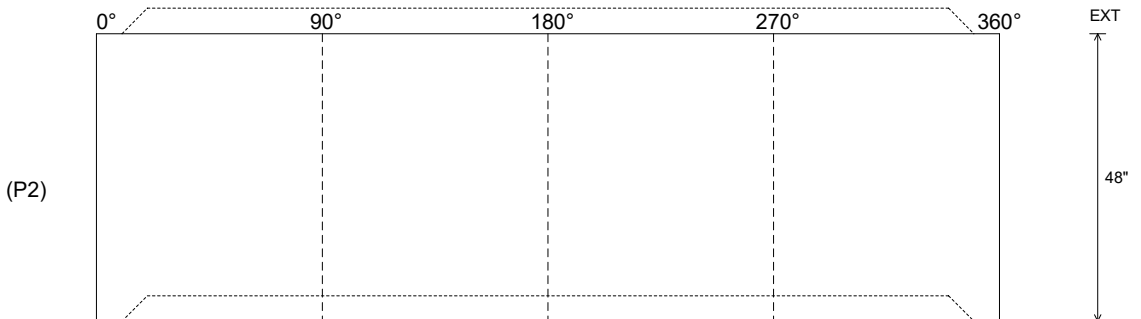

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 48" Height (Ext): 48"	Weight (Net): 3353 lb Volume (Net): 0.86cu.yd
----------------------------------	------------------------------------	--	--	--
