


Job Name: 25-3480 - Noel Ave Sewer Improvements Ph 3
 Job Location: Madisonville, KY 42431
 Contractor: Luttrell & Sons, LLC

Plant: 100

Tech: J. Horsley - A

3/6/2026 8:51:26 AM

PC: Andy Chambers



Structure ID: B2

P2 MH048RS48XS

MH RISER w/XYPEX/NO STEP T/G



P4) 24" - CASTING HEIGHT - 7"	0 lb
P3) 48" - XYPEX MH FLAT TOP w/24" ECC Hole F/G - 12"	2205 lb
P2) 48" - MH RISER w/XYPEX/NO STEP T/G - 48"	3353 lb
P1) 48" - MH BASE Custom Ht, w/XYPEX T/n - 41"	3975 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) JOINT WRAP - 0.065"x12"x50' CONSEAL CS212	0 lb
1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT	1440 lb
1) ADMIXTURE XYPEX C-1000 RED	0 lb
1) CASTING - HOE MC-375-SS F/C Sanitary	271 lb
2) 48" - Conseal CS-102 1.00" (Double)	0 lb
2) PSX - 16Y NYLO	16 lb
1) PSX - 12-08 NYLO	8 lb
Structure Total:	11268 lb

Structure Notes:
 STATION: 3+03.10 LN S-1
 1. PER ASTM C-478 SPECIFICATIONS
 2. CONCRETE: 5,000 PSI AT 28 DAYS
 3. REINFORCEMENT: PER ASTM A615
 4. XYPEX C-1000 ADMIXTURE REQUIRED
 5. NO STEPS
 6. HOE MC-375 FRAME & SELF-SEAL COVER
 "SANITARY" SUPPLIED BY ICAST


Rim: 454' Rim to Invert: 8.85' Slack: 1.2" Sump: 3" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

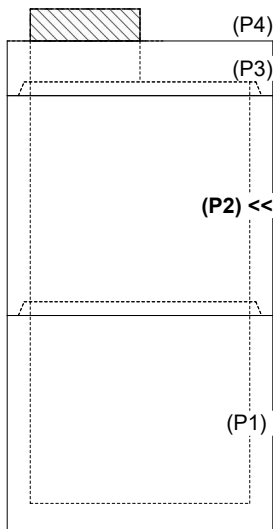

INSIDE WALL DIMENSIONS

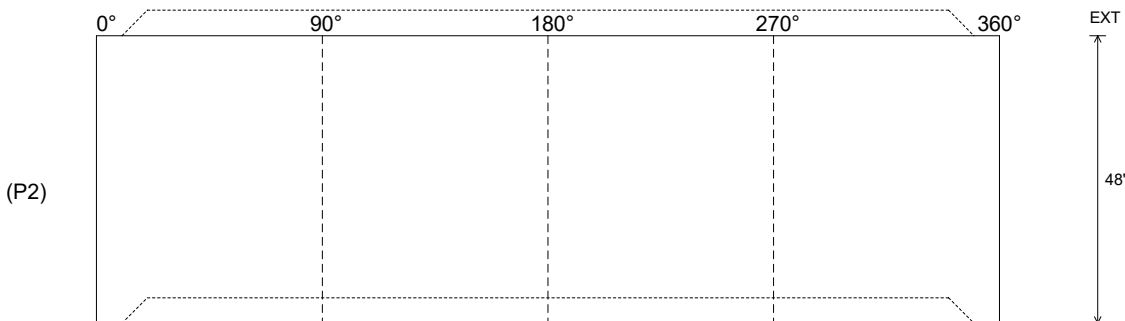

Coating (Int):
 Coating (Ext):

Seam Up: Tongue
 Seam Dn: Groove

Wall Thickness: 5"
 Floor Height: 0"

Height (Int): 48"
 Height (Ext): 48"

Weight (Net): 3353 lb
 Volume (Net): 0.86cu.yd
