




Job Name: 25-3575 - Berry Global North Parking Lot Consolidation Job Location: Evansville, IN 47710 Contractor: Deig Bros Lumber & Construction Co, Inc.				Plant: 100 6/16/2026 8:47:27 PM		Tech: Jared - F PC: A. Chambers				
Structure ID: AD104										
P1 MH048BAVF		MH BASE Custom Ht T/n								
P3) 24" x 24" - CASTING HEIGHT - 4" P2) 48" - MH FLAT TOP w/24"x24" Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 58" 1) CASTING - HOE 280T F/G 1) CASTING - BMP SNOOT 18R w/ KIT 1) 48" - Conseal CS-102 1.00" 1) 24" x 24" - Conseal CS-102 1.00" 2) Hole - 16						0 lb 1500 lb 5211 lb 182 lb 25 lb 0 lb 0 lb 0 lb ----- 6918 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING SUPPLIED BY ICAST (HOE 280T F/G). 5. 18R SNOOT SUPPLIED BY ICAST. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
Rim: 384.12' Rim to Invert: 3.29' Slack: 1.48" Sump: 36" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	380.83'	0°	0"	12" HDPE	14.5"	Hole 16	16"	16.312"	34.75"	0"
Invert 2	380.83'	180°	91.125"	12" HDPE	14.5"	Hole 16	16"	16.312"	34.75"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

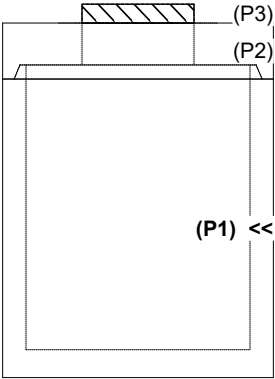


RIGHT-SIDE UP VIEW (int. dimensions)

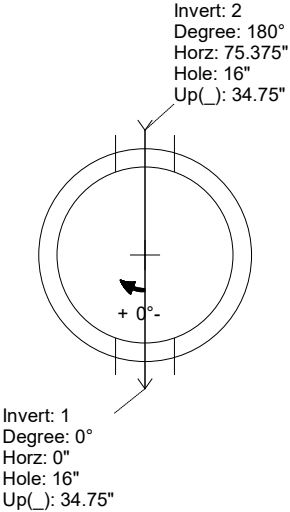

UPSIDE-DOWN VIEW (int. dimensions)

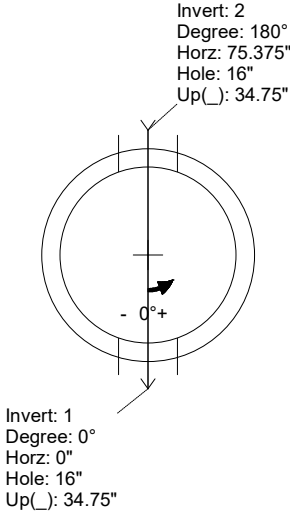

INSIDE WALL DIMENSIONS

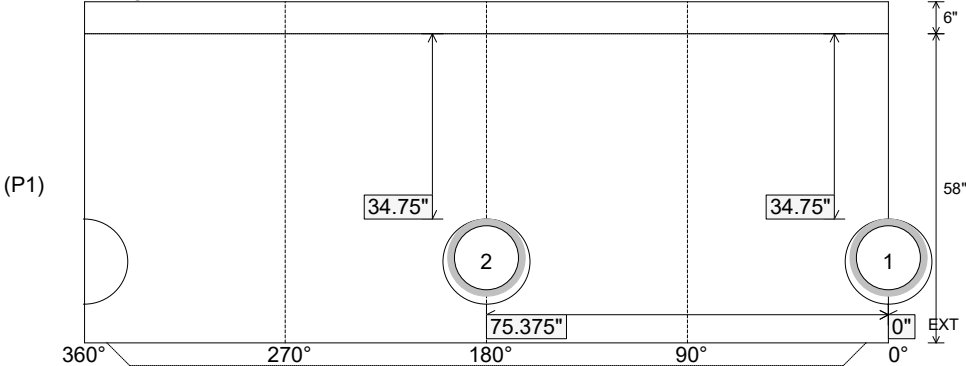

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 58" Height (Ext): 64"	Weight (Net): 5211 lb Volume (Net): 1.33cu.yd
----------------------------------	---------------------------------	--	--	--
