

Job Name: 25-3575 - Berry Global North Parking Lot Consolidation
Job Location: Evansville, IN 47710
Contractor: Deig Bros Lumber & Construction Co, Inc.

Plant: 100

6/16/2026 8:48:22 PM

Tech: Jared - F

PC: A. Chambers



Structure ID: CI106

P2 MH048LD12-24X36RECT



MH FLAT TOP w/24"x36" Hole F/G

- P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/24"x36" Hole F/G - 12"
P1) 48" - MH BASE T/n - 66"
1) CASTING - HOE 525 SET FLAT GRATE (F/G/H)
1) CASTING - BMP SNOOT 18R w/ KIT
1) 48" - Con Seal CS-102 1.00"
1) 24" x 36" - Con Seal CS-102 1.00"
1) Hole - 22

Structure Total: 7543 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. NO STEPS AND NO INVERT CHANNEL.
 4. CASTING BY ICAST (HOE 525 SET FLAT GRATE (F/G/H)).
 5. 18R SNOOT SUPPLIED BY ICAST.
- REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

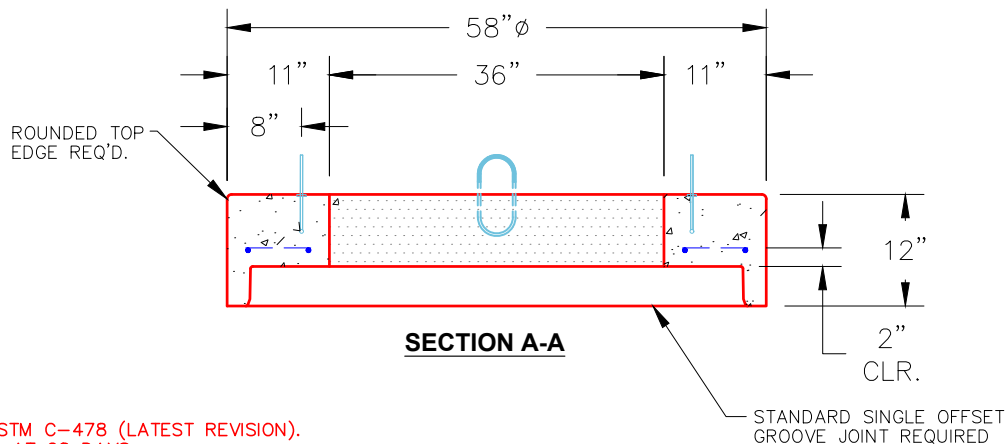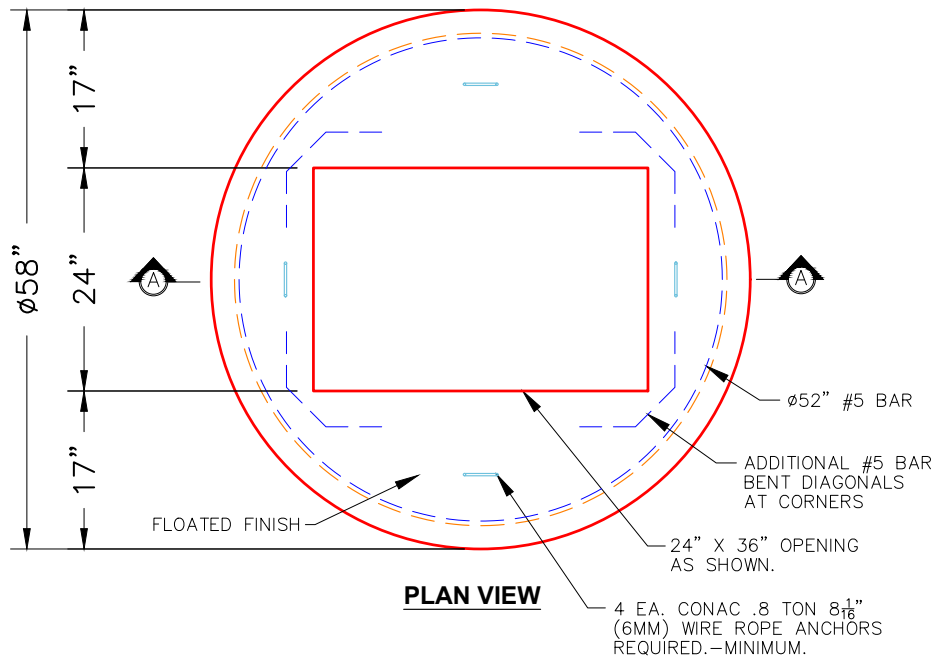

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1300 lb
Volume (Net): 0.46cu.yd
