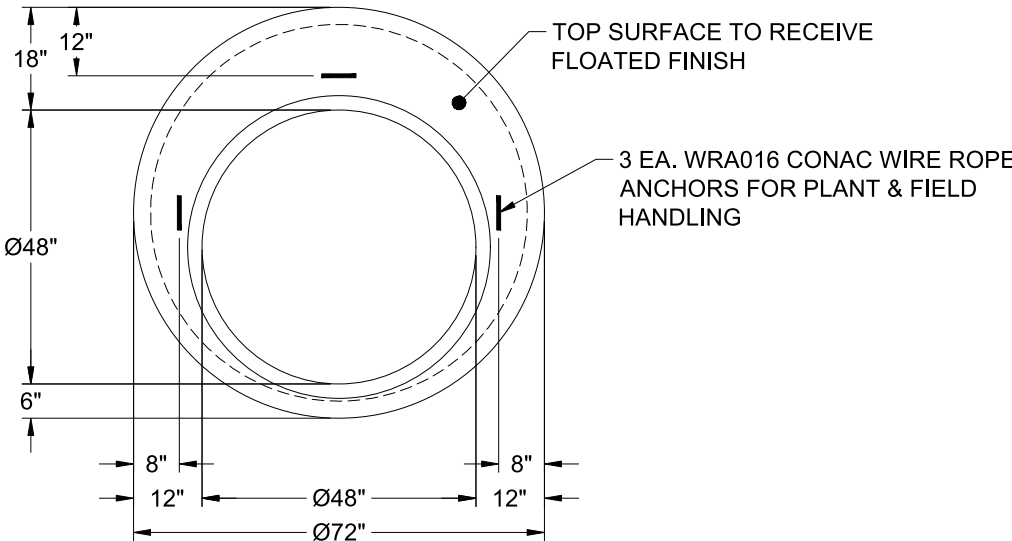
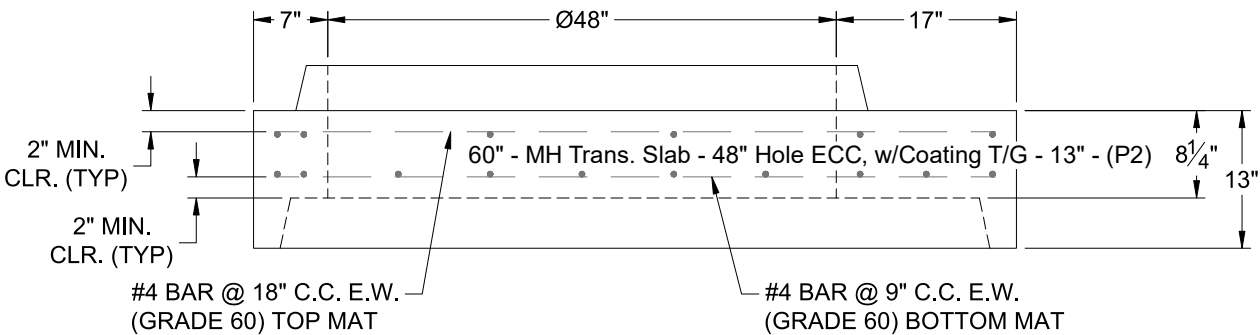


Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2 Job Location: Danville, KY Contractor: Hubert Excavating & Contracting		Plant: 100 6/7/2026 1:26:03 PM	Tech: J. Horsley PC: C. Goff	
Structure ID: MH A10		P2 MH060TS13-48ECC		
MH Trans. Slab - 48" Hole ECC, w/Coating T/G				
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 36" P3) 48" - MH RISER w/COATING T/G - 36" P2) 60" - MH Trans. Slab - 48" Hole ECC, w/Coating T/G - 13" P1) 60" - MH BASE w/FLANGE (08F/07EF) w/Coating T/n - 72" 1) JOINT WRAP - 12" WD x 060" MAC WRAP 1) 60" - MH INVERT CHANNEL - FULL HEIGHT 1) SPECIAL EXTERNAL COATING - Carboline 300M 2) JOINT WRAP - 12" WD x 048" MAC WRAP 1) SECONDARY POUR - Extended Flange 1) 60" - Conseal CS-102 1.00" (Double) 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 1040 12) MH Step ML-10-TDS-NCR - 10" 260.44 SqFt) Carboline Bitumastic 300M [EXT]		0 lb 2251 lb 2515 lb 1928 lb 10483 lb 0 lb 2692 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 2 lb 0 lb 0 lb	Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT - 2" MIN. REBAR CLEARANCE (TYP): - TOP MAT: #4 BAR @ 18" C.C. E.W. (GRADE 60) - BOTTOM MAT: #4 BAR @ 9" C.C. E.W. (GRADE 60) 4. CARBOLINE 300M EXTERIOR COATING REQUIRED 5. HOE MC-375 FRAME & COVER "SANITARY" SUPPLIED BY OTHERS 6. LIFTERS: 3 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING 7. TOP SURFACE TO RECEIVE FLOATED FINISH	
Structure Total:		19871 lb		
				
				
Coating (Int): Coating (Ext): Carboline Bitumastic 300M	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 6"	Height (Ext): 13"	Weight (Net): 1928 lb Volume (Net): 0.49cu.yd

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer
Ph 2

Structure:

MH A10

Note:

This Structure Is To Receive An
External Coating of Carboline 300M
(Supplied By iCast)
