

Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2

Job Location: Danville, KY

Contractor: Hubert Excavating & Contracting

Plant: 100

7/24/2026 7:35:40 AM

Tech: J. Horsley

PC: C. Goff



Structure ID: MH A10 Riser

P1 MH048RSVF

MH RISER Custom Ht

P1) 48" - MH RISER Custom Ht - 14"

1) SPECIAL EXTERNAL COATING - Carboline 300M

2) JOINT WRAP - 12" WD x 048" MAC WRAP

1) 48" - Conseal CS-102 1.00" (Double)

1) MH Step ML-10-TDS-NCR - 10"

17.72 SqFt) Carboline Bitumastic 300M [EXT]

978 lb

0 lb

0 lb

0 lb

0 lb

0 lb

Structure Total: 978 lb

Structure Notes: 1. PER ASTM C478 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. REINFORCING PER ASTM A615 (GRADE 60).

- RISER/WALLS (As .12)

4. CARBOLINE 300M EXTERIOR COATING REQUIRED

Rim: 902.76'

Rim to Invert: 0'


Slack: 0"

Sump: 0"


Step Position: 0°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

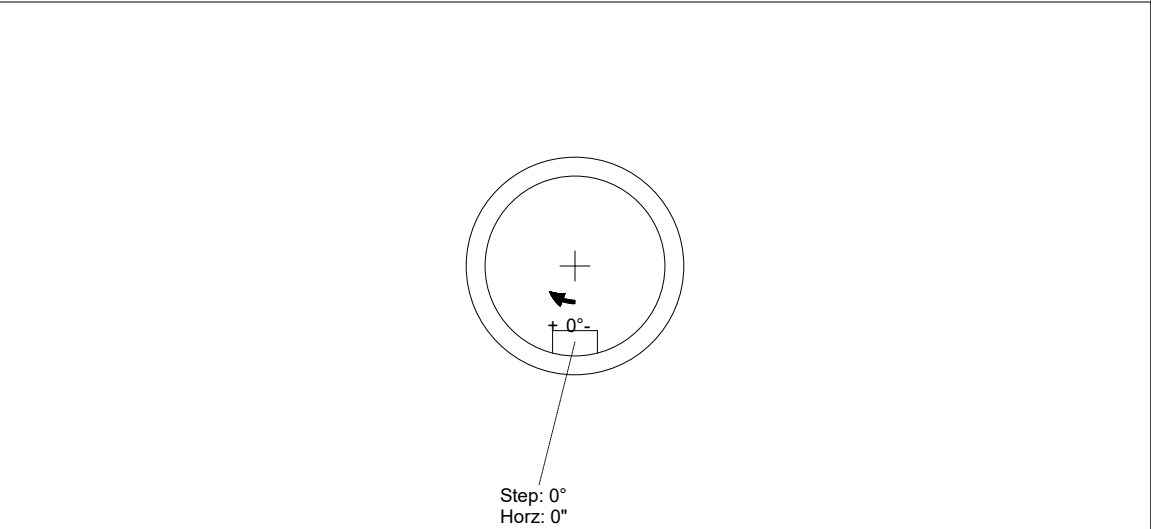

INSIDE WALL DIMENSIONS

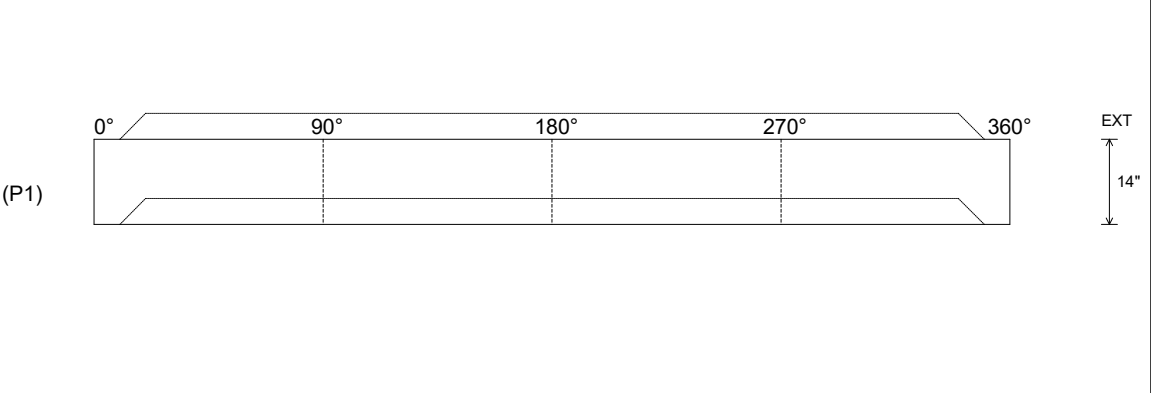

Coating (Int): Coating (Ext): Carboline Bitumastic 300M	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 14" Height (Ext): 14"	Weight (Net): 978 lb Volume (Net): 0.25cu.yd
--	------------------------------------	--	--	---
