

Contractor: Hubert Excavating & Contracting

PC:	C. Goff
TECH:	J. Horsley
Plant:	100




Structure ID: MH A10 Riser			
Spec: Sanitary	Rim: 902.76'	Sump: 0"	Floor (Bot): 901.593'
Type: SAN.MH	Invert: 902.76'	Floor (Top): 901.593'	Overall Height: 1.167'
Size: 48"	Rim to Invert: 0'	Floor Height: 0"	Slack: 0"

Structure Notes: 1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60).
- RISER/WALLS (As .12)
4. CARBOLINE 300M EXTERIOR COATING REQUIRED



STRUCTURE SUMMARY:		
P1)	48" - MH RISER Custom Ht - 14"	978 lb
1)	SPECIAL EXTERNAL COATING - Carboline 300M	0 lb
2)	JOINT WRAP - 12" WD x 048" MAC WRAP	0 lb
1)	48" - Conseal CS-102 1.00" (Double)	0 lb
1)	MH Step ML-10-TDS-NCR - 10"	0 lb
	17.72 SqFt) Carboline Bitumastic 300M [EXT]	0 lb

	Structure Total:	978 lb

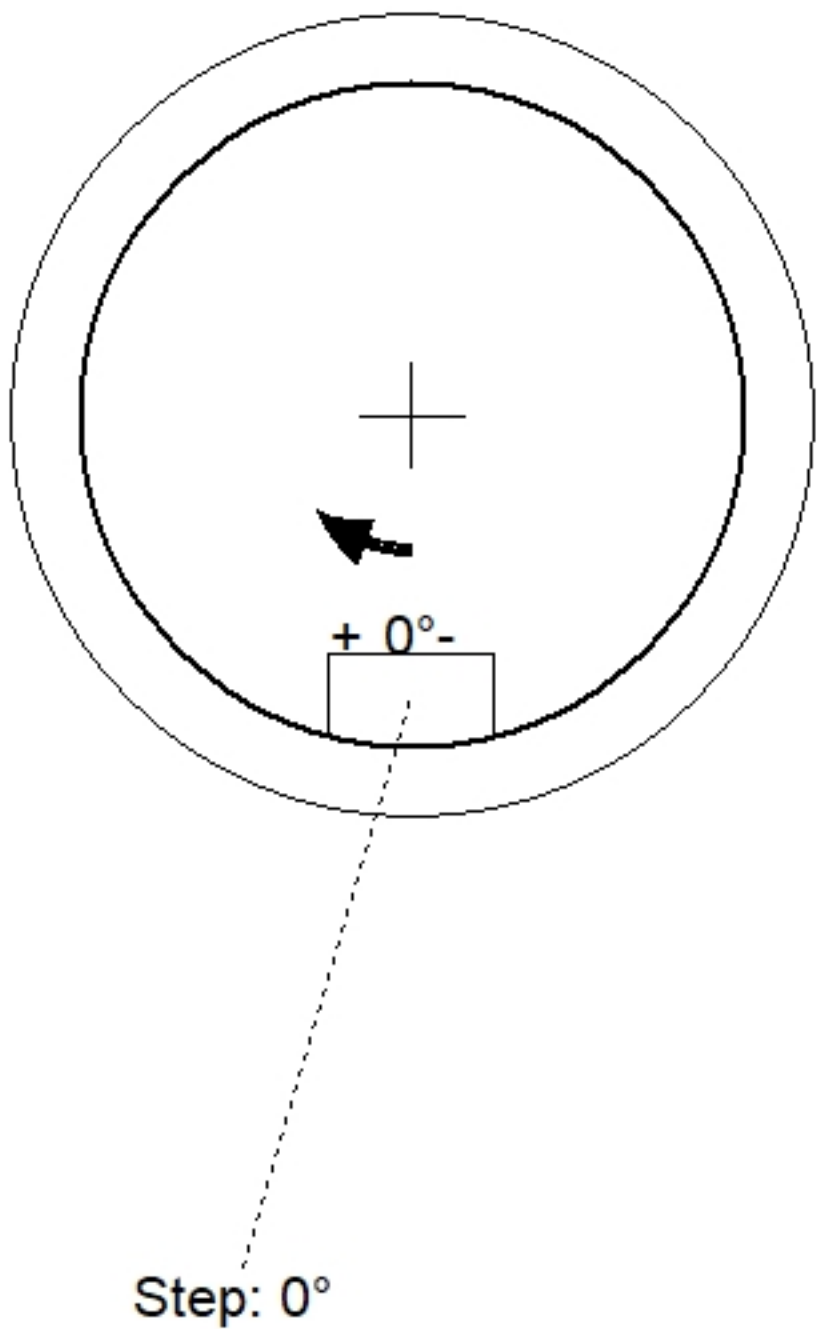

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	902.76'							
Reducer								
Invert 1								
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

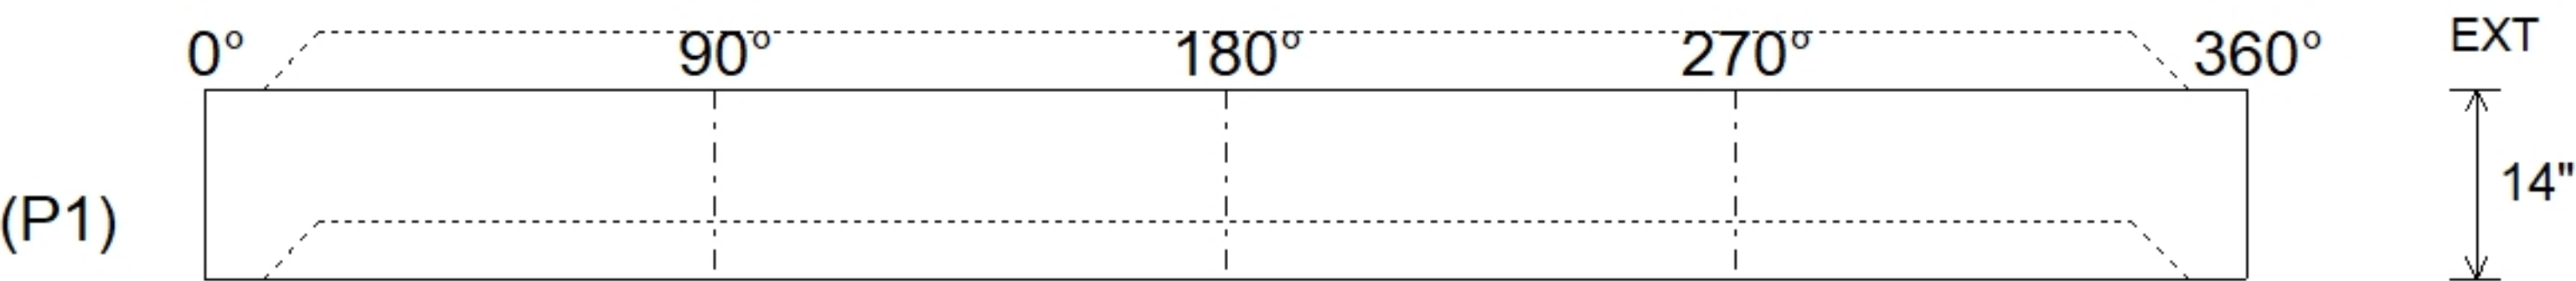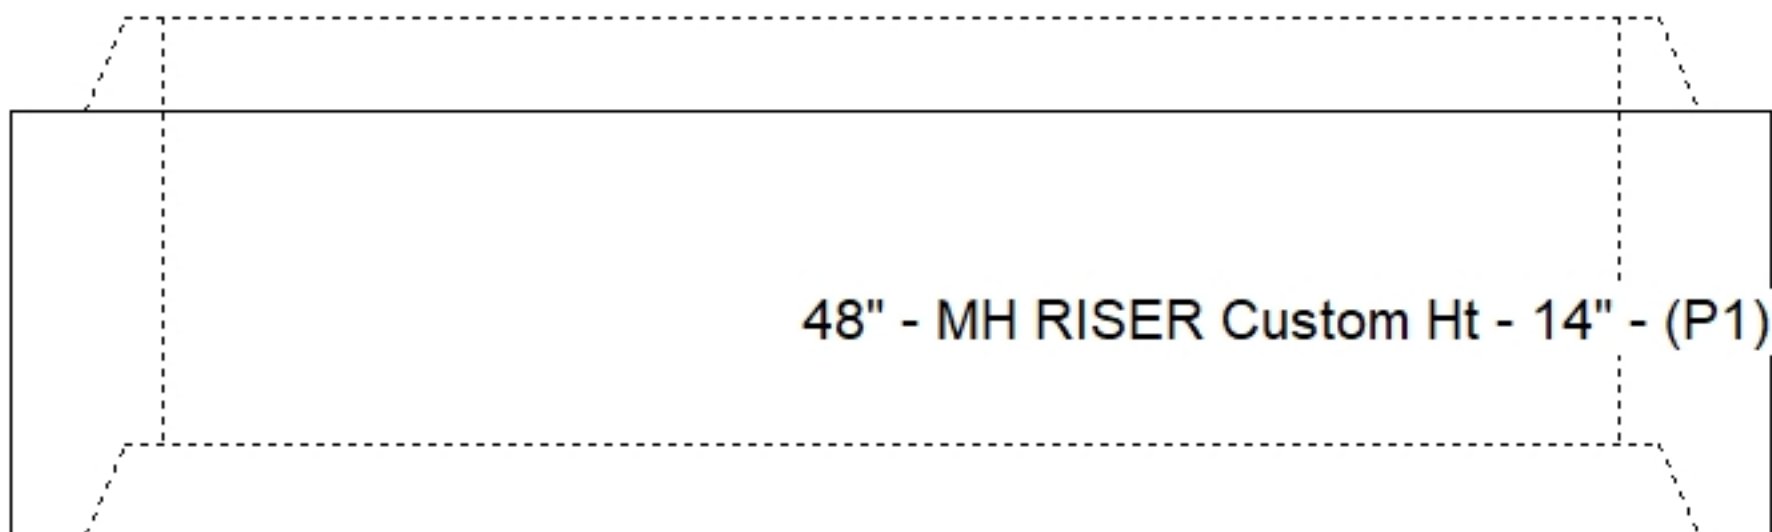

Submittal Drawing
7/27/2026 7:49:58 AM

SUBMITTAL
APPROVED BY:
