




Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2 Job Location: Danville, KY Contractor: Hubert Excavating & Contracting				Plant: 100 6/7/2026 1:25:22 PM		Tech: J. Horsley PC: C. Goff				
Structure ID: MH A11										
P2		MH060RS60S		MH RISER SPECIAL w/COATING T/G						
P4) 24" - CASTING HEIGHT - 7" P3) 60" - MH FLAT TOP w/ 24" ECC Hole F/G - 13" P2) 60" - MH RISER SPECIAL w/COATING T/G - 60" P1) 60" - MH BASE w/FLANGE (08F/07EF) w/Coating T/n - 56" 1) 60" - MH INVERT CHANNEL - FULL HEIGHT 2) JOINT WRAP - 12" WD x 060" MAC WRAP 1) SPECIAL EXTERNAL COATING - Carboline 300M 1) SECONDARY POUR - Extended Flange 2) 60" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 1040 1) PSX - 8QRS-S NYLO 9) MH Step ML-10-TDS-NCR - 10" 245.92 SqFt) Carboline Bitumastic 300M [EXT] <td colspan="2"> 0 lb 2869 lb 6238 lb 8813 lb 2692 lb 0 lb 0 lb 0 lb 0 lb 0 lb 2 lb 6 lb 0 lb 0 lb Structure Total: 20621 lb </td> <td colspan="5"> Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. CARBOLINE 300M EXTERIOR COATING REQUIRED 5. STEPS AT 278.5 DEGREES 6. HOE MC-375 FRAME & COVER "SANITARY" SUPPLIED BY OTHERS </td>				0 lb 2869 lb 6238 lb 8813 lb 2692 lb 0 lb 0 lb 0 lb 0 lb 0 lb 2 lb 6 lb 0 lb 0 lb Structure Total: 20621 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. CARBOLINE 300M EXTERIOR COATING REQUIRED 5. STEPS AT 278.5 DEGREES 6. HOE MC-375 FRAME & COVER "SANITARY" SUPPLIED BY OTHERS				
Rim: 900.6' Rim to Invert: 11.165' Slack: 0.195' Sump: 2.215' Step Position: 278.5°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3	897.6'	90°	56.5"	4" DI (vent pipe)	4.75"	PSX 8QRS-S NYLO	8"	8.024"	37.5"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)



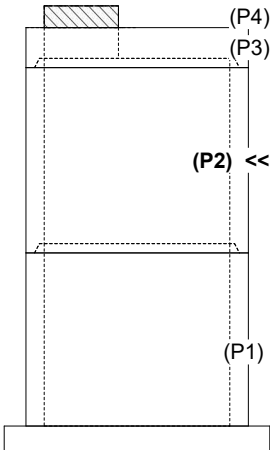

INSIDE WALL DIMENSIONS

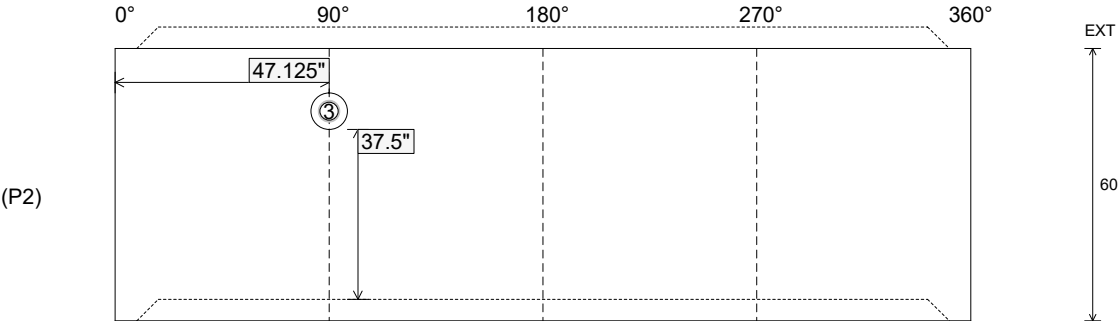

Coating (Int):
Coating (Ext): Carboline Bitumastic 300M

Seam Up: Tongue
Seam Dn: Groove

Wall Thickness: 6"
Floor Height: 0"

Height (Int): 60"
Height (Ext): 60"

Weight (Net): 6238 lb
Volume (Net): 1.59cu.yd

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer
Ph 2

Structure:

MH A11

Note:

This Structure Is To Receive An
External Coating of Carboline 300M
(Supplied By iCast)
