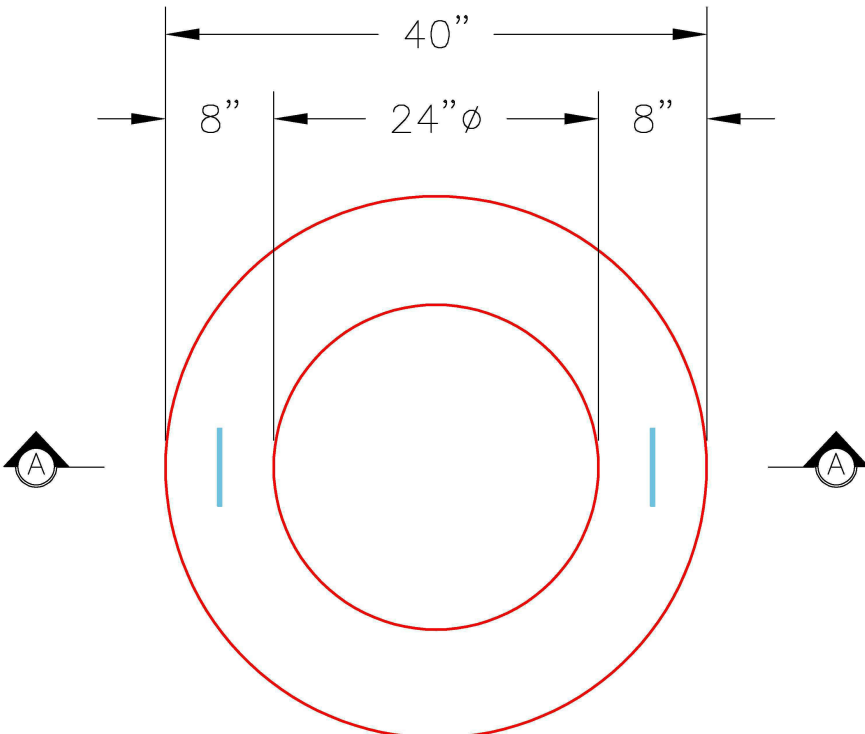
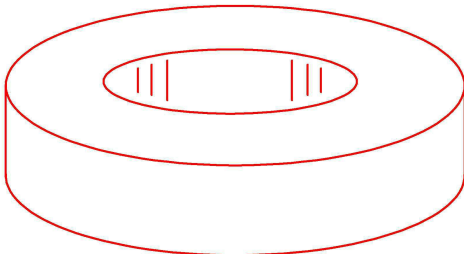
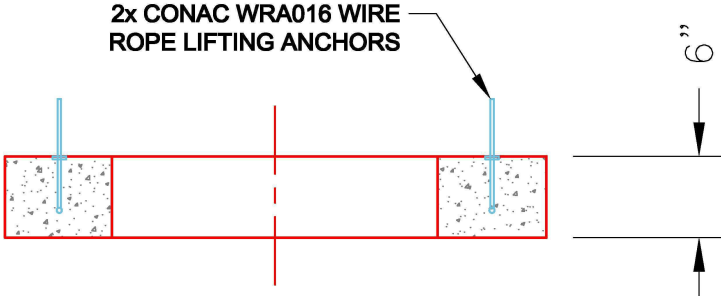


Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2		Plant: 100	Tech: J. Horsley	
Job Location: Danville, KY		6/7/2026 1:26:08 PM	PC: C. Goff	
Contractor: Hubert Excavating & Contracting				
Structure ID: MH A14				
P4	GR6	GRADE RING F/F		
P5) 24" - CASTING HEIGHT - 7"		0 lb	Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: (1) #3 HOOP CENTERED (GRADE 60) 4. CARBOLINE 300M EXTERIOR COATING REQUIRED 5. LIFTERS: 2 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING	
P4) 24" - GRADE RING F/F - 6"		405 lb		
P3) 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 42"		3116 lb		
P2) 60" - MH Trans. Slab - 48" Hole ECC, w/Coating T/G - 13"		1928 lb		
P1) 60" - MH BASE w/FLANGE (08F/07EF) w/Coating T/n - 72"		10426 lb		
1) JOINT WRAP - 12" WD x 060" MAC WRAP		0 lb		
1) 60" - MH INVERT CHANNEL - FULL HEIGHT		2692 lb		
1) SPECIAL EXTERNAL COATING - Carboline 300M		0 lb		
1) JOINT WRAP - 12" WD x 048" MAC WRAP		0 lb		
1) SECONDARY POUR - Extended Flange		0 lb		
1) 60" - Conseal CS-102 1.00" (Double)		0 lb		
1) 48" - Conseal CS-102 1.00" (Double)		0 lb		
2) 24" - Conseal CS-102 1.00" (Double)		0 lb		
2) A-Lok - 1040		2 lb		
1) PSX - 12-08 NYLO		8 lb		
10) MH Step ML-10-TDS-NCR - 10"		0 lb		
220.64 SqFt) Carboline Bitumastic 300M [EXT]		0 lb		
Structure Total:		18577 lb		
 PLAN VIEW				
 ISOMETRIC VIEW				
 SECTION A-A				
Coating (Int): Coating (Ext): Carboline Bitumastic 300M		Seam Up: Flat Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 6"
				Weight (Net): 405 lb Volume (Net): 0.1cu.yd

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer
Ph 2

Structure:

MH A14

Note:

This Structure Is To Receive An
External Coating of Carboline 300M
(Supplied By iCast)
