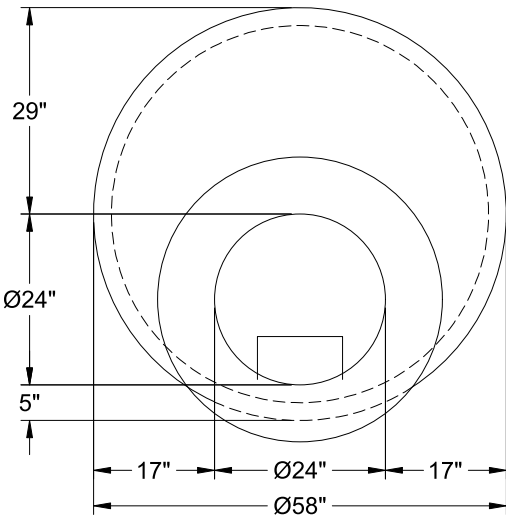



Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2		Plant: 100	Tech: J. Horsley	
Job Location: Danville, KY		6/7/2026 1:26:09 PM	PC: C. Goff	
Contractor: Hubert Excavating & Contracting				
Structure ID: MH A15				
P4	MH048CN36SP	ECC CONE w/ 24" HOLE, w/Coating F/G		
P5) 24" - CASTING HEIGHT - 7"		0 lb	Structure Notes:	
P4) 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 36"		2251 lb	1. PER ASTM C-478 SPECIFICATIONS	
P3) 48" - MH RISER w/COATING T/G - 24"		1677 lb	2. CONCRETE: 4,000 PSI AT 28 DAYS	
P2) 60" - MH Trans. Slab - 48" Hole ECC, w/Coating T/G - 13"		1928 lb	3. REINFORCEMENT: PER ASTM A615	
P1) 60" - MH BASE w/FLANGE (08F/07EF) w/Coating T/n - 68"		10066 lb	4. CARBOLINE 300M EXTERIOR COATING REQUIRED	
1) 60" - MH INVERT CHANNEL - FULL HEIGHT		2692 lb	5. STEPS REQUIRED	
1) JOINT WRAP - 12" WD x 060" MAC WRAP		0 lb	6. HOE MC-375 FRAME & COVER "SANITARY"	
1) SPECIAL EXTERNAL COATING - Carboline 300M		0 lb	SUPPLIED BY OTHERS	
1) SECONDARY POUR - Extended Flange		0 lb		
2) JOINT WRAP - 12" WD x 048" MAC WRAP		0 lb		
1) 60" - Conseal CS-102 1.00" (Double)		0 lb		
2) 48" - Conseal CS-102 1.00" (Double)		0 lb		
1) 24" - Conseal CS-102 1.00" (Double)		0 lb		
2) A-Lok - 1040		2 lb		
10) MH Step ML-10-TDS-NCR - 10"		0 lb		
238.97 SqFt) Carboline Bitumastic 300M [EXT]		0 lb		
Structure Total:		18615 lb		
				
				
48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 36" - (P4)				
Coating (Int): Coating (Ext): Carboline Bitumastic 300M		Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"
				Weight (Net): 2251 lb Volume (Net): 0.57cu.yd

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer
Ph 2

Structure:

MH A15

Note:

This Structure Is To Receive An
External Coating of Carboline 300M
(Supplied By iCast)
