



P5)	24" - CASTING HEIGHT - 7"	0 lb	Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE WT-375 SAN. F/C) 4. ALL PIECES TO HAVE EXTERIOR COATING (CARBOLINE BITUMASTIC 300M). 5. INTERIOR DROP TO BE SUPPLIED BY OTHERS. REINFORCING PER ASTM A615 (GRADE 60). - TRANS. SLAB = HS20 LOADING (PER ATTACHED STAMPED DESIGNS). - RISER/WALLS (As .18) - FLOOR (As .47) #5 BARS AT 8" C.C.E.W.
P4)	48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 24"	1738 lb	
P3)	48" - MH RISER SPECIAL T/G - 36"	2515 lb	
P2)	60" - MH Transition Slab 48" Hole T/G - 13"	1928 lb	
P1)	60" - MH BASE w/FLANGE CUSTOM HT T/n - 72"	10629 lb	
1)	JOINT WRAP - 12" WD x 060" MAC WRAP	0 lb	
1)	60" - MH INVERT CHANNEL - FULL HEIGHT	2692 lb	
1)	SPECIAL EXTERNAL COATING	0 lb	
1)	60" - Conseal CS-102 1.00" (Double)	0 lb	
2)	48" - Conseal CS-102 1.00" (Double)	0 lb	
1)	24" - Conseal CS-102 1.00" (Double)	0 lb	
2)	A-Lok - 1040	2 lb	
1)	A-Lok - 0285	1 lb	
11)	MH Step ML-10-TDS-NCR - 10"	0 lb	
249.63 SqFt) Carboline Bitumastic 300M [EXT]		0 lb	
Structure Total:		19505 lb	

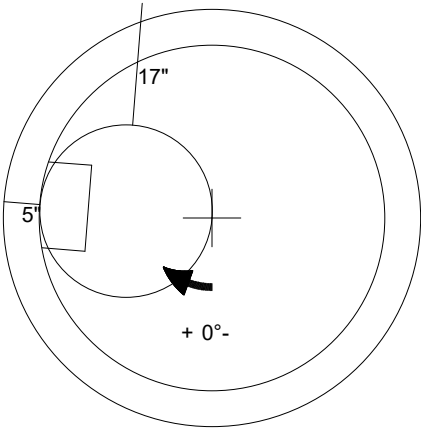

Coating (Int):	Seam Up: Flat	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 1738 lb
Coating (Ext): Carboline Bitumastic 300M	Seam Dn: Groove			Volume (Net): 0.44cu.yd

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer Ph 2

Structure:

MH A16

Note:

This structure is to receive an external coating of carbolite 300M (supplied by ICAST)
