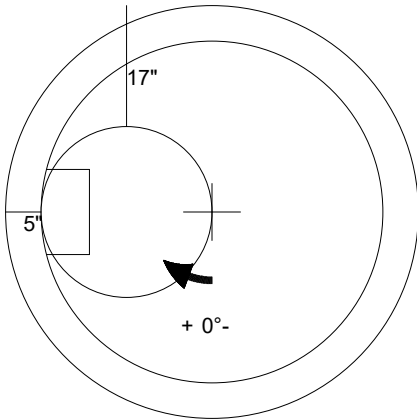



Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2		Plant: 100	Tech: J. Horsley			
Job Location: Danville, KY		8/21/2026 1:04:03 PM	PC: C. Goff			
Contractor: Hubert Excavating & Contracting						
Structure ID: MH A27						
P3	MH048CN42SP	ECC CONE w/ 24" HOLE, w/Coating F/G				
P5) 24" - CASTING HEIGHT - 7"		0 lb	Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE WT-375 SAN. F/C) 4. ALL PIECES TO HAVE EXTERIOR COATING (CARBOLINE BITUMASTIC 300M). REINFORCING PER ASTM A615 (GRADE 60). - TRANS. SLAB = HS20 LOADING (PER ATTACHED STAMPED DESIGNS). - RISER/WALLS (As .18) - FLOOR (As .47) #5 BARS AT 8" C.C.E.W.			
P4) 24" - GRADE RING F/F - 6"		405 lb				
P3) 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 42"		3116 lb				
P2) 60" - MH Trans. Slab - 48" Hole ECC, w/Coating T/G - 13"		1928 lb				
P1) 60" - MH BASE w/FLANGE (08F/07EF) w/Coating T/n - 72"		10584 lb				
1) 60" - MH INVERT CHANNEL - FULL HEIGHT		2692 lb				
2) JOINT WRAP - 12" WD x 060" MAC WRAP		0 lb				
1) SPECIAL EXTERNAL COATING		0 lb				
1) 60" - Conseal CS-102 1.00" (Double)		0 lb				
1) 48" - Conseal CS-102 1.00" (Double)		0 lb				
2) 24" - Conseal CS-102 1.00" (Double)		0 lb				
2) A-Lok - 0890		2 lb				
1) Kor-N-Seal2 - S206-18L		6 lb				
10) MH Step ML-10-TDS-NCR - 10"		0 lb				
220.64 SqFt) Carboline Bitumastic 300M [EXT]		0 lb				
Structure Total:		18733 lb				
						
						
48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 42" - (P3)						
Coating (Int): Coating (Ext): Carboline Bitumastic 300M		Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 42"		
				Weight (Net): 3116 lb Volume (Net): 0.8cu.yd		

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer Ph 2

Structure:

MH A27

Note:

This structure is to receive an external coating of carboline 300M (supplied by ICAST)
