

Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2

Job Location: Danville, KY

Contractor: Hubert Excavating & Contracting

Plant: 100

8/21/2026 12:57:17 PM

Tech: J. Horsley

PC: C. Goff



Structure ID: MH A32

P1 MH048BAEVF

MH BASE w/FLANGE (08F/08EF) w/Coating T/n

P5) 24" - CASTING HEIGHT - 7"

P4) 24" - GRADE RING F/F - 4"

P3) 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 30"

P2) 48" - MH RISER w/COATING T/G - 60"

P1) 48" - MH BASE w/FLANGE (08F/08EF) w/Coating T/n - 42"

1) 48" - MH INVERT CHANNEL - FULL HEIGHT

2) JOINT WRAP - 12" WD x 048" MAC WRAP

1) SPECIAL EXTERNAL COATING

2) 48" - Con Seal CS-102 1.00" (Double)

2) Kor-N-Seal2 - S206-28

11) MH Step ML-10-TDS-NCR - 10"

174.41 SqFt) Carboline Bitumastic 300M [EXT]

0 lb

270 lb

1961 lb

4192 lb

5276 lb

1440 lb

0 lb

0 lb

0 lb

13 lb

0 lb

0 lb

13152 lb

Structure Notes: 1. PER ASTM C478 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. CASTING BY OTHERS (HOE WT-375 SAN. F/C).

4. ALL PIECES TO HAVE EXTERIOR COATING (CARBOLINE BITUMASTIC 300M).

REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 911.71' Rim to Invert: 11.832' Slack: 1.294" Sump: 2.309" Step Position: 96.5°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	899.878'	0°	0"	24" PVC F679 (PS46)	24.803"	Kor-N-Seal2 S206-28	28"	29.896"	0"	0"
Invert 2	899.925'	193°	97.686"	24" PVC F679 (PS46)	24.803"	Kor-N-Seal2 S206-28	28"	29.896"	0.564"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

Coating (Int):

Coating (Ext): Carboline Bitumastic 300M

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 5"

Floor Height: 8"

Height (Int): 42"


Height (Ext): 50"

Weight (Net): 5276 lb


Volume (Net): 1.35cu.yd

Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2				Plant: 100		Tech: J. Horsley				
Job Location: Danville, KY				8/21/2026 12:57:17 PM		PC: C. Goff				
Contractor: Hubert Excavating & Contracting										
Structure ID: MH A32										
P1		MH048BAEVF		MH BASE w/FLANGE (08F/08EF) w/Coating T/n						
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING F/F - 4" P3) 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 30" P2) 48" - MH RISER w/COATING T/G - 60" P1) 48" - MH BASE w/FLANGE (08F/08EF) w/Coating T/n - 42" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 2) JOINT WRAP - 12" WD x 048" MAC WRAP 1) SPECIAL EXTERNAL COATING 2) 48" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-28 11) MH Step ML-10-TDS-NCR - 10" 174.41 SqFt) Carboline Bitumastic 300M [EXT] <td colspan="2"> 0 lb 270 lb 1961 lb 4192 lb 5276 lb 1440 lb 0 lb 0 lb 0 lb 13 lb 0 lb 0 lb </td> <td colspan="4"> Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE WT-375 SAN. F/C). 4. ALL PIECES TO HAVE EXTERIOR COATING (CARBOLINE BITUMASTIC 300M). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. </td>				0 lb 270 lb 1961 lb 4192 lb 5276 lb 1440 lb 0 lb 0 lb 0 lb 13 lb 0 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE WT-375 SAN. F/C). 4. ALL PIECES TO HAVE EXTERIOR COATING (CARBOLINE BITUMASTIC 300M). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Structure Total:				13152 lb		Invert channel drawing Full height invert				
Rim: 911.71' Rim to Invert: 11.832' Slack: 1.294" Sump: 2.309" Step Position: 96.5°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	899.878'	0°	0"	24" PVC F679 (PS46)	24.803"	Kor-N-Seal2 S206-28	28"	29.896"	0"	0"
Invert 2	899.925'	193°	97.686"	24" PVC F679 (PS46)	24.803"	Kor-N-Seal2 S206-28	28"	29.896"	0.564"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

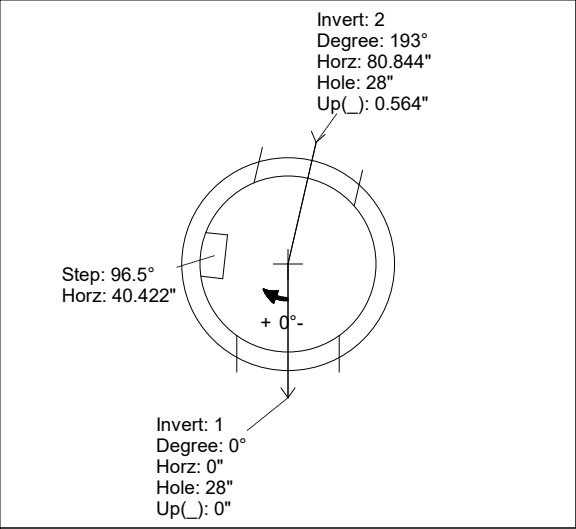

UPSIDE-DOWN VIEW (int. dimensions)

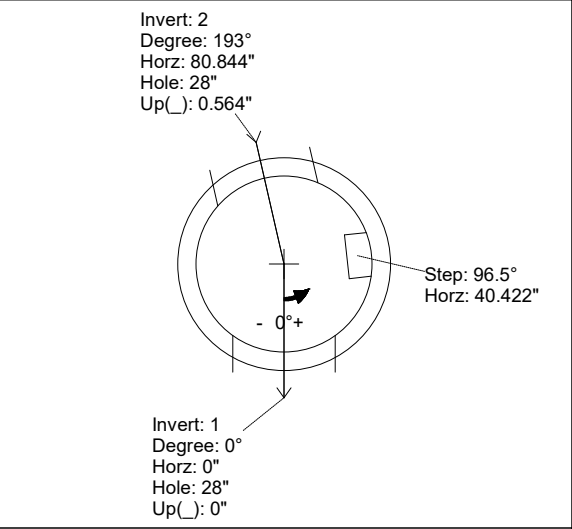

INSIDE WALL DIMENSIONS

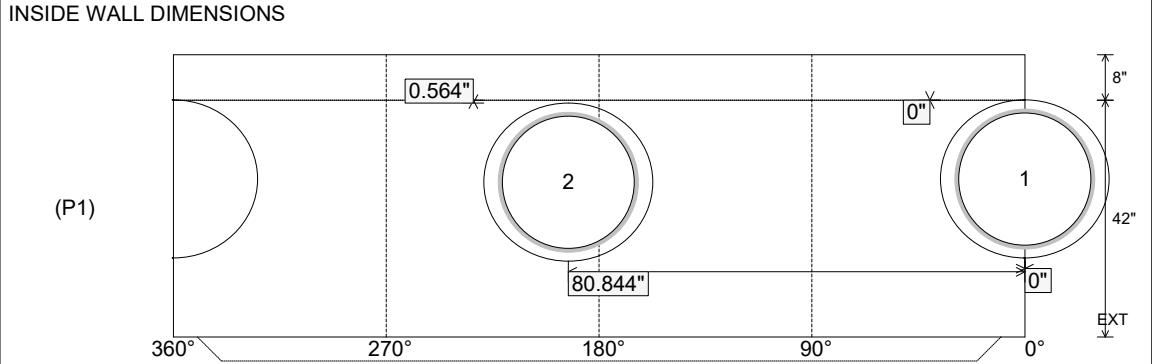

Coating (Int):

Coating (Ext): Carboline Bitumastic 300M

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 5"

Floor Height: 8"

Height (Int): 42"

Height (Ext): 50"

Weight (Net): 5276 lb

Volume (Net): 1.35cu.yd

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer Ph 2

Structure:

MH A32

Note:

This structure is to receive an external coating of carboline 300M (supplied by ICAST)
