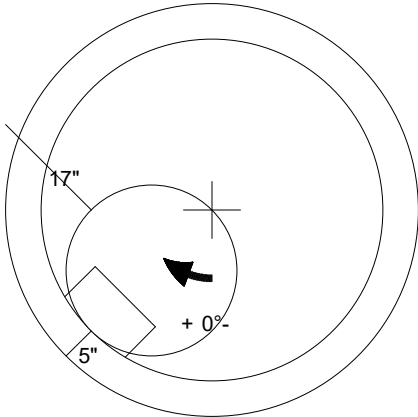



Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2		Plant: 100		Tech: J. Horsley		
Job Location: Danville, KY		8/21/2026 1:04:15 PM		PC: C. Goff		
Contractor: Hubert Excavating & Contracting						
Structure ID: MH A34						
P3 MH048CN42SP		ECC CONE w/ 24" HOLE, w/Coating F/G				
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 42" P2) 48" - MH RISER w/COATING T/G - 60" P1) 48" - MH BASE w/FLANGE (08F/08EF) w/Coating T/n - 66" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 2) JOINT WRAP - 12" WD x 048" MAC WRAP 1) SPECIAL EXTERNAL COATING 2) 48" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-28 3) Kor-N-Seal2 - S206-18L 14) MH Step ML-10-TDS-NCR - 10" 216.19 SqFt) Carboline Bitumastic 300M [EXT]		0 lb 3116 lb 4192 lb 6625 lb 1440 lb 0 lb 0 lb 0 lb 13 lb 18 lb 0 lb 0 lb ----- 15404 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE WT-375 SAN. F/C). 4. ALL PIECES TO HAVE EXTERIOR COATING (CARBOLINE BITUMASTIC 300M). 5. EXTERIOR DROP ASSEMBLY BY OTHERS. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
						
 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 42" - (P3)						
Coating (Int): Coating (Ext): Carboline Bitumastic 300M		Seam Up: Flat Seam Dn: Groove		Wall Thickness: 5"		Height (Ext): 42"
						Weight (Net): 3116 lb Volume (Net): 0.8cu.yd

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer Ph 2

Structure:

MH A34

Note:

This structure is to receive an external coating of carbolite 300M (supplied by ICAST)
