

Contractor: Hubert Excavating & Contracting

PC:	C. Goff
TECH:	J. Horsley
Plant:	100



Structure ID: MH A36

Spec: Sanitary
Type: SAN.MH w/Coating
Size: 48"


Rim: 913.8'	Sump: 2.309"
Invert: 903.075'	Floor (Top): 902.883'
Rim to Invert: 10.725'	Floor Height: 8"

Floor (Bot): 902.216'
Overall Height: 11.583'
Slack: 0.009"


Structure Notes: 1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY OTHERS (HOE WT-375 SAN. F/C).
4. ALL PIECES TO HAVE EXTERIOR COATING (CARBOLINE BITUMASTIC 300M).
REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:


P4)	24" - CASTING HEIGHT - 7"	0 lb
P3)	48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 24"	1738 lb
P2)	48" - MH RISER Custom Ht, w/Coating T/G - 58"	4031 lb
P1)	48" - MH BASE w/FLANGE (08F/08EF) w/Coating T/n - 42"	5276 lb
1)	48" - MH INVERT CHANNEL - FULL HEIGHT	1440 lb
2)	JOINT WRAP - 12" WD x 048" MAC WRAP	0 lb
1)	SPECIAL EXTERNAL COATING	0 lb
2)	48" - Conseal CS-102 1.00" (Double)	0 lb
2)	Kor-N-Seal2 - S206-28	13 lb
1)	PSX - 8QRS-S NYLO	6 lb
10)	MH Step ML-10-TDS-NCR - 10"	0 lb
166.38	SqFt) Carboline Bitumastic 300M [EXT]	0 lb
Structure Total:		12504 lb

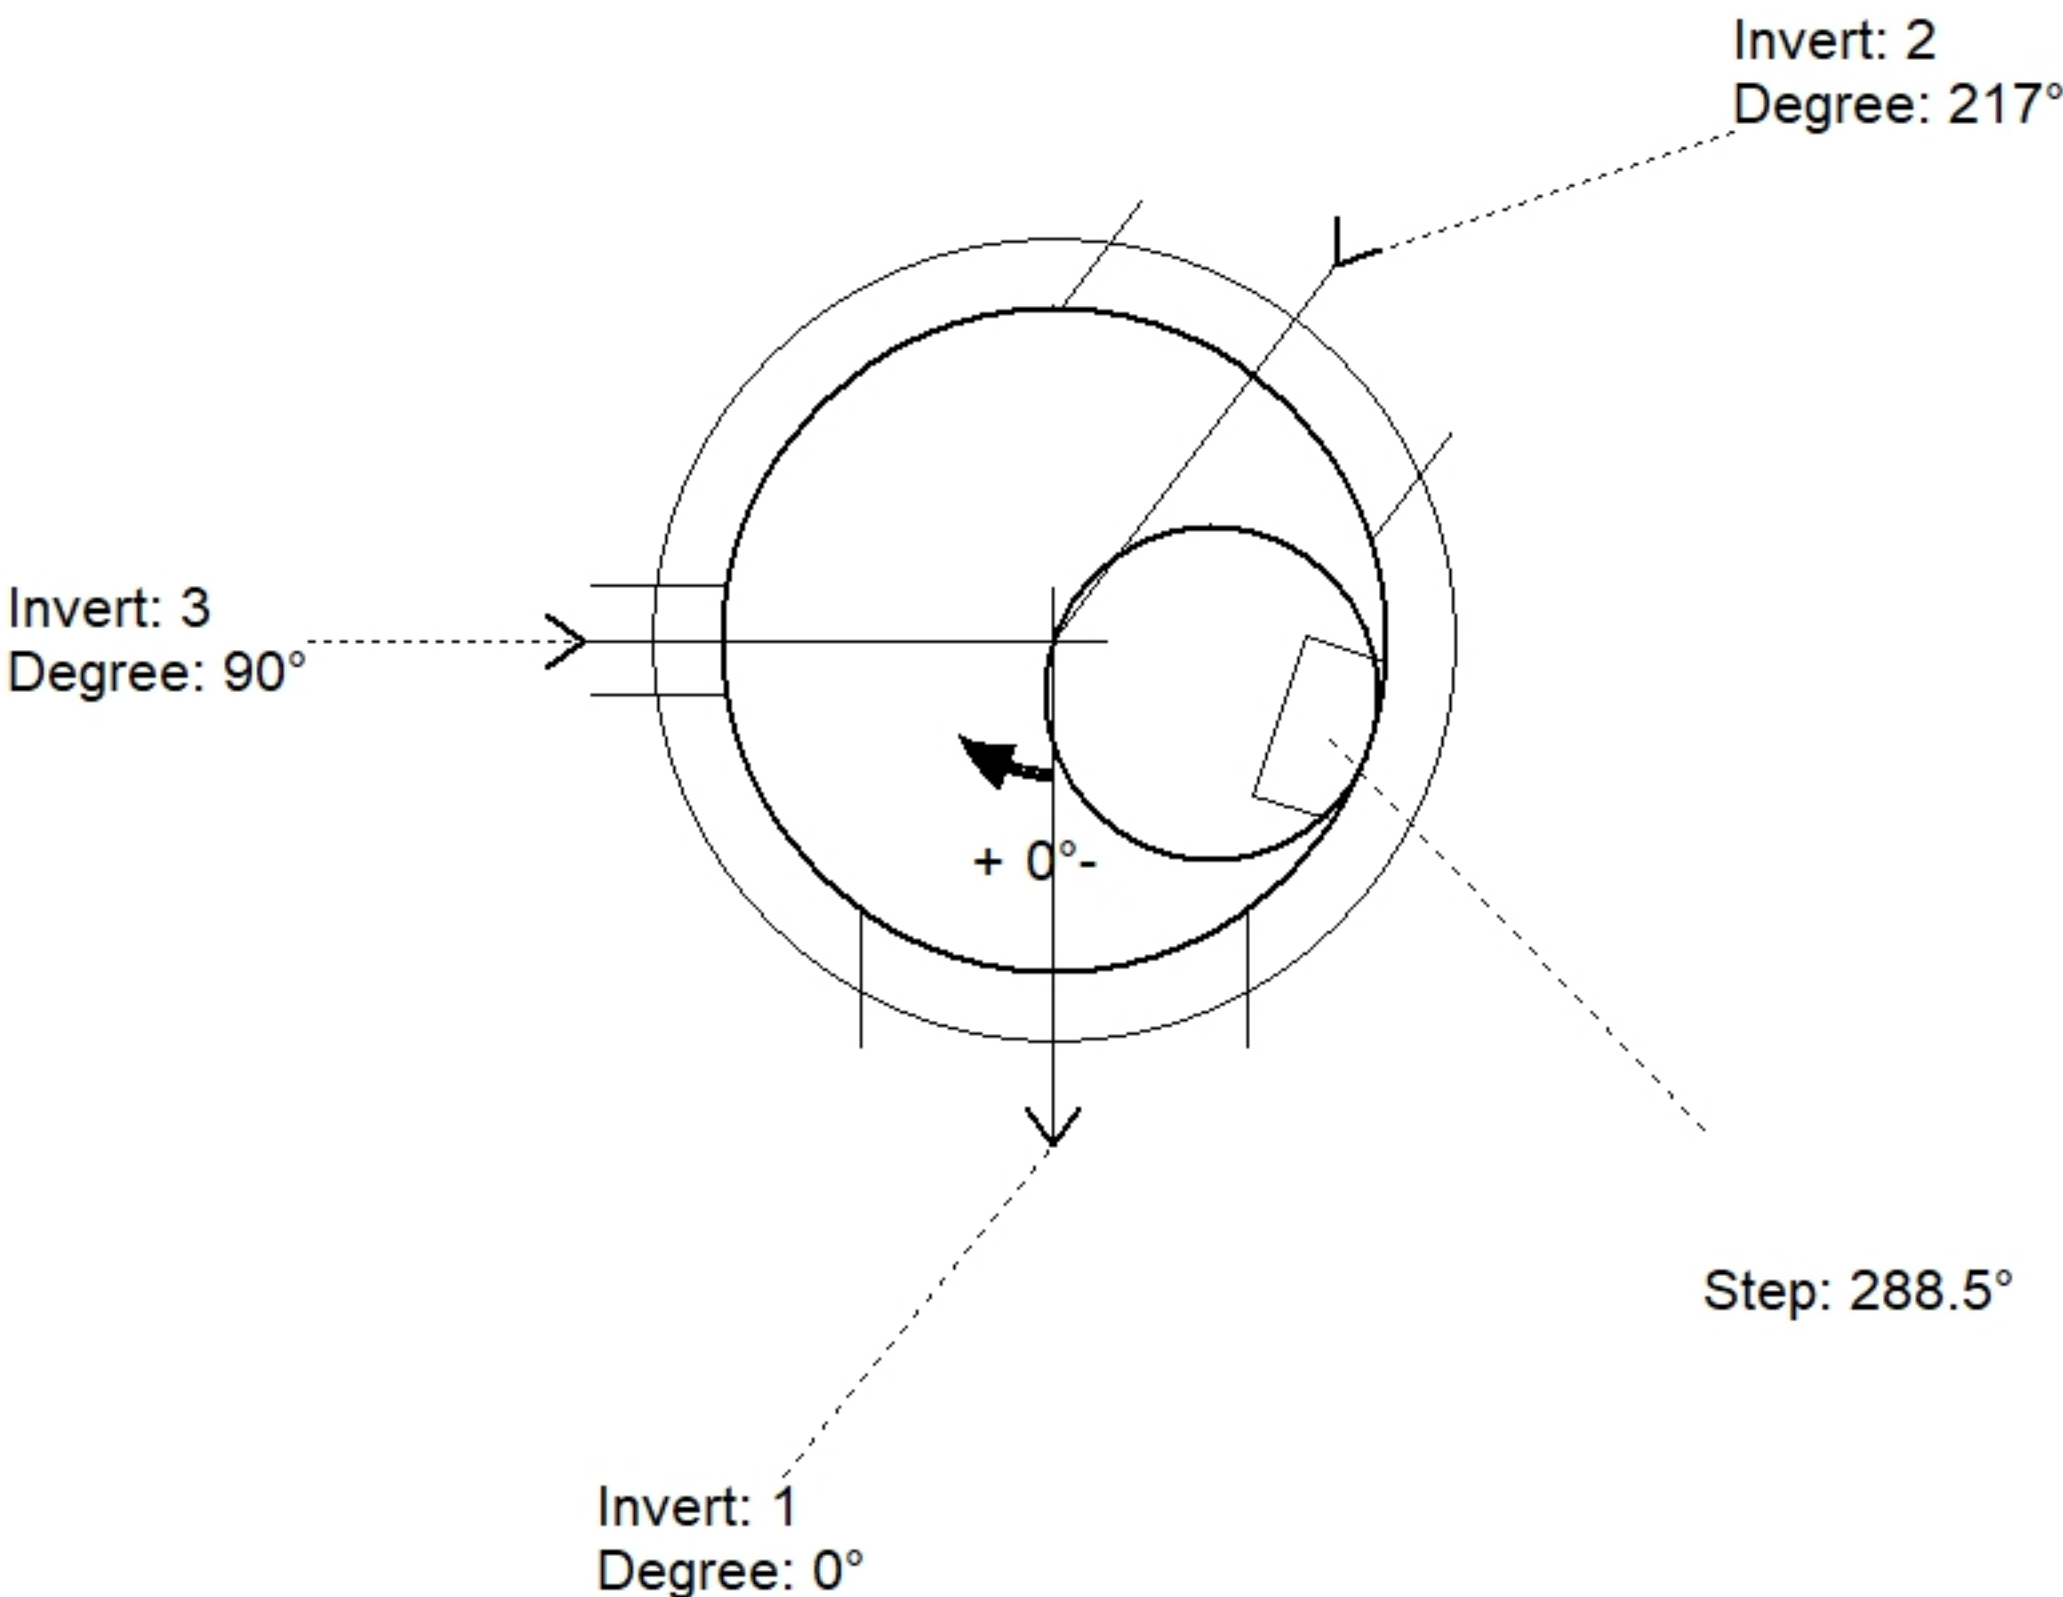

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (␣)	Ref
Rim	913.8'							
Reducer								
Invert 1	903.075'	0°	24" PVC F679 (PS46)	24.803"	28"	Kor-N-Seal2 S206-28	0"	P1
Invert 2	903.125'	217°	24" PVC F679 (PS46)	24.803"	28"	Kor-N-Seal2 S206-28	0.6"	P1
Invert 3	910.3'	90°	4" DI (vent pipe)	4.75"	8"	PSX 8QRS-S NYLO	40.759"	P2
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

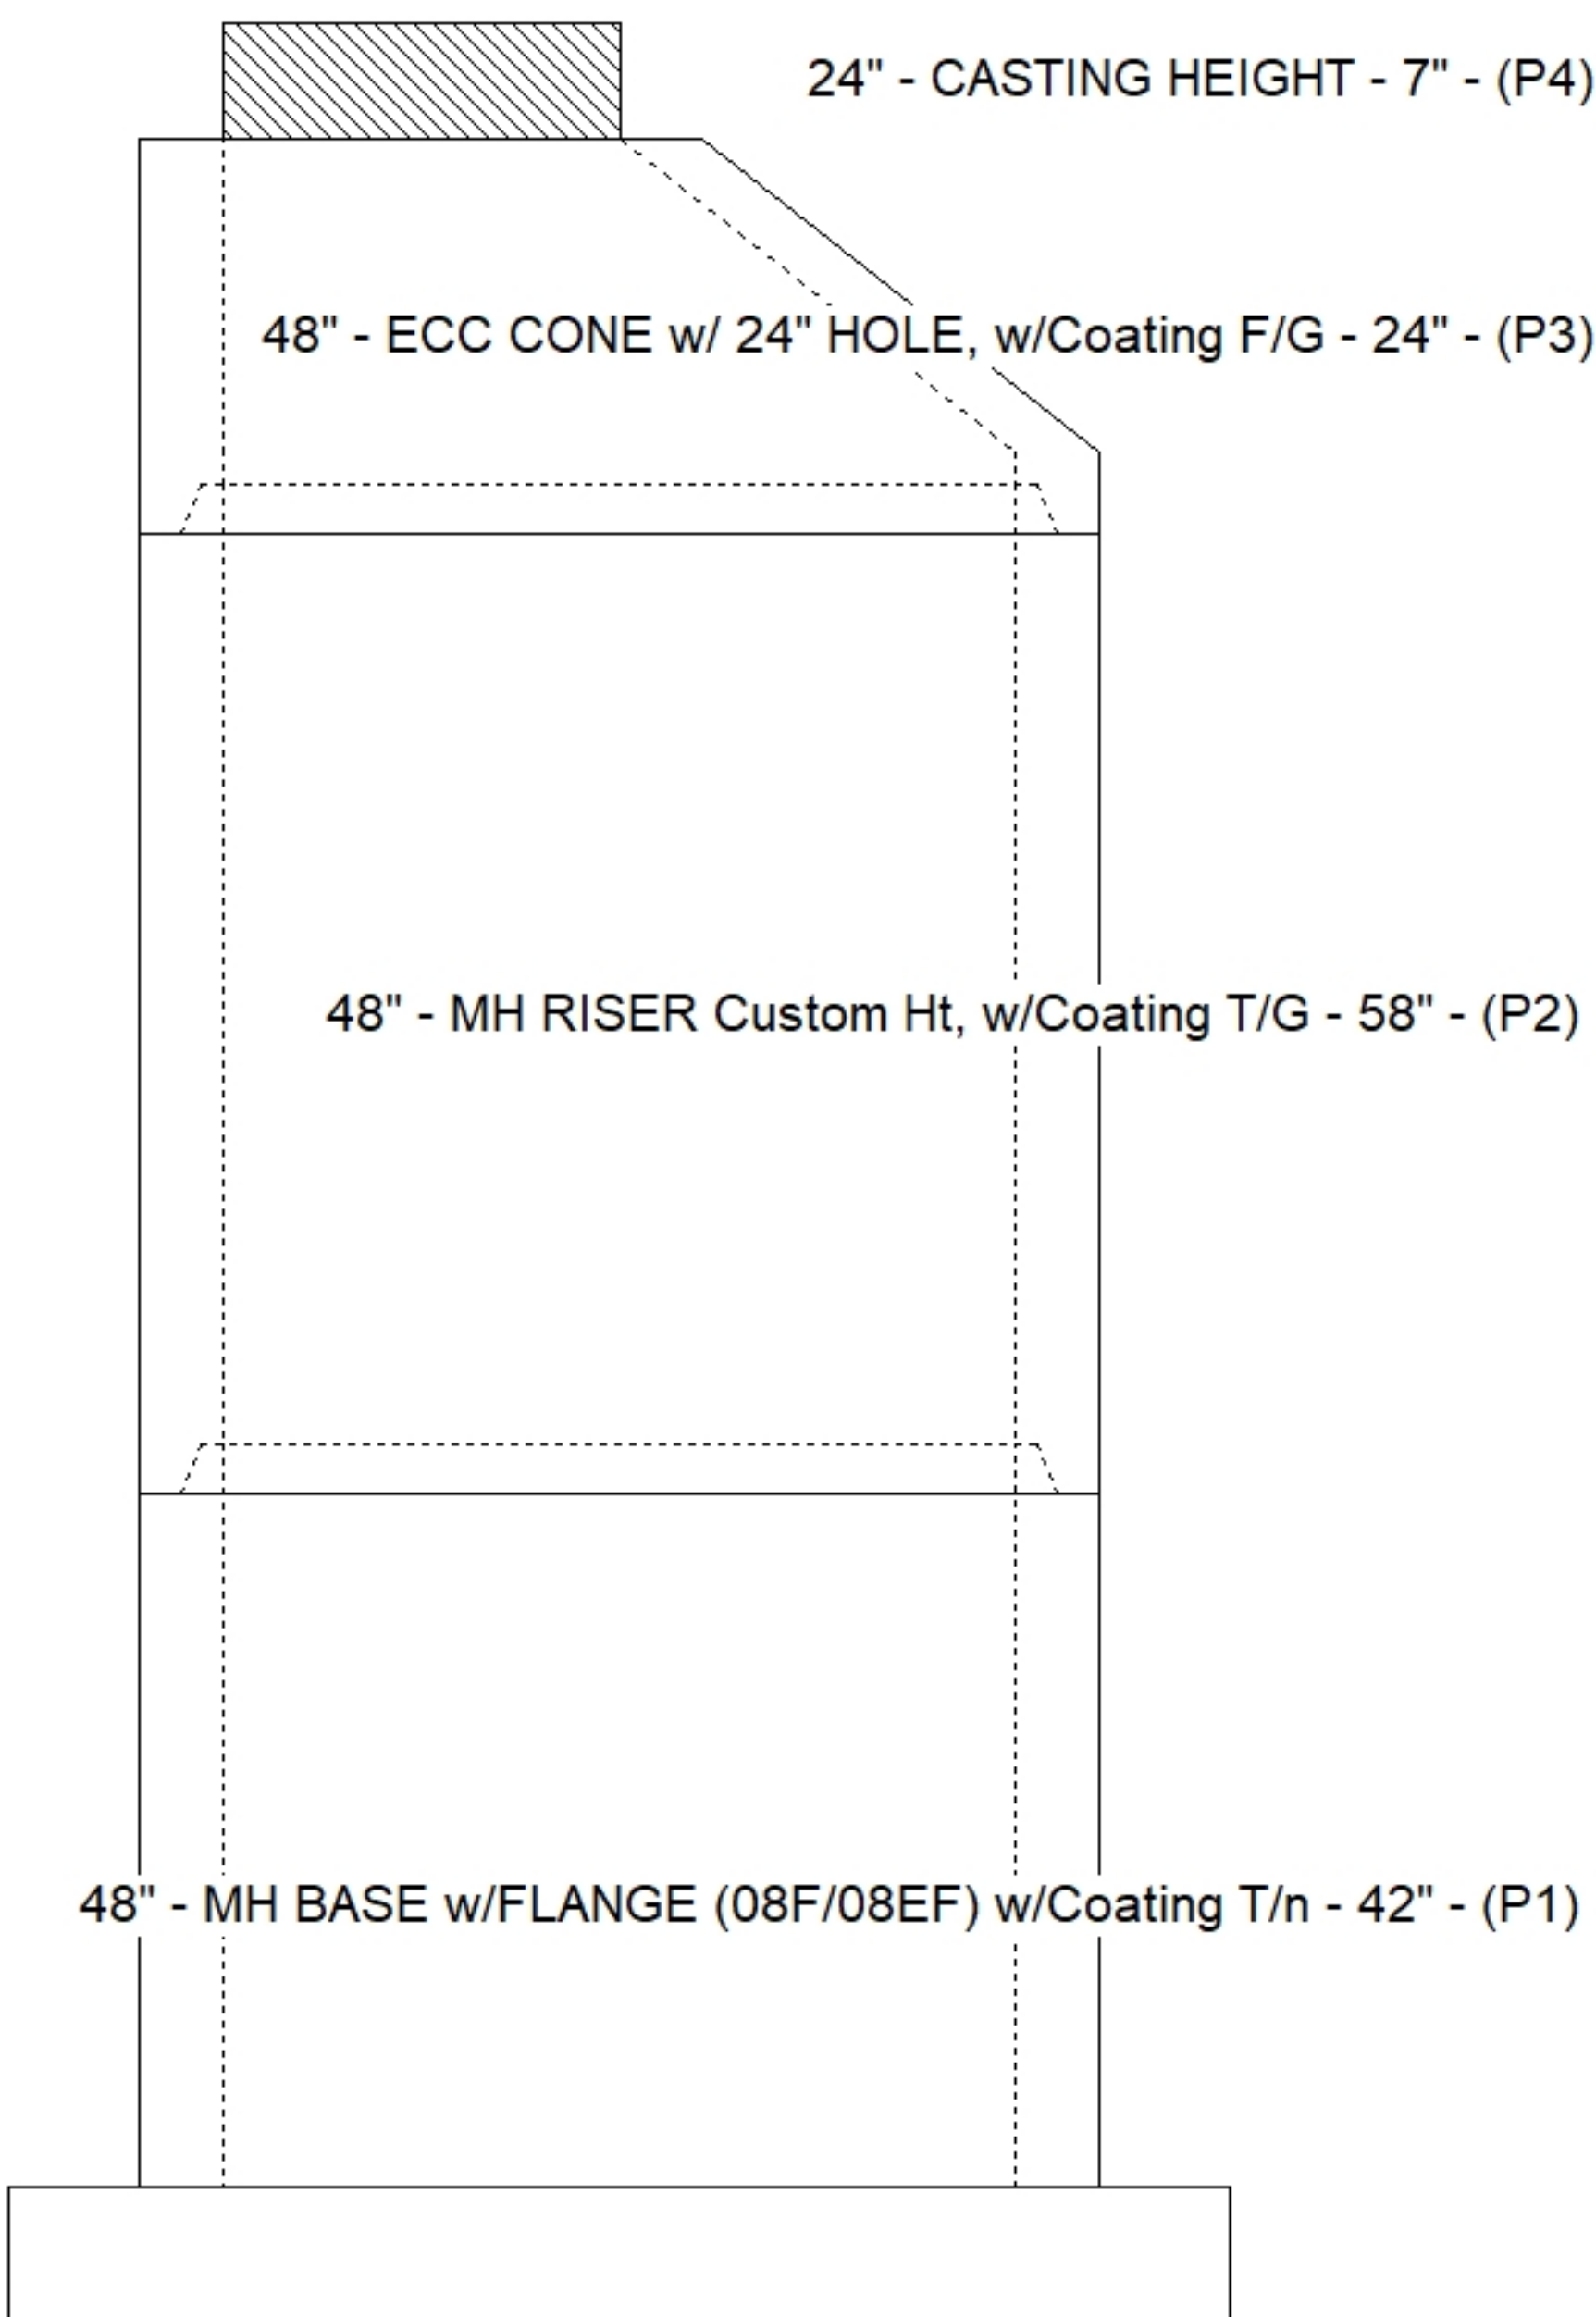

Default - Interior Dimensions

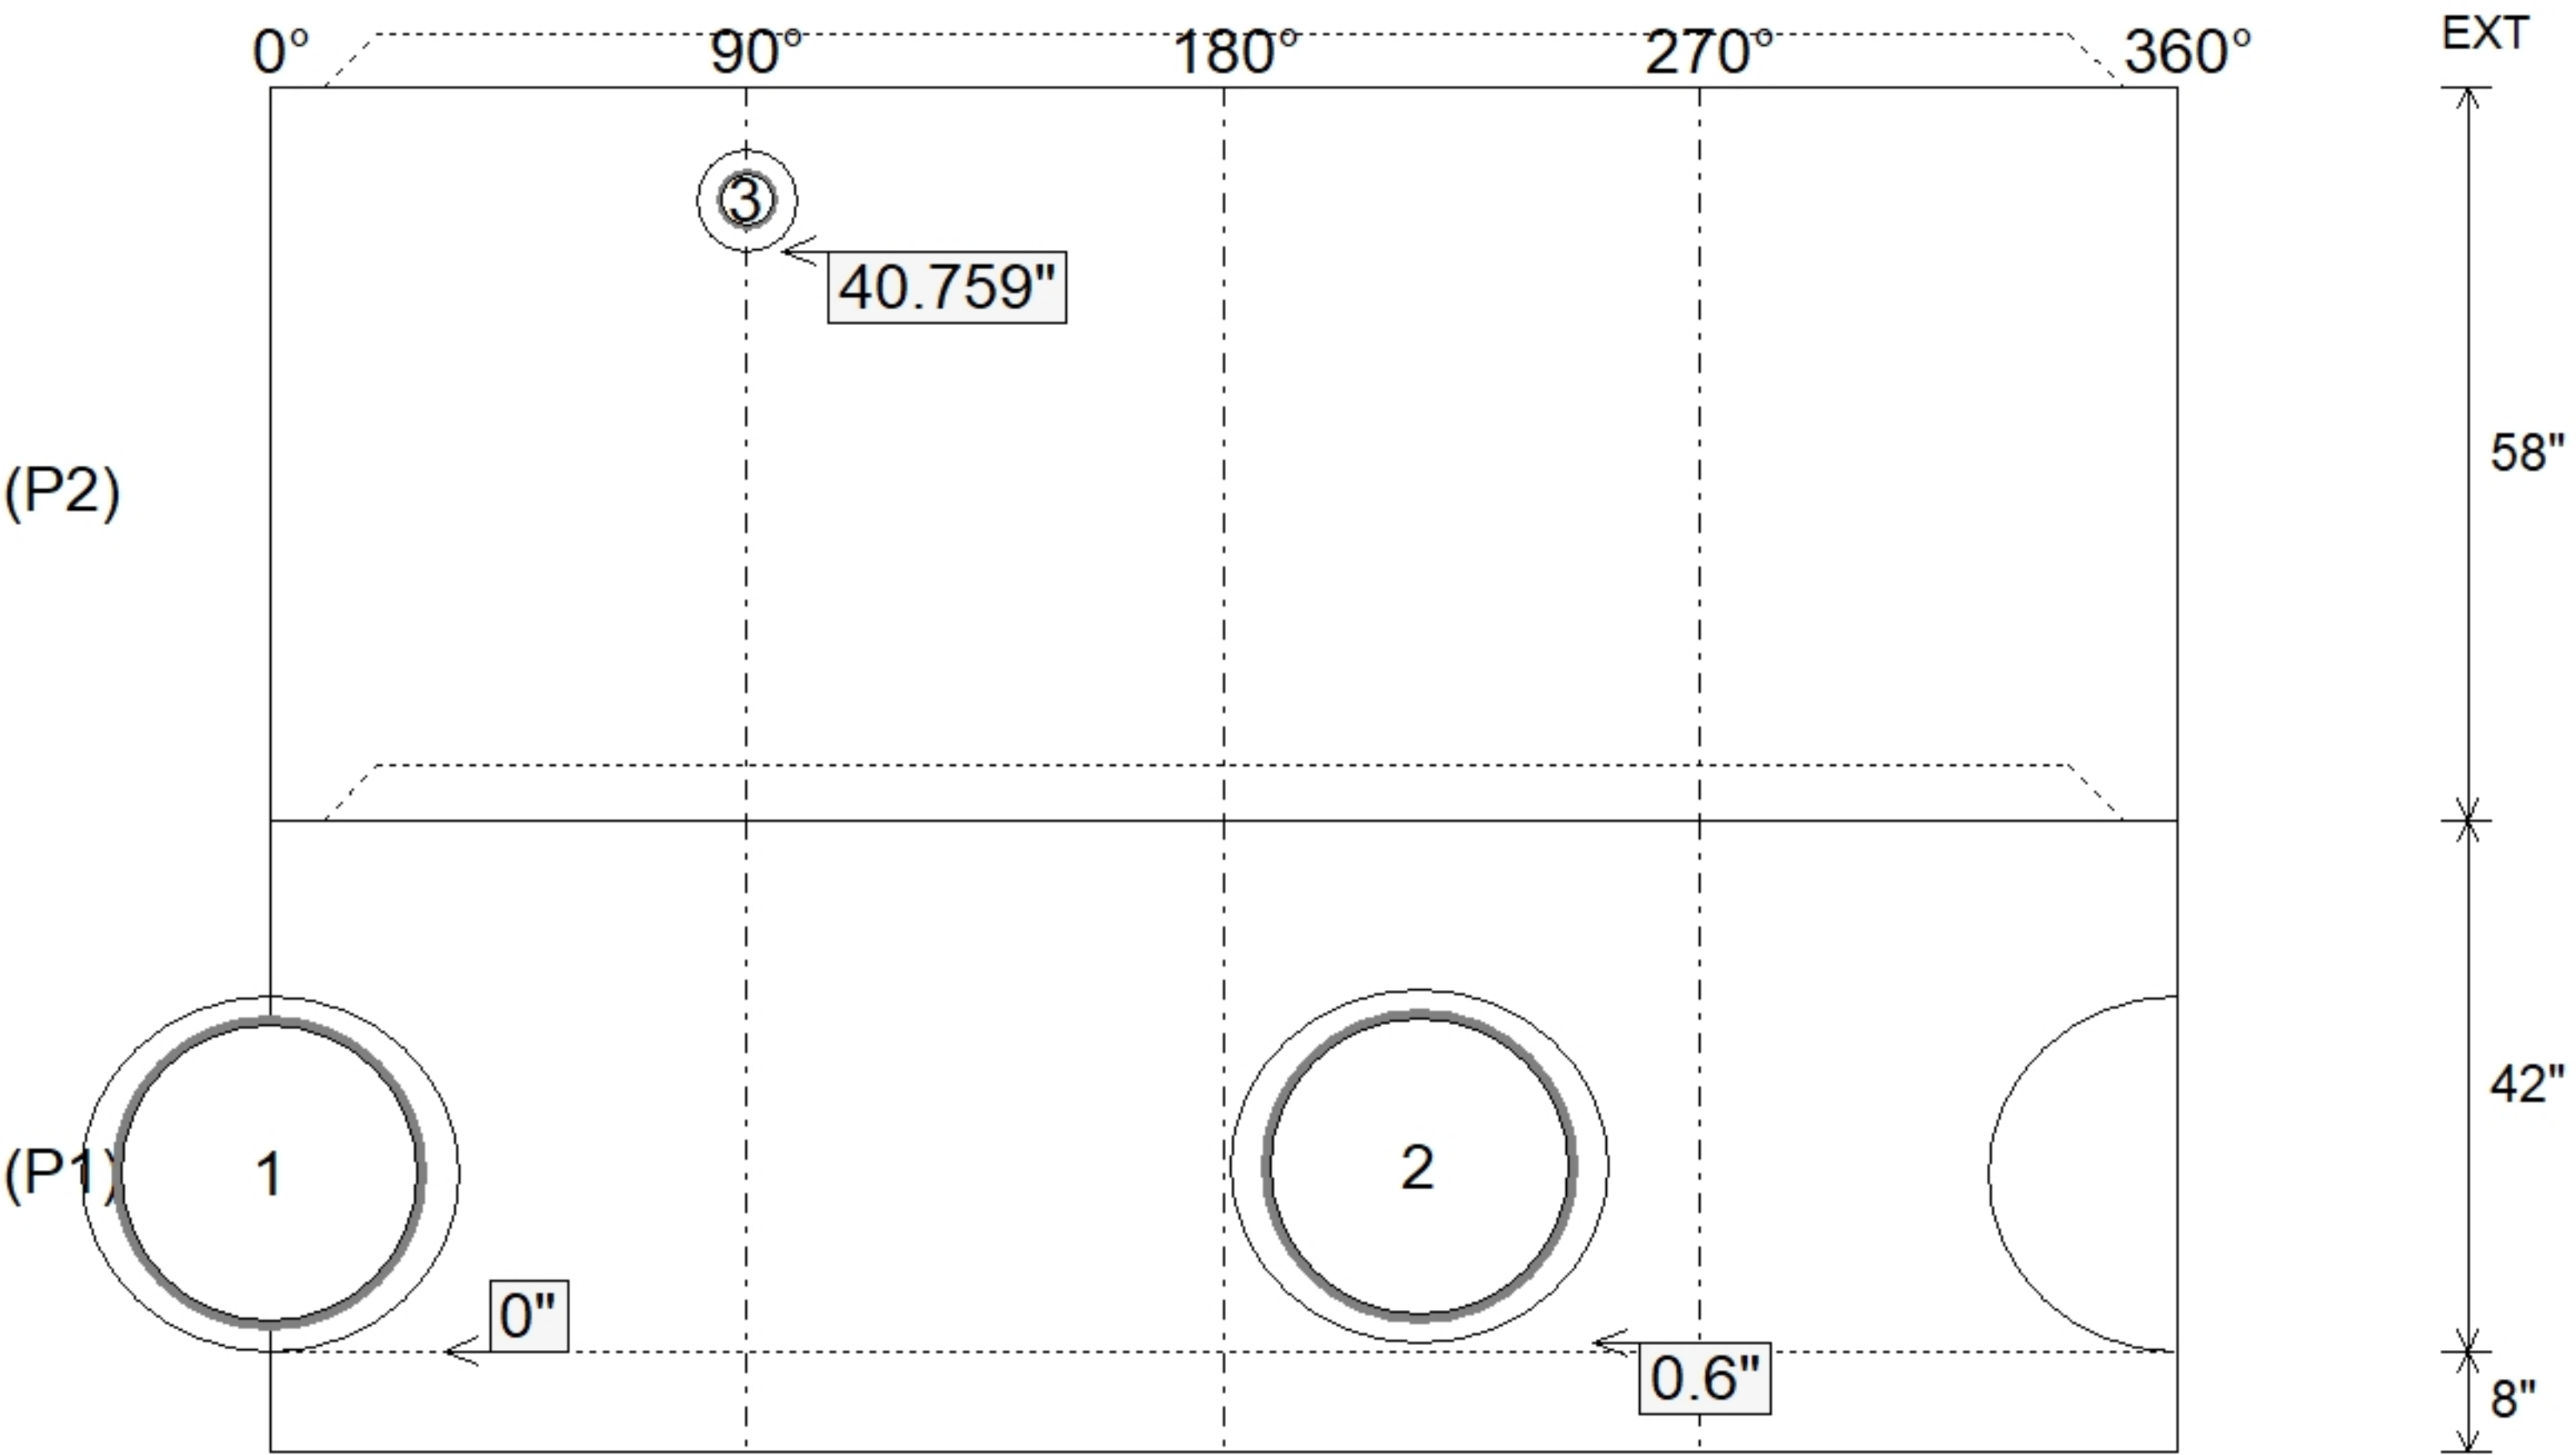

Submittal Drawing
8/27/2026 3:32:24 PM

SUBMITTAL
APPROVED BY:
