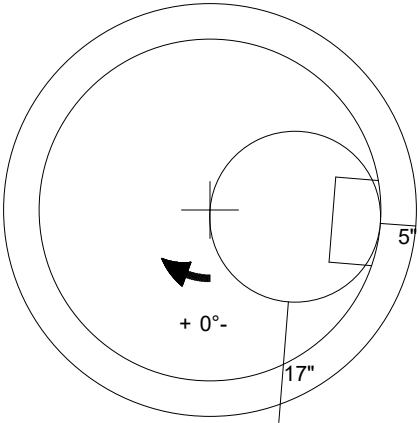



Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2		Plant: 100	Tech: J. Horsley	
Job Location: Danville, KY		8/21/2026 1:04:29 PM	PC: C. Goff	
Contractor: Hubert Excavating & Contracting				
Structure ID: MH A41				
P3 MH048CN24SP		ECC CONE w/ 24" HOLE, w/Coating F/G		
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 24" P2) 48" - MH RISER w/COATING T/G - 72" P1) 48" - MH BASE w/FLANGE (08F/08EF) w/Coating T/n - 39" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 2) JOINT WRAP - 12" WD x 048" MAC WRAP 1) SPECIAL EXTERNAL COATING 2) 48" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-28 1) PSX - 8QRS-S NYLO 11) MH Step ML-10-TDS-NCR - 10" 180.3 SqFt) Carboline Bitumastic 300M [EXT]		0 lb 1738 lb 5009 lb 5066 lb 1440 lb 0 lb 0 lb 0 lb 13 lb 6 lb 0 lb 0 lb ----- 13273 lb	Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE WT-375 SAN. F/C). 4. ALL PIECES TO HAVE EXTERIOR COATING (CARBOLINE BITUMASTIC 300M). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 24" - (P3)				
Coating (Int): Coating (Ext): Carboline Bitumastic 300M	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 1738 lb Volume (Net): 0.44cu.yd

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer Ph 2

Structure:

MH A41

Note:

This structure is to receive an external coating of carboline 300M (supplied by ICAST)
