


Contractor: Hubert Excavating & Contracting

Plant: 100





Slack: 1.01"

Structure Total: 13273 lb

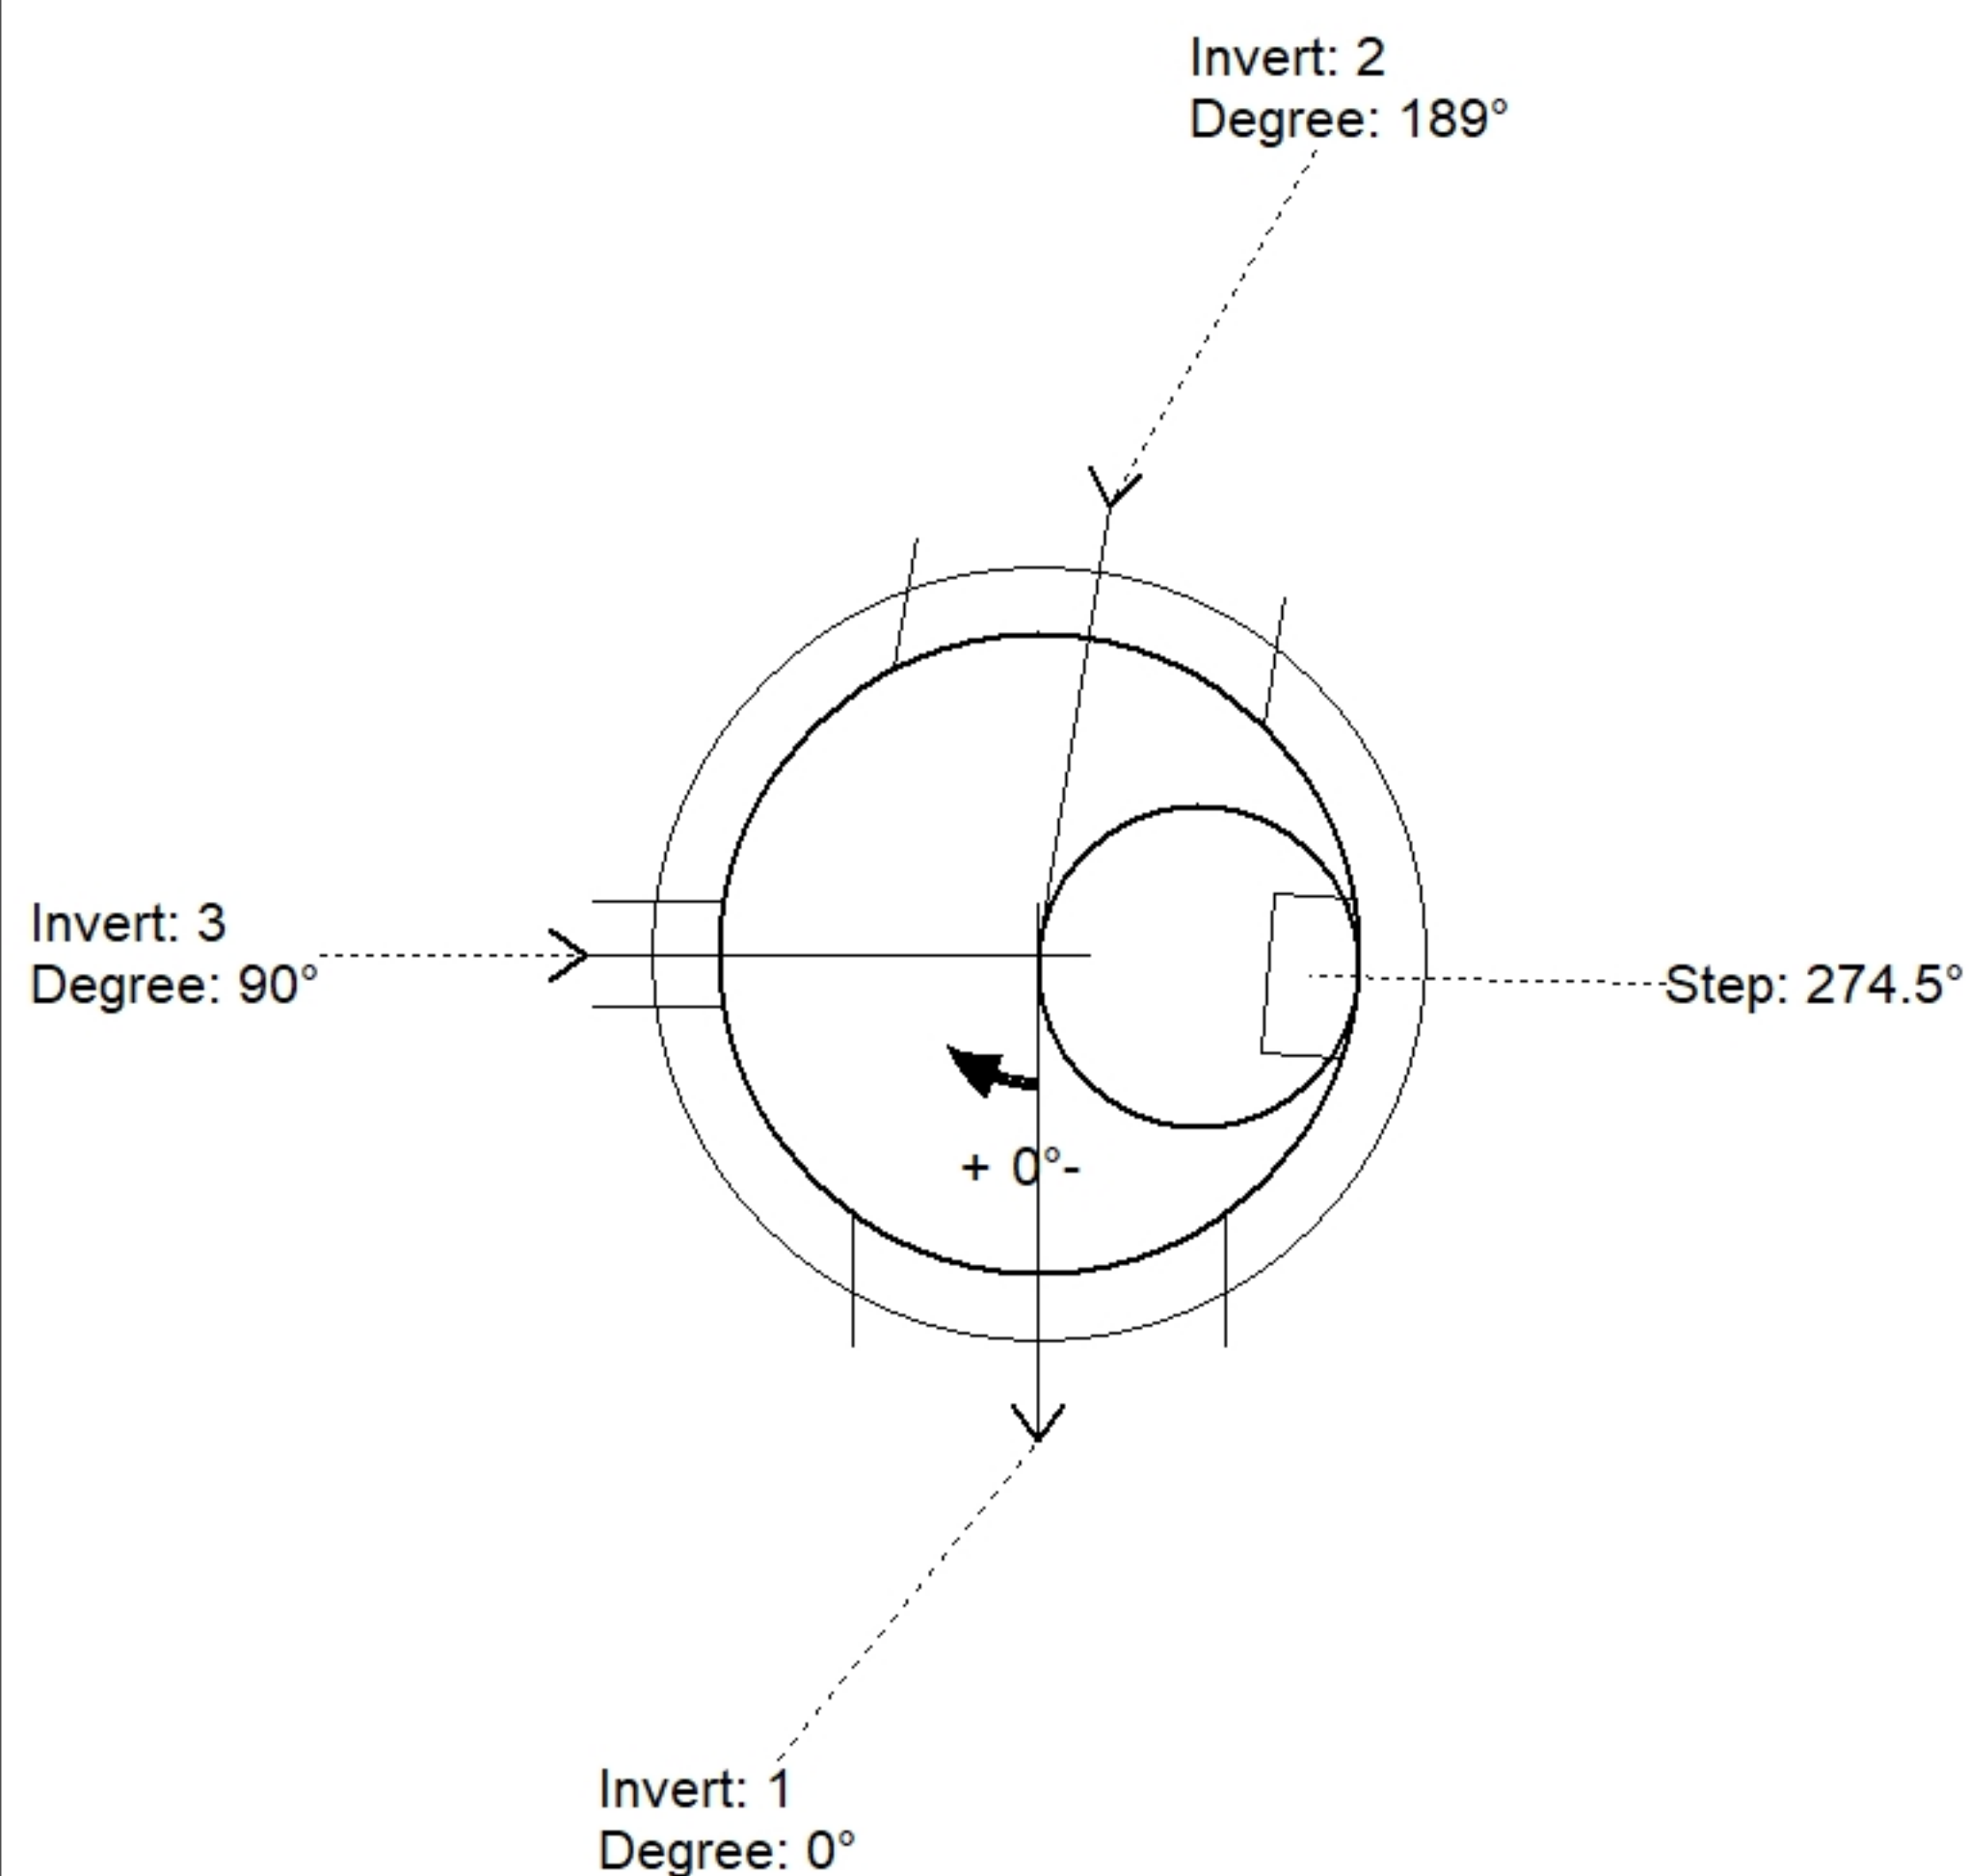

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	917.41'							
Reducer								
Invert 1	905.685'	0°	24" PVC F679 (PS46)	24.803"	28"	Kor-N-Seal2 S206-28	0"	P1
Invert 2	905.735'	189°	24" PVC F679 (PS46)	24.803"	28"	Kor-N-Seal2 S206-28	0.6"	P1
Invert 3	913.81'	90°	4" DI (vent pipe)	4.75"	8"	PSX 8QRS-S NYLO	54.559"	P2
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

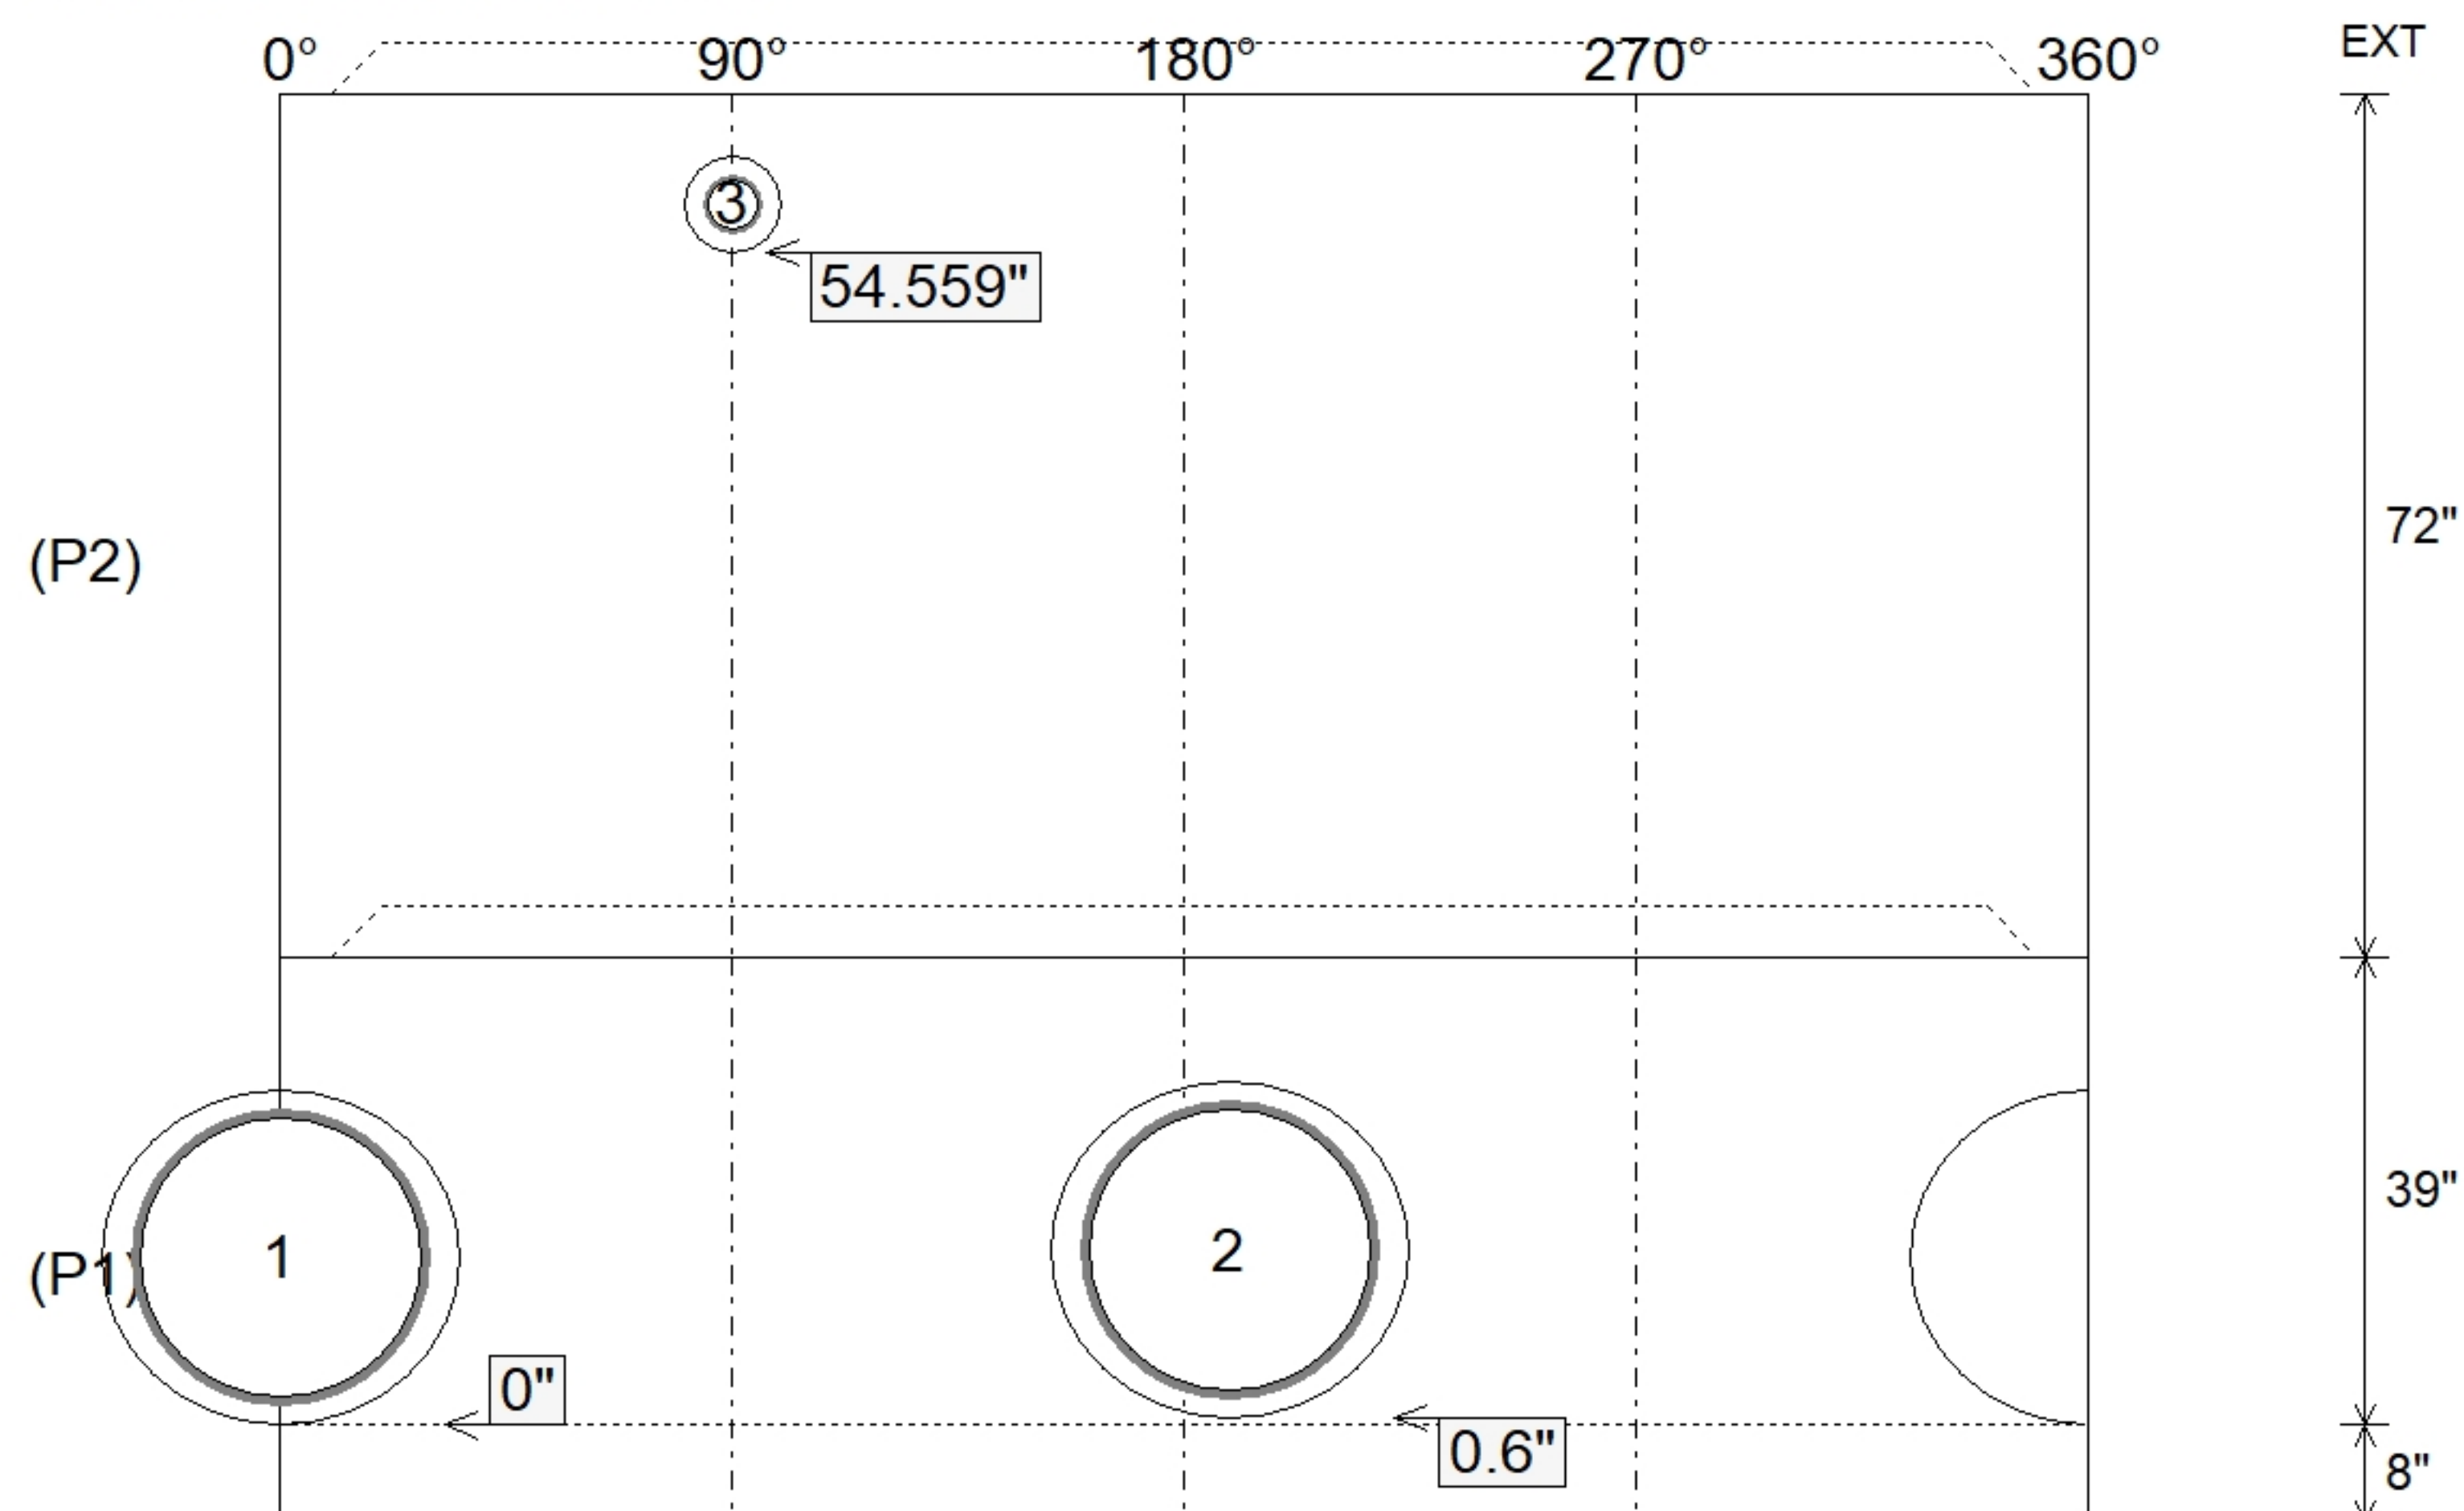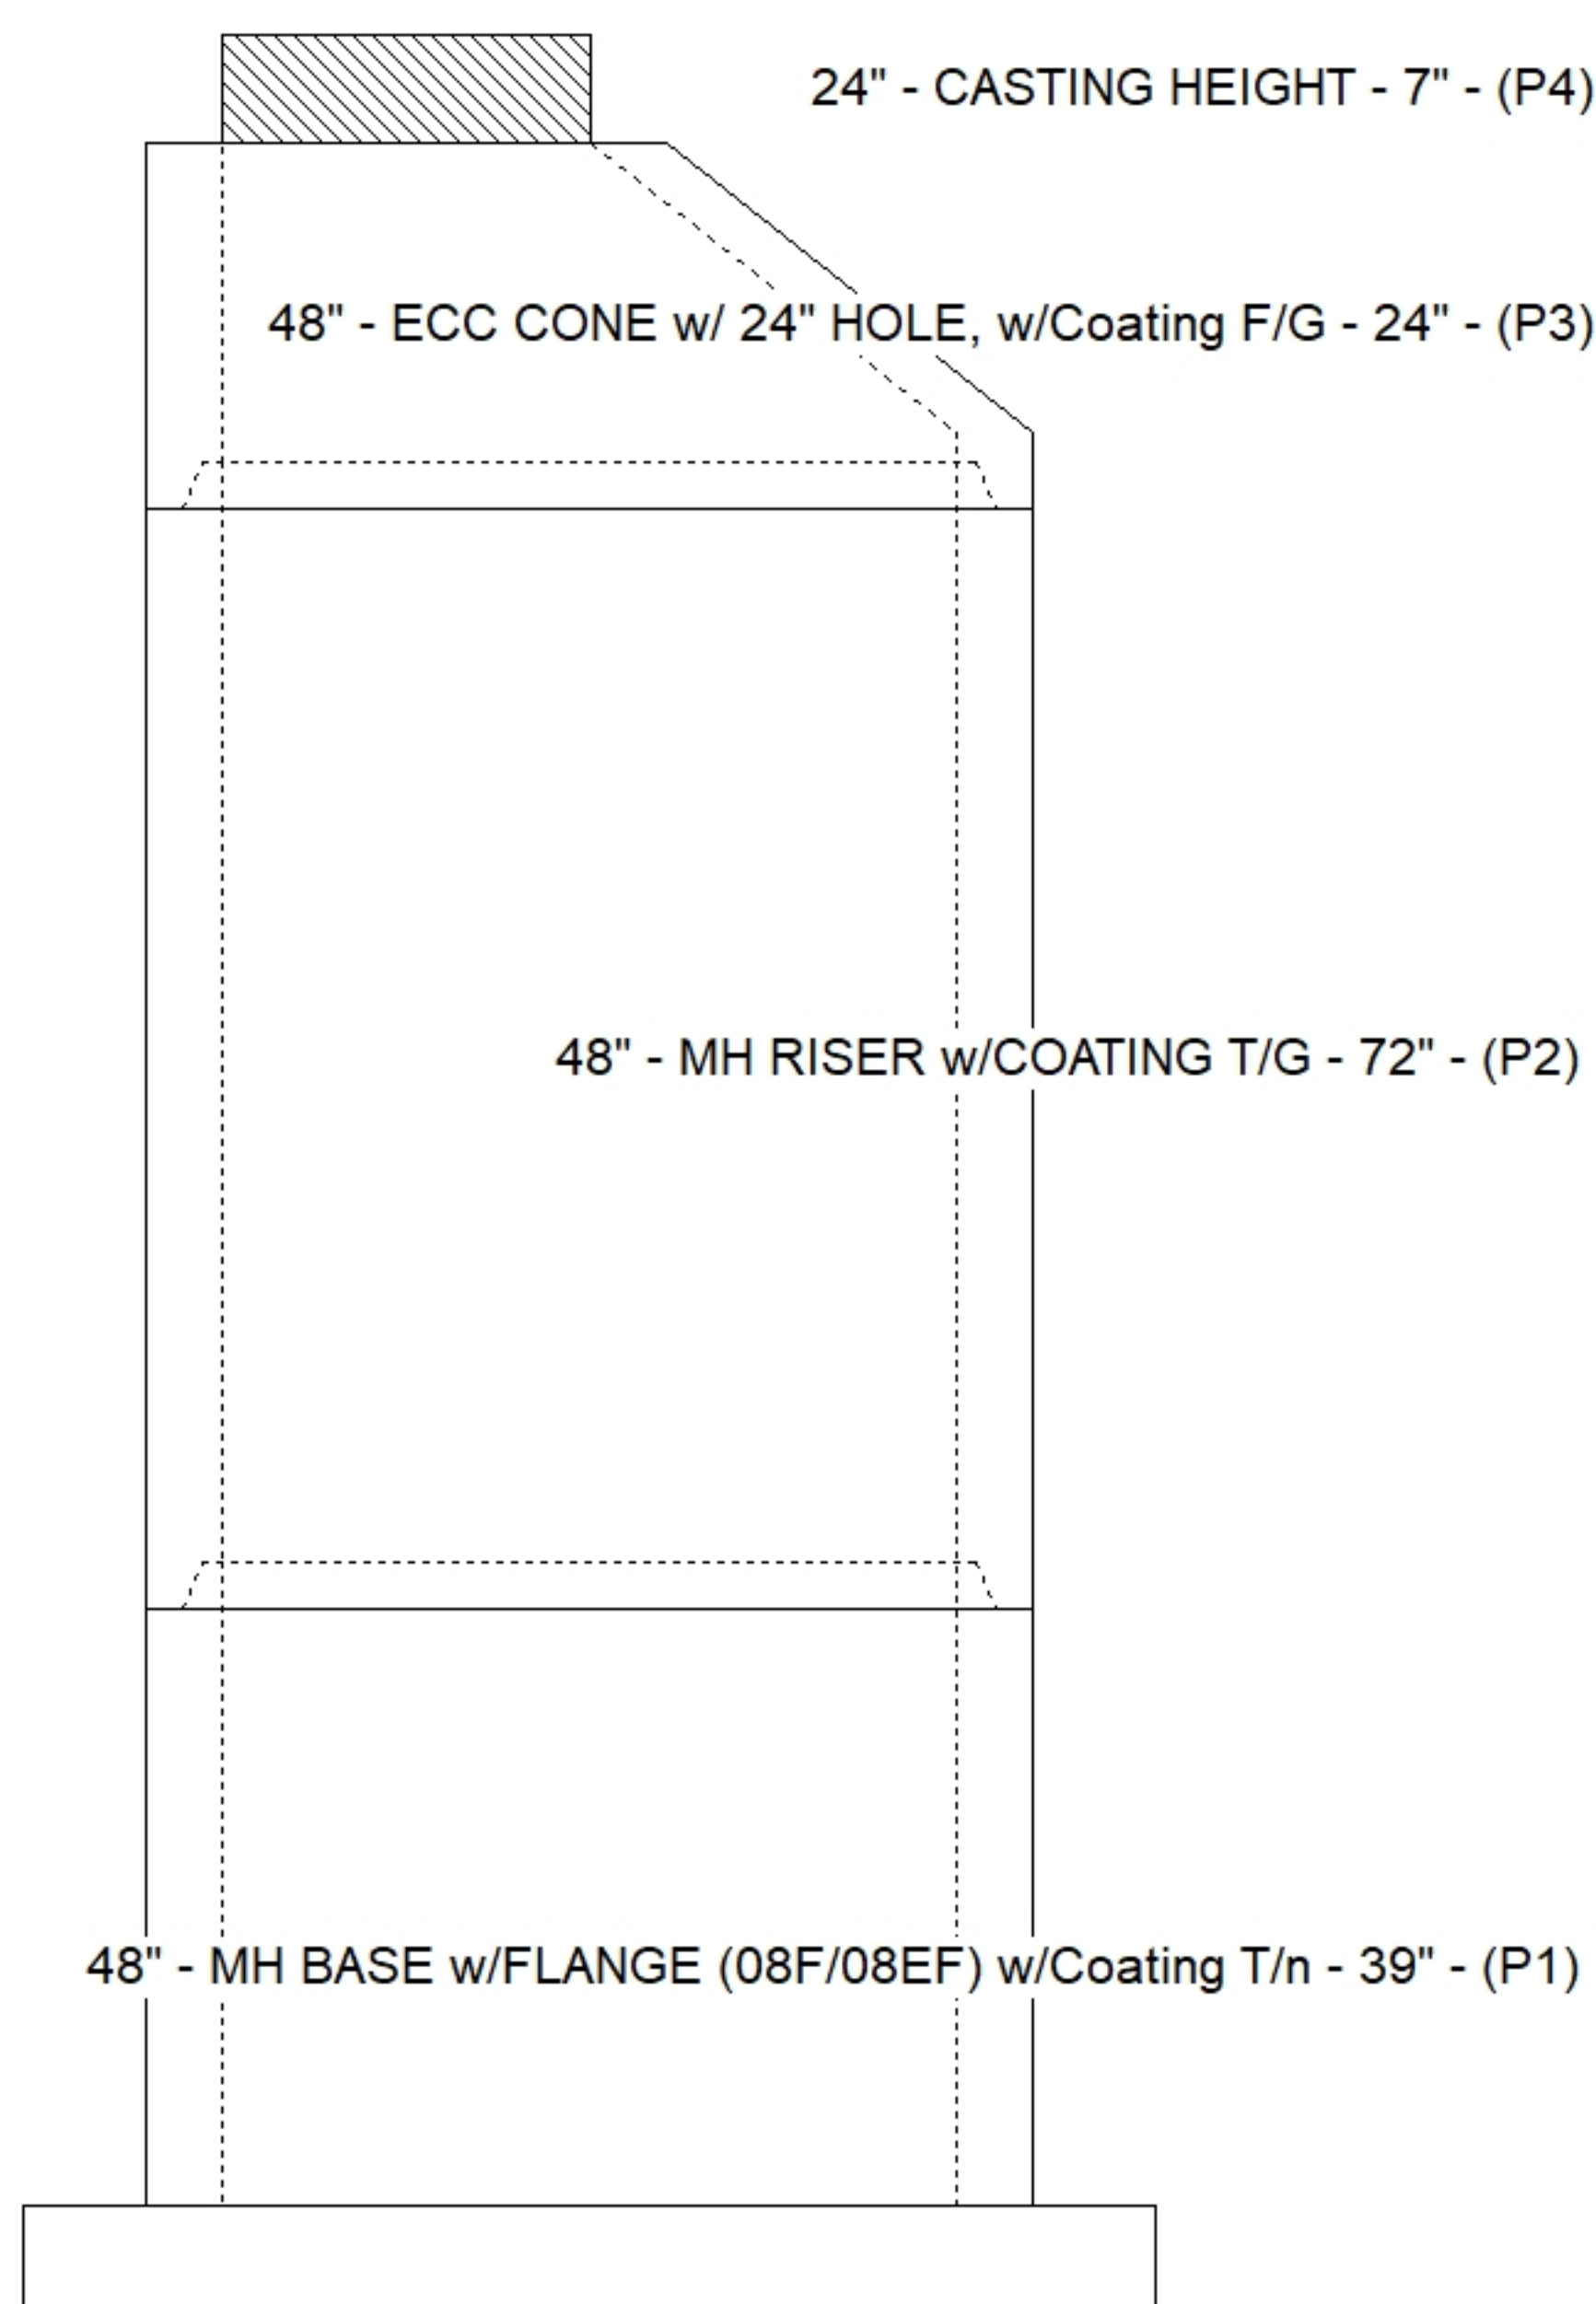

SUBMITTAL
APPROVED BY:
