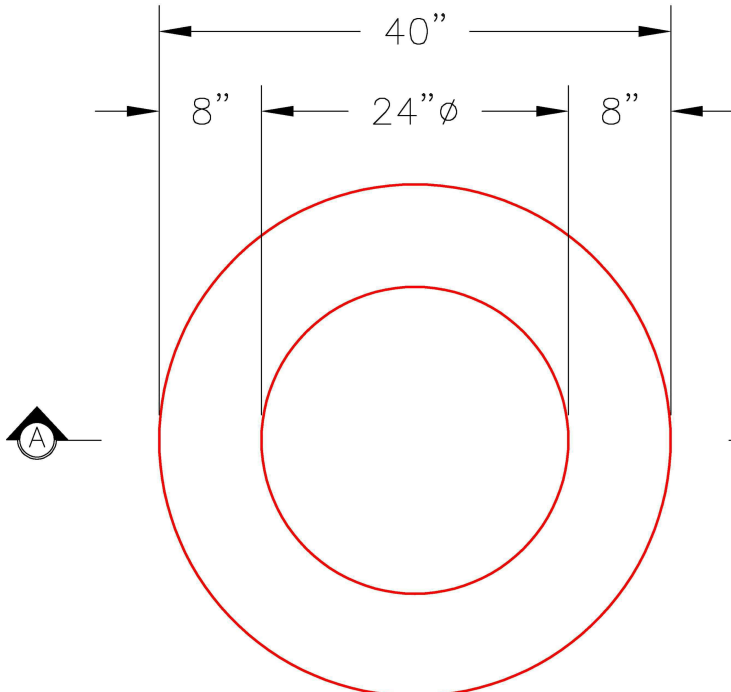

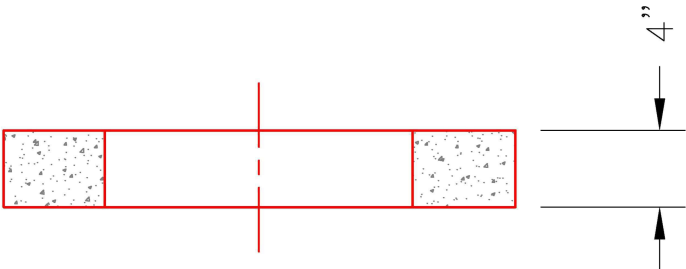


Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2		Plant: 100	Tech: J. Horsley			
Job Location: Danville, KY		6/3/2026 3:01:26 PM	PC: C. Goff			
Contractor: Hubert Excavating & Contracting						
Structure ID: MH A7						
P5	GR4	GRADE RING F/F				
P6) 24" - CASTING HEIGHT - 7"		0 lb	Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: (1) #3 HOOP CENTERED (GRADE 60) 4. CARBOLINE 300M EXTERIOR COATING REQUIRED			
P5) 24" - GRADE RING F/F - 4"		270 lb				
P4) 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 42"		3116 lb				
P3) 48" - MH RISER w/COATING T/G - 72"		5030 lb				
P2) 60" - MH Trans. Slab - 48" Hole ECC, w/Coating T/G - 13"		1928 lb				
P1) 60" - MH BASE w/FLANGE (08F/07EF) w/Coating T/n - 60"		9231 lb				
1) 60" - MH INVERT CHANNEL - FULL HEIGHT		2692 lb				
1) JOINT WRAP - 12" WD x 060" MAC WRAP		0 lb				
1) SPECIAL EXTERNAL COATING - Carboline 300M		0 lb				
1) SECONDARY POUR - Extended Flange		0 lb				
2) JOINT WRAP - 12" WD x 048" MAC WRAP		0 lb				
1) 60" - Conseal CS-102 1.00" (Double)		0 lb				
2) 48" - Conseal CS-102 1.00" (Double)		0 lb				
2) 24" - Conseal CS-102 1.00" (Double)		0 lb				
2) A-Lok - 1040		2 lb				
15) MH Step ML-10-TDS-NCR - 10"		0 lb				
292.89 SqFt) Carboline Bitumastic 300M [EXT]		0 lb				
Structure Total:		22269 lb				
 PLAN VIEW  ISOMETRIC VIEW  SECTION A-A						
Coating (Int): Coating (Ext): Carboline Bitumastic 300M		Seam Up: Flat Seam Dn: Flat			Wall Thickness: 8"	Height (Ext): 4"
				Weight (Net): 270 lb Volume (Net): 0.07cu.yd		

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer
Ph 2

Structure:

MH A7

Note:

This Structure Is To Receive An
External Coating of Carboline 300M
(Supplied By iCast)
