




Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2 Job Location: Danville, KY Contractor: Hubert Excavating & Contracting				Plant: 100 6/7/2026 1:25:20 PM		Tech: J. Horsley PC: C. Goff				
Structure ID: MH A9										
P3 MH072RS72S				MH RISER SPECIAL w/COATING T/G						
P5) 24" - CASTING HEIGHT - 7" P4) 72" - MH FLAT TOP SPECIAL F/G - 15" P3) 72" - MH RISER SPECIAL w/COATING T/G - 72" P2) 72" - MH RISER w/COATING T/G - 72" P1) 72" - MH BASE w/FLANGE (08F/07EF) w/Coating T/n - 43" 1) SPECIAL EXTERNAL COATING - Carboline 300M 1) 72" - MH INVERT CHANNEL - FULL HEIGHT 3) JOINT WRAP - 12" WD x 072" MAC WRAP 1) SECONDARY POUR - Extended Flange 3) 72" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 1040 2) Kor-N-Seal2 - S206-28 15) MH Step ML-10-TDS-NCR - 10" 436.79 SqFt) Carboline Bitumastic 300M [EXT] <td colspan="2"> 0 lb 5254 lb 10126 lb 10496 lb 10101 lb 0 lb 5422 lb 0 lb 0 lb 0 lb 0 lb 2 lb 13 lb 0 lb 0 lb Structure Total: 41414 lb </td> <td colspan="5"> Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. CARBOLINE 300M EXTERIOR COATING REQUIRED 5. STEPS AT 90 DEGREES 6. HOE MC-375 FRAME & COVER "SANITARY" SUPPLIED BY OTHERS 7. EXTERIOR DROP ASSEMBLY AT INVERTS 3 & 4 BY OTHERS - ICAST TO SUPPLY OPENINGS & BOOTS </td>				0 lb 5254 lb 10126 lb 10496 lb 10101 lb 0 lb 5422 lb 0 lb 0 lb 0 lb 0 lb 2 lb 13 lb 0 lb 0 lb Structure Total: 41414 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. CARBOLINE 300M EXTERIOR COATING REQUIRED 5. STEPS AT 90 DEGREES 6. HOE MC-375 FRAME & COVER "SANITARY" SUPPLIED BY OTHERS 7. EXTERIOR DROP ASSEMBLY AT INVERTS 3 & 4 BY OTHERS - ICAST TO SUPPLY OPENINGS & BOOTS				
Rim: 906' Rim to Invert: 17.315' Slack: 0.995" Sump: 2.215" Step Position: 90°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4	900.95'	245°	183.875"	24" PVC F679 (PS46)	24.803"	Kor-N-Seal2 S206-28	28"	28.759"	27.125"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

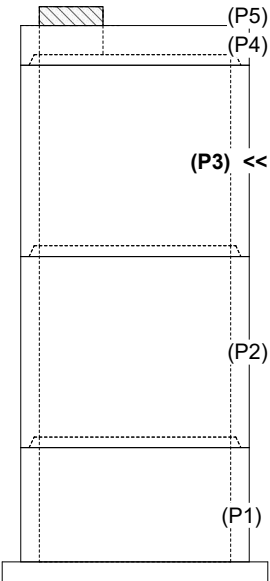

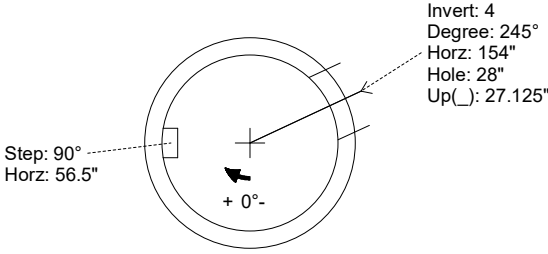

INSIDE WALL DIMENSIONS

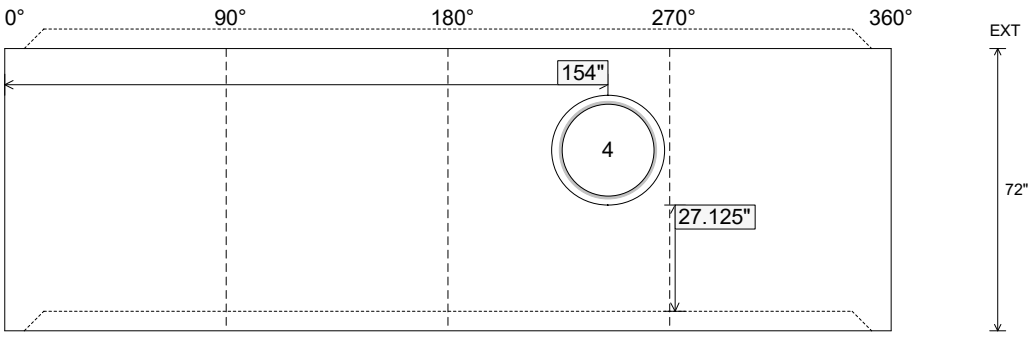

Coating (Int): Coating (Ext): Carboline Bitumastic 300M	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 7" Floor Height: 0"	Height (Int): 72" Height (Ext): 72"	Weight (Net): 10126 lb Volume (Net): 2.59cu.yd
--	------------------------------------	--	--	---

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer
Ph 2

Structure:

MH A9

Note:

This Structure Is To Receive An
External Coating of Carboline 300M
(Supplied By iCast)
