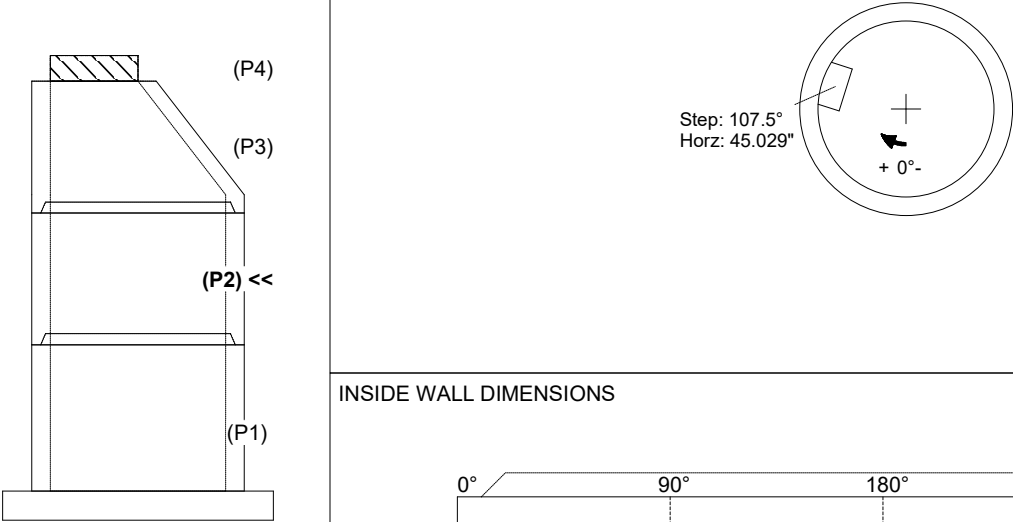



Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2					Plant: 100		Tech: J. Horsley				
Job Location: Danville, KY					8/21/2026 1:12:54 PM		PC: C. Goff				
Contractor: Hubert Excavating & Contracting											
Structure ID: MH D1											
P2		MH048RS36S									
MH RISER w/COATING T/G											
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 36" P2) 48" - MH RISER w/COATING T/G - 36" P1) 48" - MH BASE w/FLANGE (08F/08EF) w/Coating T/n - 40" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 12" WD x 048" MAC WRAP 1) SPECIAL EXTERNAL COATING 2) 48" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-28 9) MH Step ML-10-TDS-NCR - 10" 147.17 SqFt) Carboline Bitumastic 300M [EXT] 0 lb 2251 lb 2515 lb 5136 lb 1440 lb 0 lb 0 lb 0 lb 13 lb 0 lb 0 lb ----- 11355 lb Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE WT-375 SAN. F/C). 4. ALL PIECES TO HAVE EXTERIOR COATING (CARBOLINE BITUMASTIC 300M). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					Rim: 902.47' Rim to Invert: 9.83' Slack: 1.27" Sump: 2.31" Step Position: 107.5°						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
 INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext): Carboline Bitumastic 300M			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 36" Height (Ext): 36"		Weight (Net): 2515 lb Volume (Net): 0.64cu.yd		

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer Ph 2

Structure:

MH D1

Note:

This structure is to receive an external coating of carbolite 300M (supplied by ICAST)
