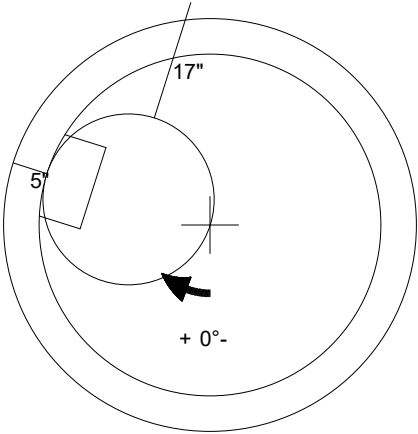



Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2		Plant: 100	Tech: J. Horsley		
Job Location: Danville, KY		8/21/2026 1:04:31 PM	PC: C. Goff		
Contractor: Hubert Excavating & Contracting					
Structure ID: MH D1					
P3 MH048CN36SP		ECC CONE w/ 24" HOLE, w/Coating F/G			
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 36" P2) 48" - MH RISER w/COATING T/G - 36" P1) 48" - MH BASE w/FLANGE (08F/08EF) w/Coating T/n - 40" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 12" WD x 048" MAC WRAP 1) SPECIAL EXTERNAL COATING 2) 48" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-28 9) MH Step ML-10-TDS-NCR - 10" 147.17 SqFt) Carboline Bitumastic 300M [EXT]		0 lb 2251 lb 2515 lb 5136 lb 1440 lb 0 lb 0 lb 0 lb 13 lb 0 lb 0 lb ----- 11355 lb	Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE WT-375 SAN. F/C). 4. ALL PIECES TO HAVE EXTERIOR COATING (CARBOLINE BITUMASTIC 300M). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
					
 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 36" - (P3)					
Coating (Int): Coating (Ext): Carboline Bitumastic 300M		Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 2251 lb Volume (Net): 0.57cu.yd

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer Ph 2

Structure:

MH D1

Note:

This structure is to receive an external coating of carbolite 300M (supplied by ICAST)
