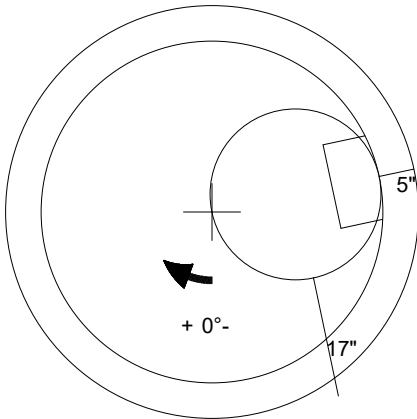



Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2		Plant: 100	Tech: J. Horsley	
Job Location: Danville, KY		8/21/2026 1:04:32 PM	PC: C. Goff	
Contractor: Hubert Excavating & Contracting				
Structure ID: MH E1				
P3	MH048CN42SP	ECC CONE w/ 24" HOLE, w/Coating F/G		
P4) 24" - CASTING HEIGHT - 7"		0 lb	Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE WT-375 SAN. F/C). 4. ALL PIECES TO HAVE EXTERIOR COATING (CARBOLINE BITUMASTIC 300M). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
P3) 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 42"		3116 lb		
P2) 48" - MH RISER w/COATING T/G - 24"		1677 lb		
P1) 48" - MH BASE w/FLANGE (08F/08EF) w/Coating T/n - 24"		4392 lb		
1) 48" - MH INVERT CHANNEL - FULL HEIGHT		1440 lb		
1) JOINT WRAP - 12" WD x 048" MAC WRAP		0 lb		
1) SPECIAL EXTERNAL COATING		0 lb		
2) 48" - Conseal CS-102 1.00" (Double)		0 lb		
2) PSX - 16M NYLO		16 lb		
8) MH Step ML-10-TDS-NCR - 10"		0 lb		
117.49 SqFt) Carboline Bitumastic 300M [EXT]		0 lb		
Structure Total:		10641 lb		
				
				
Coating (Int): Coating (Ext): Carboline Bitumastic 300M	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 42"	Weight (Net): 3116 lb Volume (Net): 0.8cu.yd

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer Ph 2

Structure:

MH E1

Note:

This structure is to receive an external coating of carboline 300M (supplied by ICAST)
