

Contractor: Hubert Excavating & Contracting

PC:	C. Goff
TECH:	J. Horsley
Plant:	100



Spec: Sanitary
Type: SAN.MH w/Coating
Size: 48"

Rim: 903.3'
Invert: 895.38'
Rim to Invert: 7.92'

Sump: 2"
Floor (Top): 895.213'
Floor Height: 8"


Floor (Bot): 894.547'
Overall Height: 8.75'
Slack: 0.04"

Structure Notes: 1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY OTHERS (HOE WT-375 SAN. F/C).
4. ALL PIECES TO HAVE EXTERIOR COATING (CARBOLINE BITUMASTIC 300M).
REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


STRUCTURE SUMMARY:

P4)	24" - CASTING HEIGHT - 7"	0 lb
P3)	48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 42"	3116 lb
P2)	48" - MH RISER w/COATING T/G - 24"	1677 lb
P1)	48" - MH BASE w/FLANGE (08F/08EF) w/Coating T/n - 24"	4392 lb
1)	48" - MH INVERT CHANNEL - FULL HEIGHT	1440 lb
1)	JOINT WRAP - 12" WD x 048" MAC WRAP	0 lb
1)	SPECIAL EXTERNAL COATING	0 lb
2)	48" - Conseal CS-102 1.00" (Double)	0 lb
2)	PSX - 16M NYLO	16 lb
8)	MH Step ML-10-TDS-NCR - 10"	0 lb
	117.49 SqFt) Carboline Bitumastic 300M [EXT]	0 lb


Structure Total: 10641 lb

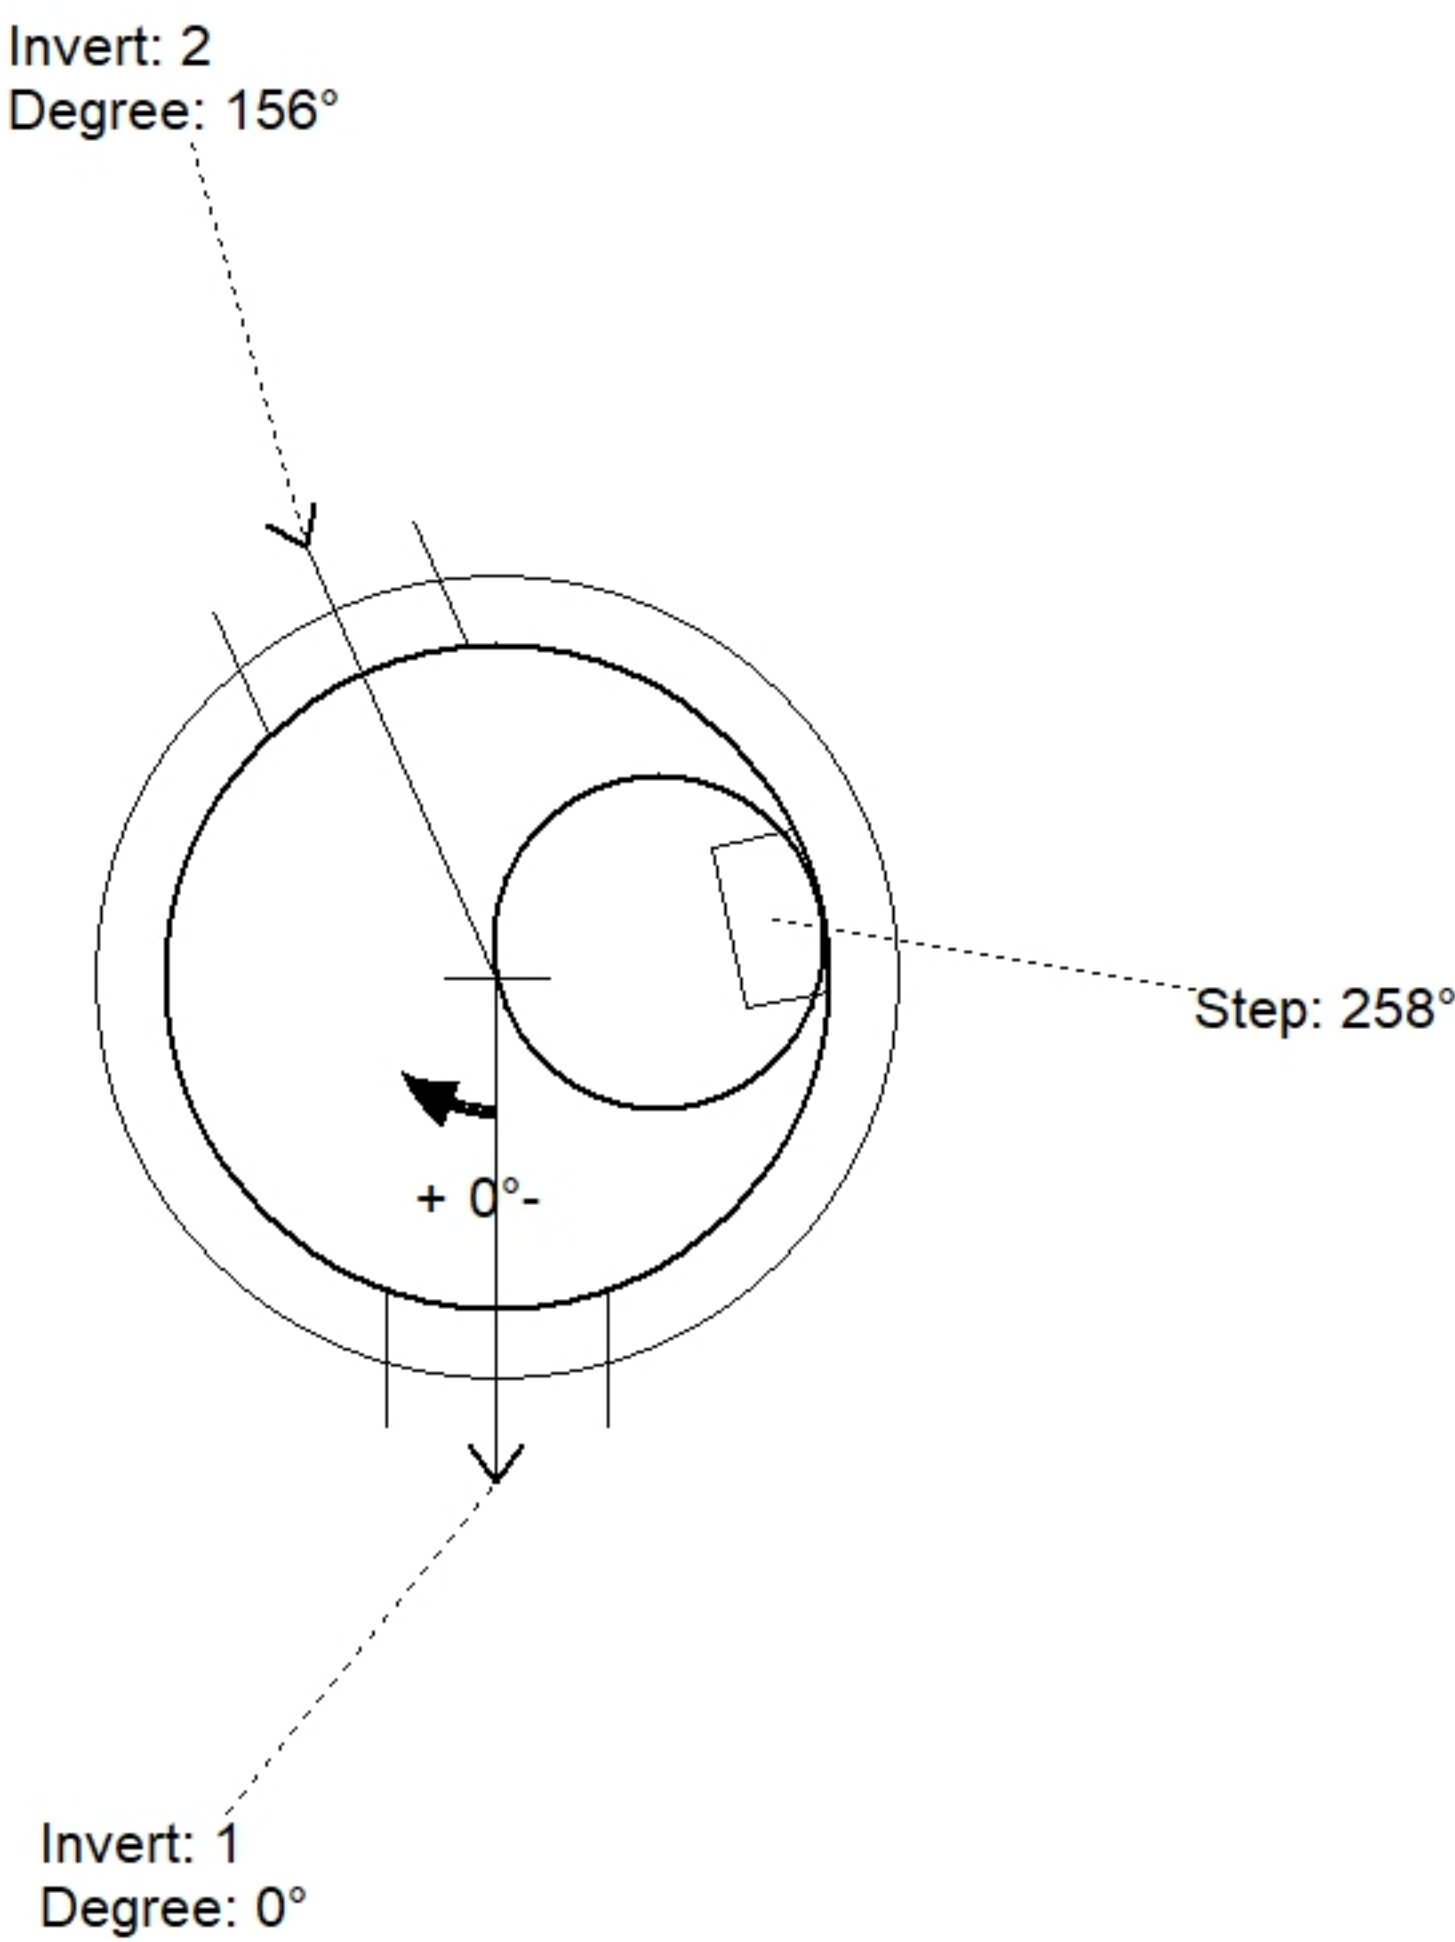

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	903.3'							
Reducer								
Invert 1	895.38'	0°	12" PVC SDR35	12.5"	16"	PSX 16M NYLO	0"	P1
Invert 2	895.43'	156°	12" PVC SDR35	12.5"	16"	PSX 16M NYLO	0.6"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

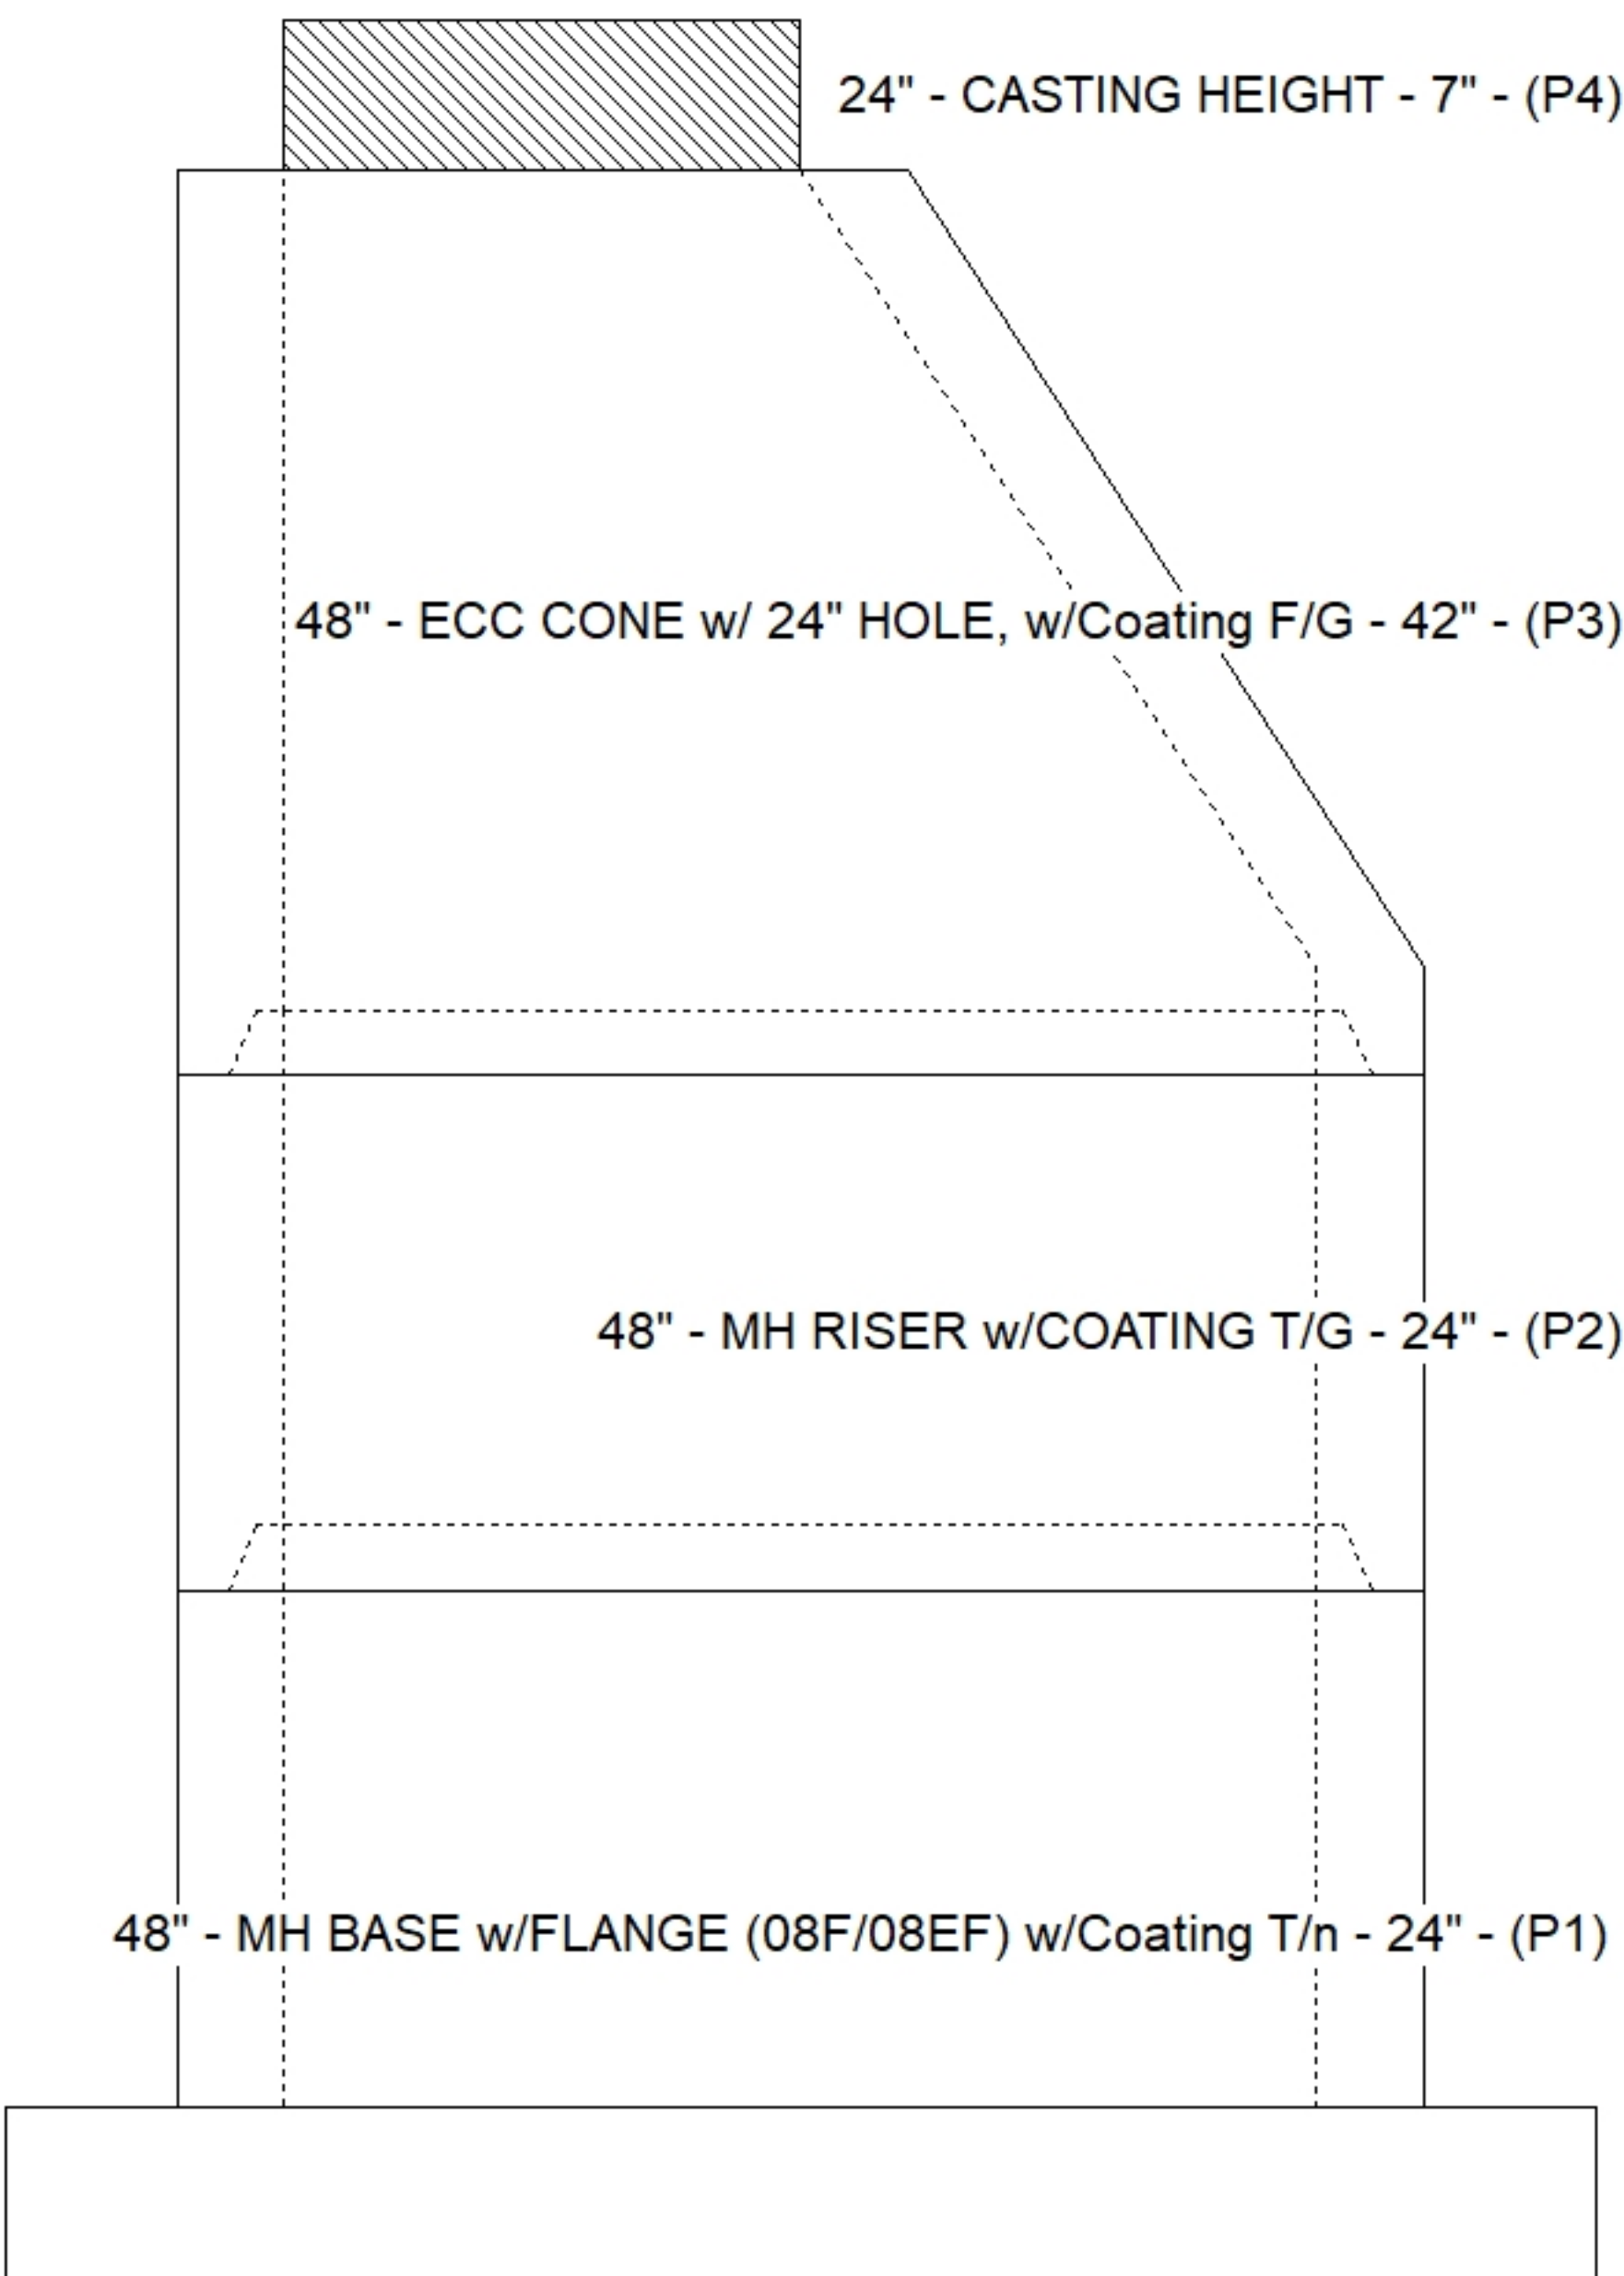

Default - Interior Dimensions

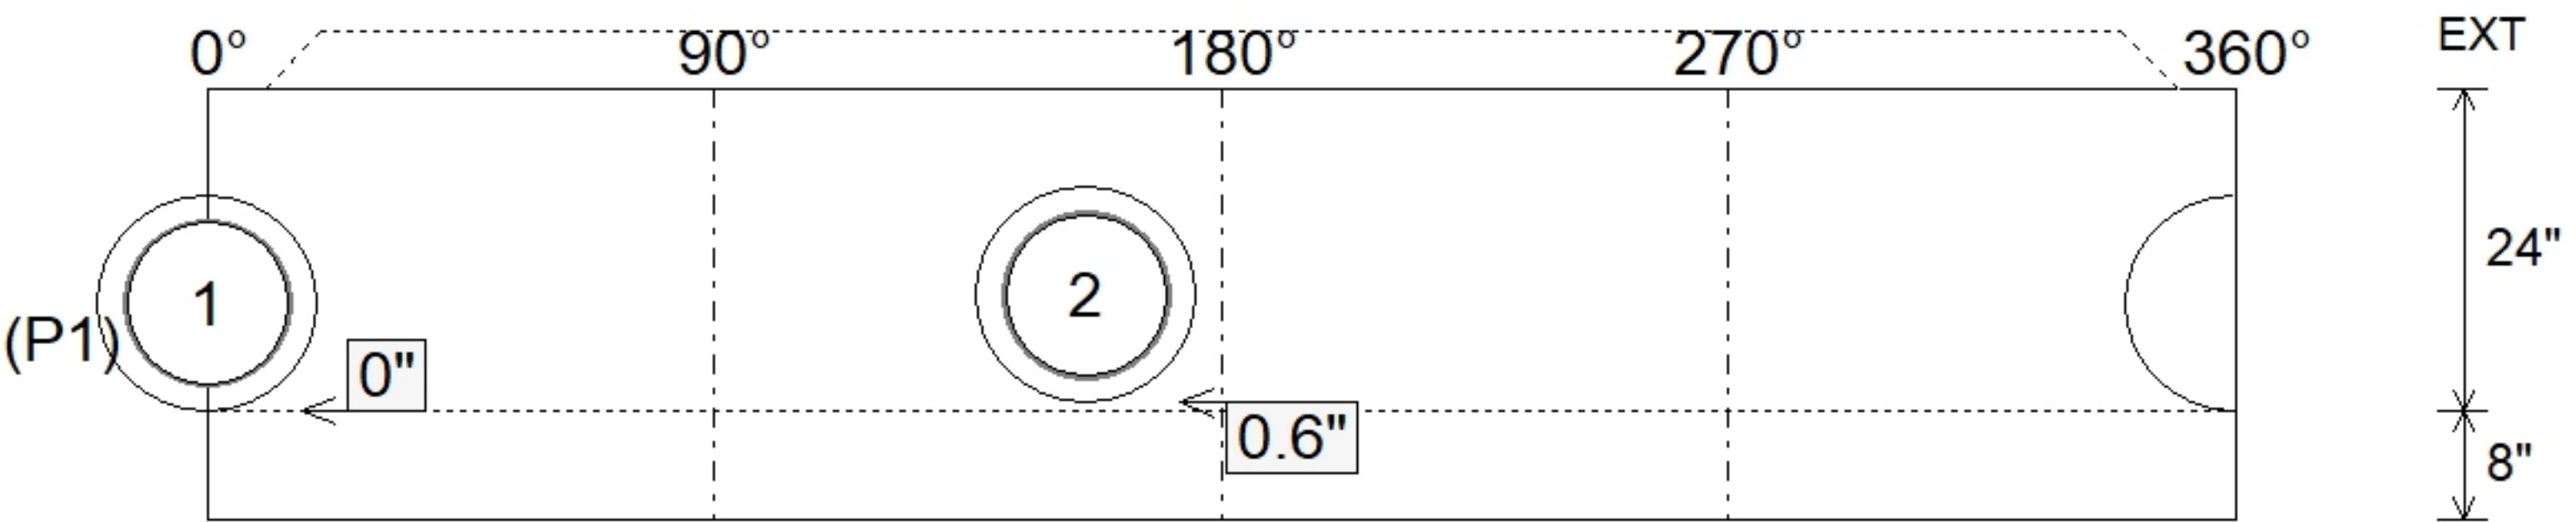

Submittal Drawing
8/27/2026 3:32:33 PM

SUBMITTAL
APPROVED BY:
