

Contractor: Hubert Excavating & Contracting

PC:	C. Goff
TECH:	J. Horsley
Plant:	100



Structure ID: MH E2

Spec: Sanitary
Type: SAN.MH w/Coating
Size: 48"


Rim: 903.62'	Sump: 2"
Invert: 896.34'	Floor (Top): 896.173'
Rim to Invert: 7.28'	Floor Height: 8"

Floor (Bot): 895.507'
Overall Height: 8.083'
Slack: 0.36"


Structure Notes: 1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY OTHERS (HOE WT-375 SAN. F/C).
4. ALL PIECES TO HAVE EXTERIOR COATING (CARBOLINE BITUMASTIC 300M).
REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:


P4)	24" - CASTING HEIGHT - 7"	0 lb
P3)	24" - GRADE RING F/F - 4"	270 lb
P2)	48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 42"	3116 lb
P1)	48" - MH BASE w/FLANGE (08F/08EF) w/Coating T/n - 36"	5268 lb
1)	48" - MH INVERT CHANNEL - FULL HEIGHT	1440 lb
1)	JOINT WRAP - 12" WD x 048" MAC WRAP	0 lb
1)	SPECIAL EXTERNAL COATING	0 lb
1)	48" - Conseal CS-102 1.00" (Double)	0 lb
1)	PSX - 16M NYLO	8 lb
1)	PSX - 12-08 NYLO	8 lb
7)	MH Step ML-10-TDS-NCR - 10"	0 lb
	102.3 SqFt) Carboline Bitumastic 300M [EXT]	0 lb
	Structure Total:	10111 lb

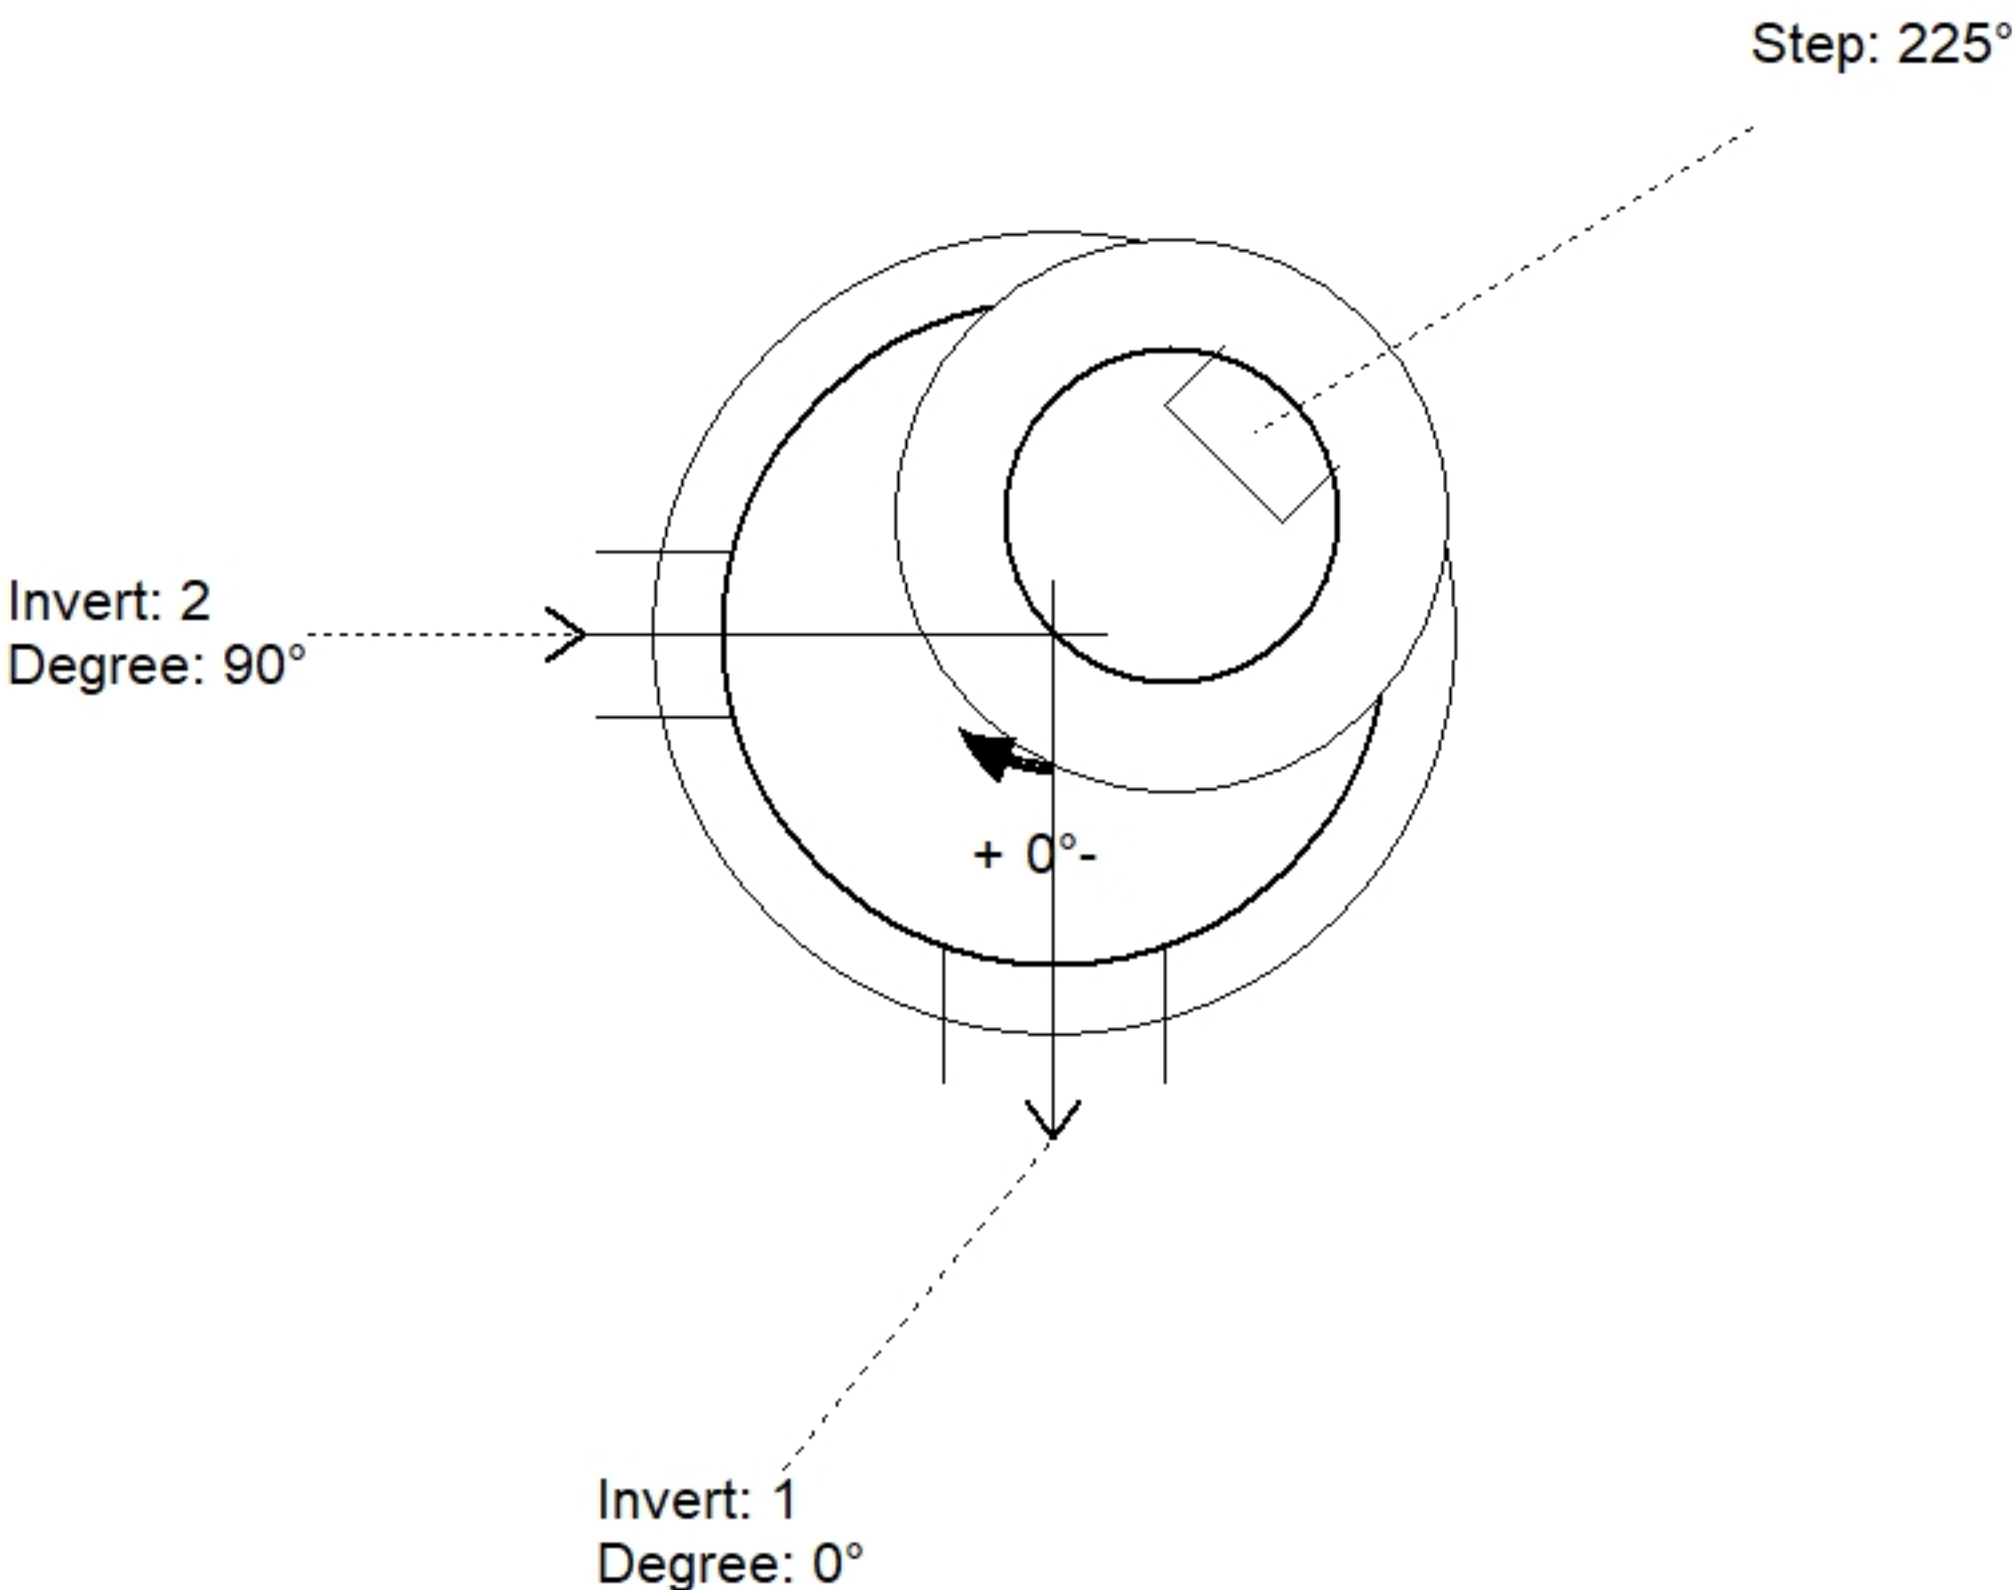

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')_	Ref
Rim	903.62'							
Reducer								
Invert 1	896.34'	0°	12" PVC SDR35	12.5"	16"	PSX 16M NYLO	0"	P1
Invert 2	896.44'	90°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

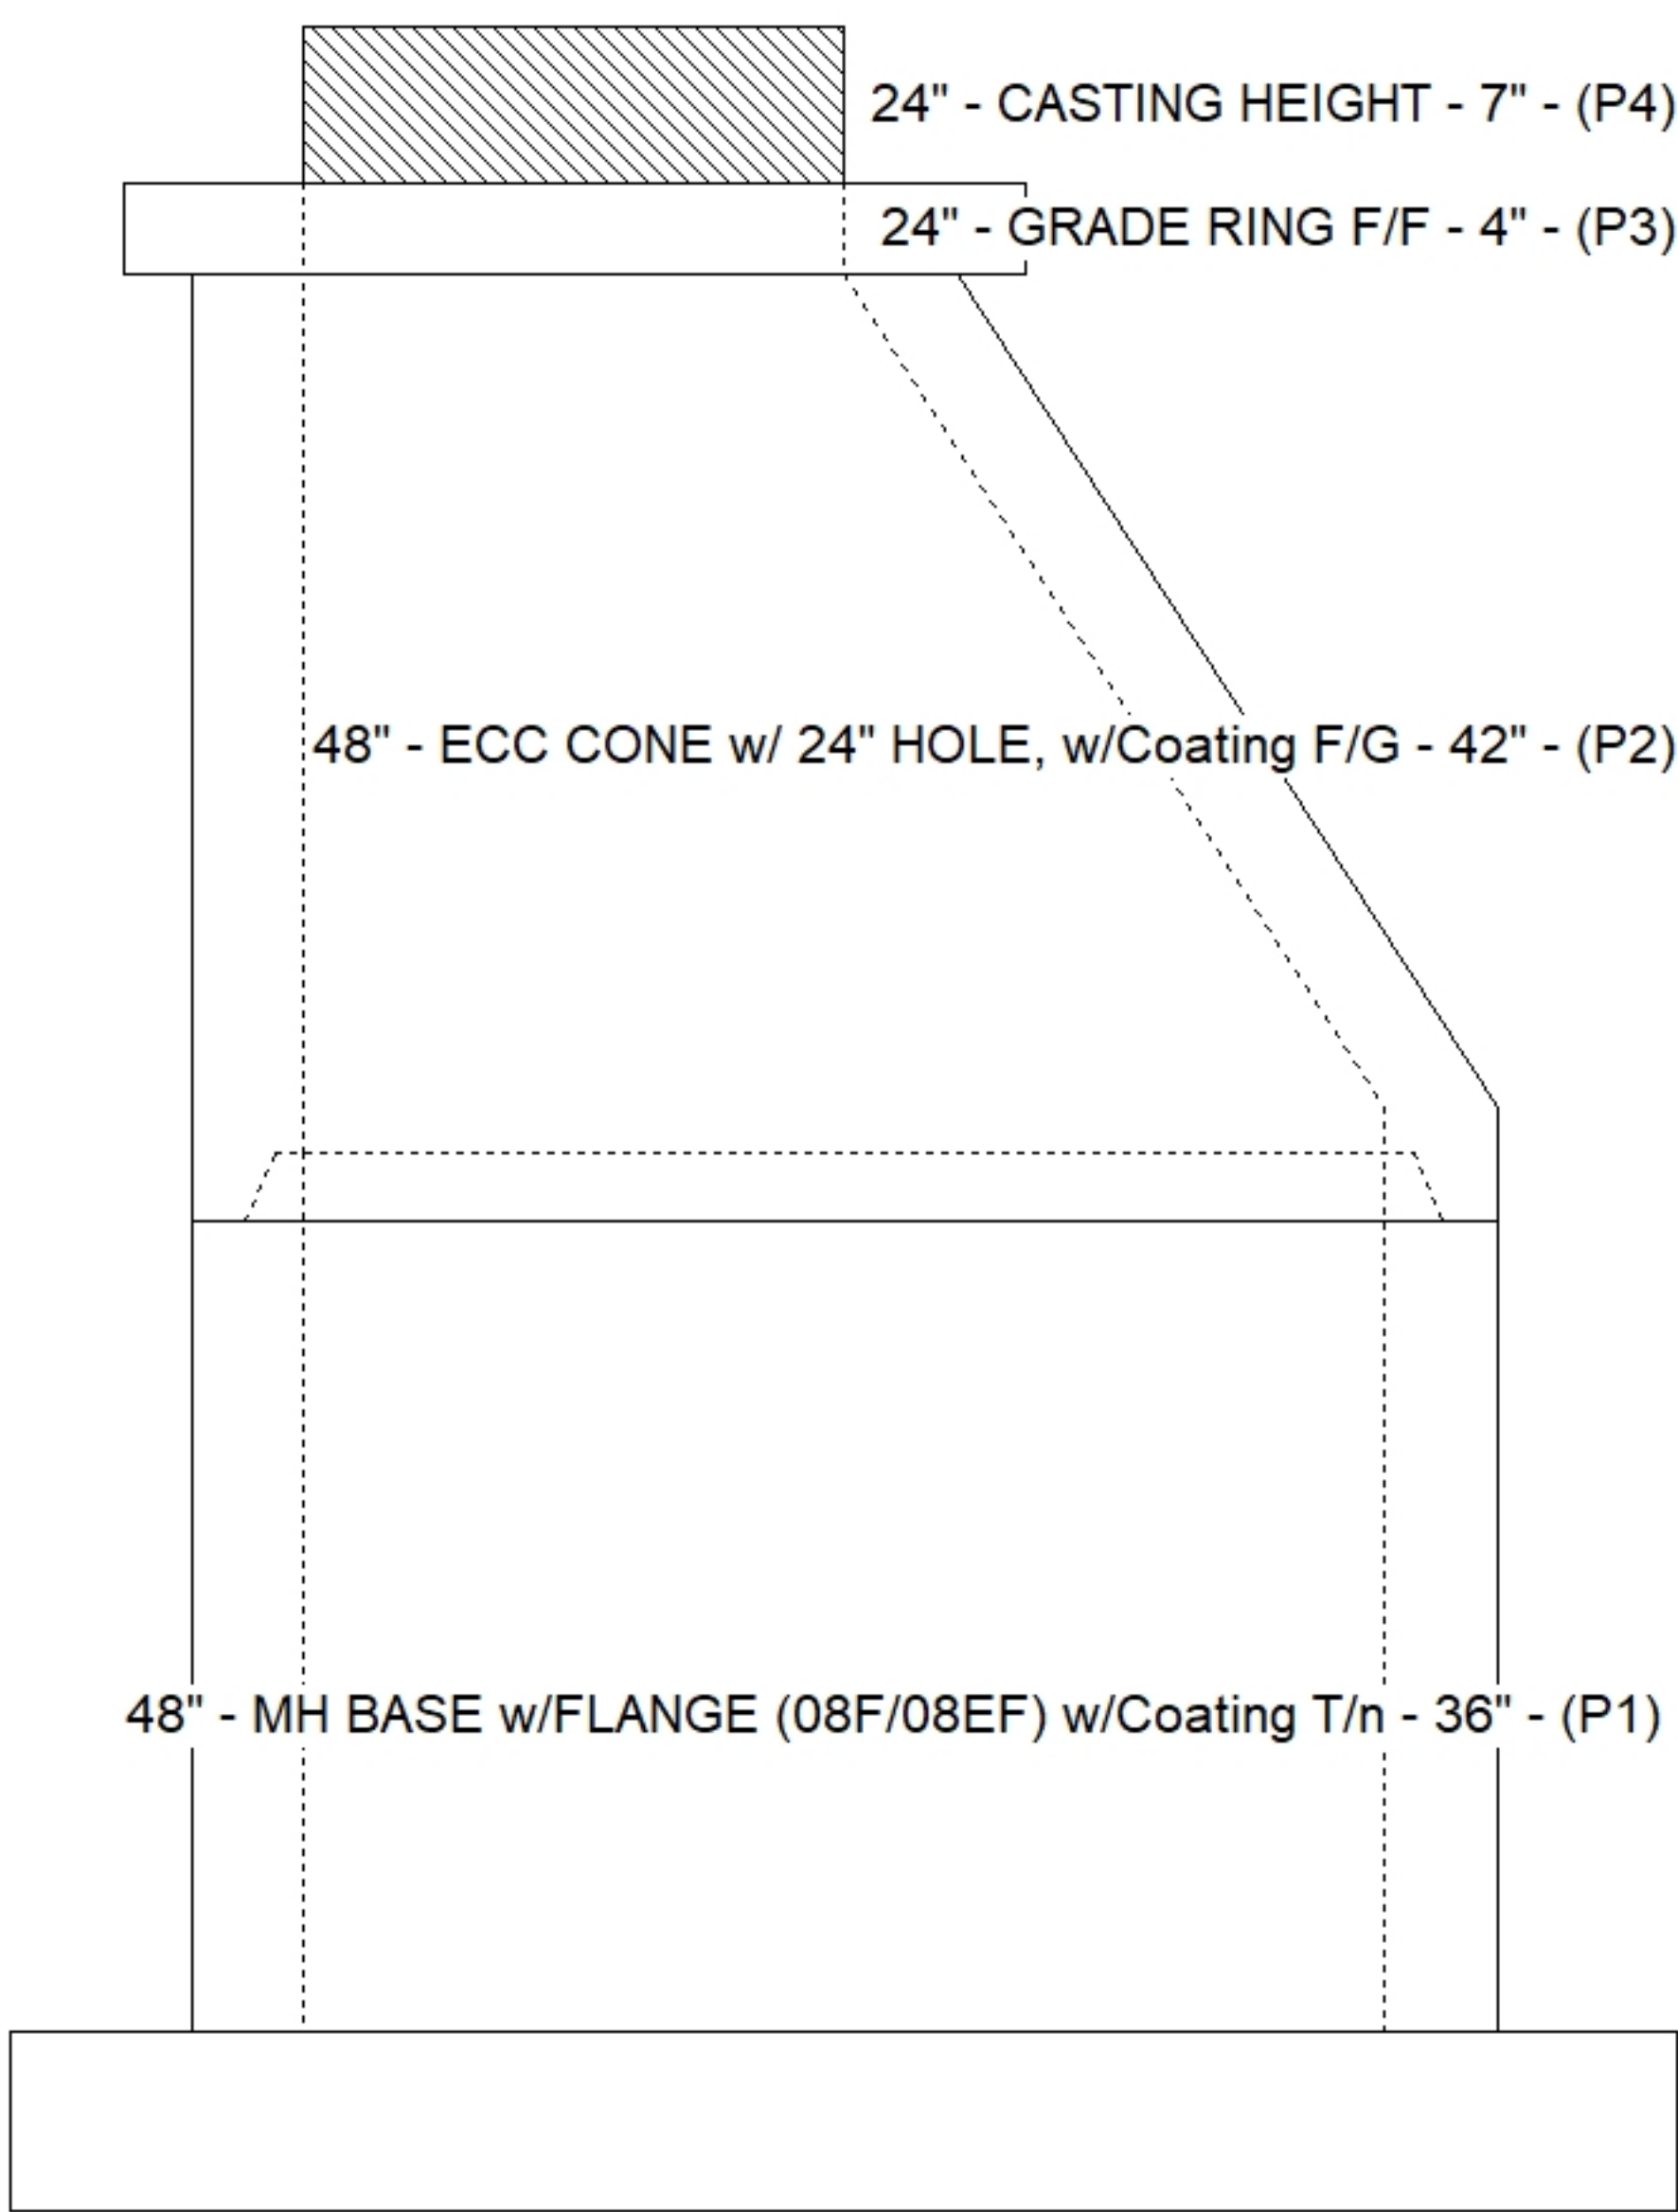

Default - Interior Dimensions

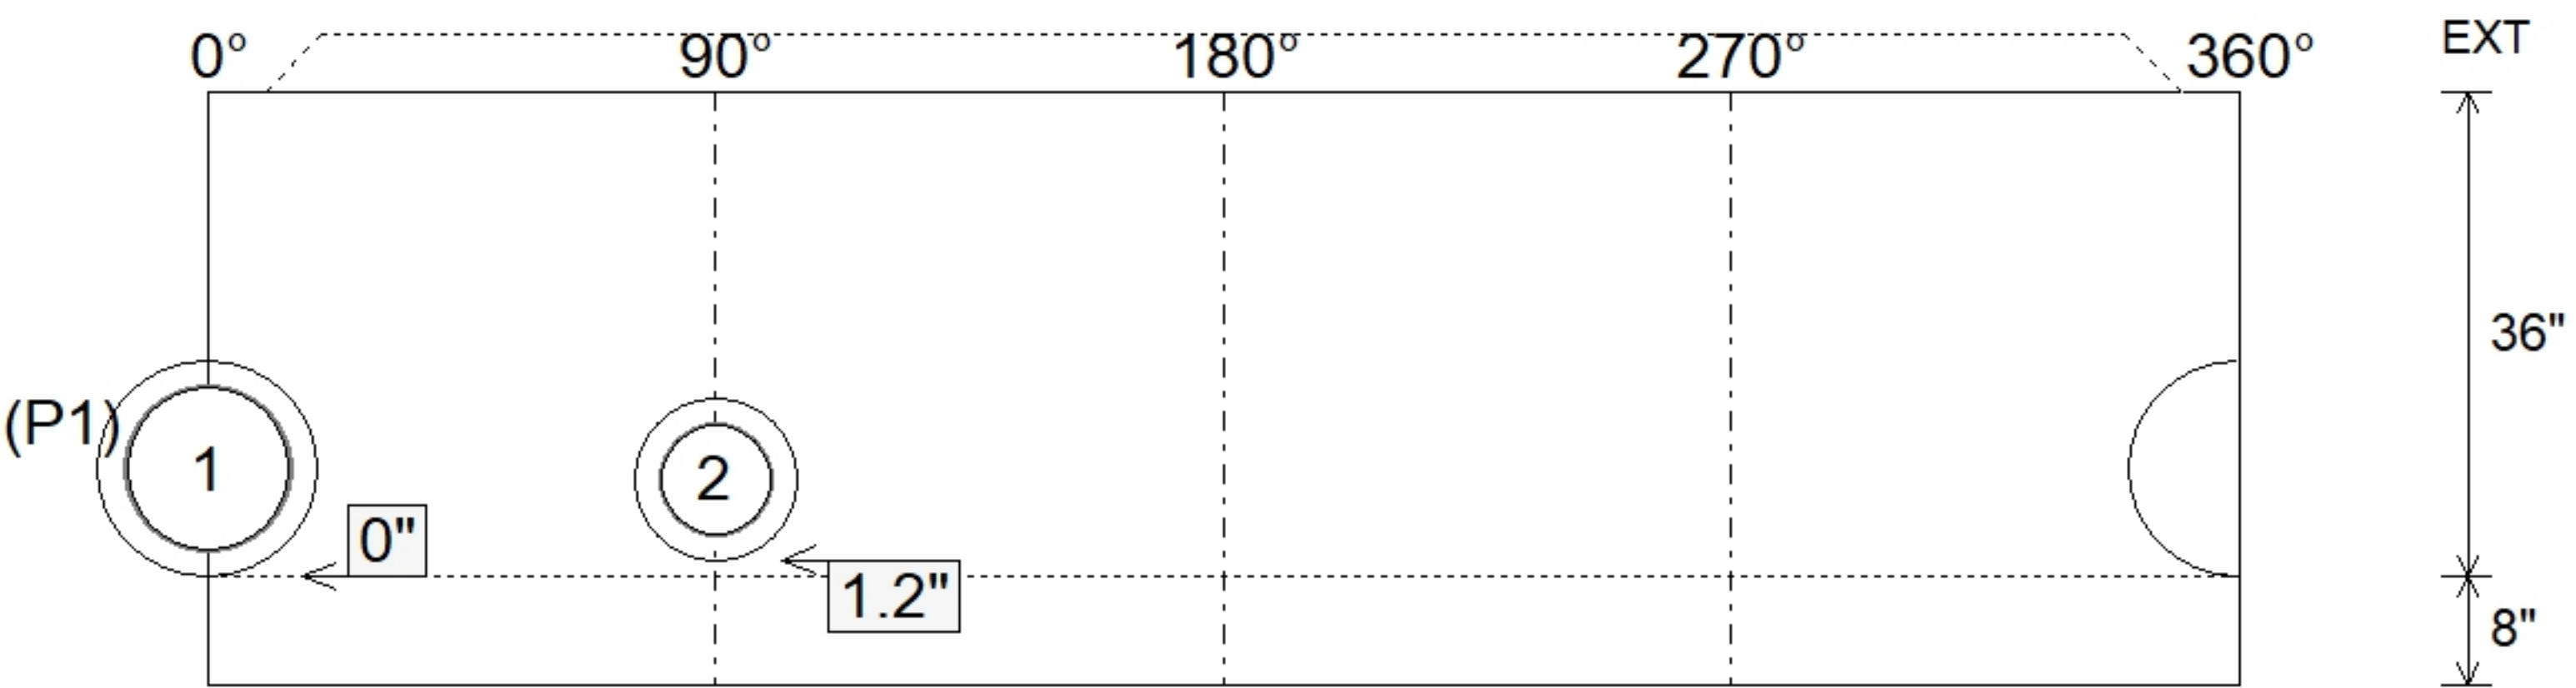

Submittal Drawing
8/27/2026 3:32:33 PM

SUBMITTAL
APPROVED BY:
