



Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2 Job Location: Danville, KY Contractor: Hubert Excavating & Contracting				Plant: 100 8/21/2026 12:57:37 PM		Tech: J. Horsley PC: C. Goff				
Structure ID: MH G1										
P1 MH048BAEVF		MH BASE w/FLANGE (08F/08EF) w/Coating T/n								
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 36" P2) 48" - MH RISER w/COATING T/G - 60" P1) 48" - MH BASE w/FLANGE (08F/08EF) w/Coating T/n - 32" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 2) JOINT WRAP - 12" WD x 048" MAC WRAP 1) SPECIAL EXTERNAL COATING 2) 48" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-18L 10) MH Step ML-10-TDS-NCR - 10" 167.41 SqFt) Carboline Bitumastic 300M [EXT]				0 lb 2251 lb 4192 lb 4905 lb 1440 lb 0 lb 0 lb 0 lb 12 lb 0 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE WT-375 SAN. F/C). 4. ALL PIECES TO HAVE EXTERIOR COATING (CARBOLINE BITUMASTIC 300M). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Structure Total:				12799 lb						
Rim: 911.13' Rim to Invert: 11.145' Slack: 0.744" Sump: 2.004" Step Position: 247"										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	899.985'	0°	0"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.451"	0.504"	0"
Invert 2	900.035'	134°	67.823"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.451"	1.104"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

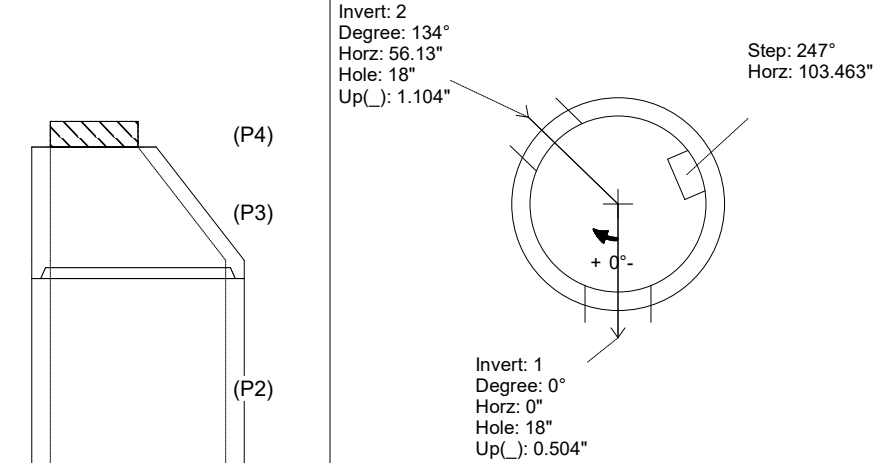

UPSIDE-DOWN VIEW (int. dimensions)

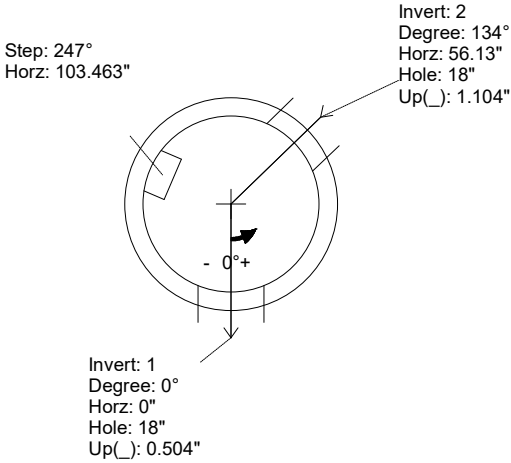


INSIDE WALL DIMENSIONS

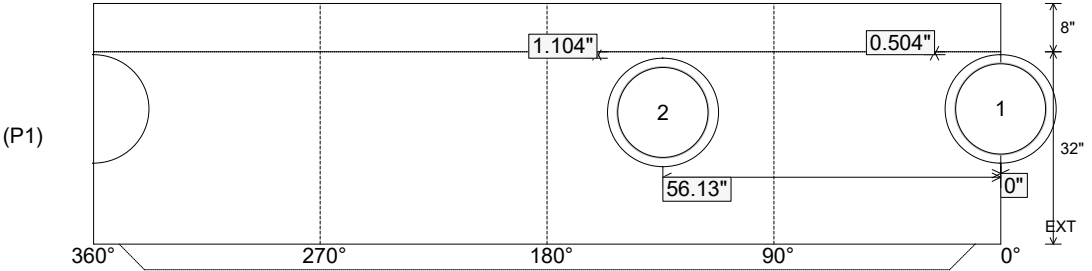


Coating (Int): Coating (Ext): Carboline Bitumastic 300M	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 8"	Height (Int): 32" Height (Ext): 40"	Weight (Net): 4905 lb Volume (Net): 1.25cu.yd
--	---------------------------------	--	--	--

Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2 Job Location: Danville, KY Contractor: Hubert Excavating & Contracting				Plant: 100 8/21/2026 12:57:37 PM		Tech: J. Horsley PC: C. Goff				
Structure ID: MH G1										
P1 MH048BAEVF		MH BASE w/FLANGE (08F/08EF) w/Coating T/n								
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 36" P2) 48" - MH RISER w/COATING T/G - 60" P1) 48" - MH BASE w/FLANGE (08F/08EF) w/Coating T/n - 32" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 2) JOINT WRAP - 12" WD x 048" MAC WRAP 1) SPECIAL EXTERNAL COATING 2) 48" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-18L 10) MH Step ML-10-TDS-NCR - 10" 167.41 SqFt) Carboline Bitumastic 300M [EXT]				0 lb 2251 lb 4192 lb 4905 lb 1440 lb 0 lb 0 lb 0 lb 12 lb 0 lb 0 lb Structure Total: 12799 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE WT-375 SAN. F/C). 4. ALL PIECES TO HAVE EXTERIOR COATING (CARBOLINE BITUMASTIC 300M). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 911.13' Rim to Invert: 11.145' Slack: 0.744" Sump: 2.004" Step Position: 247"										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	899.985'	0°	0"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.451"	0.504"	0"
Invert 2	900.035'	134°	67.823"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.451"	1.104"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

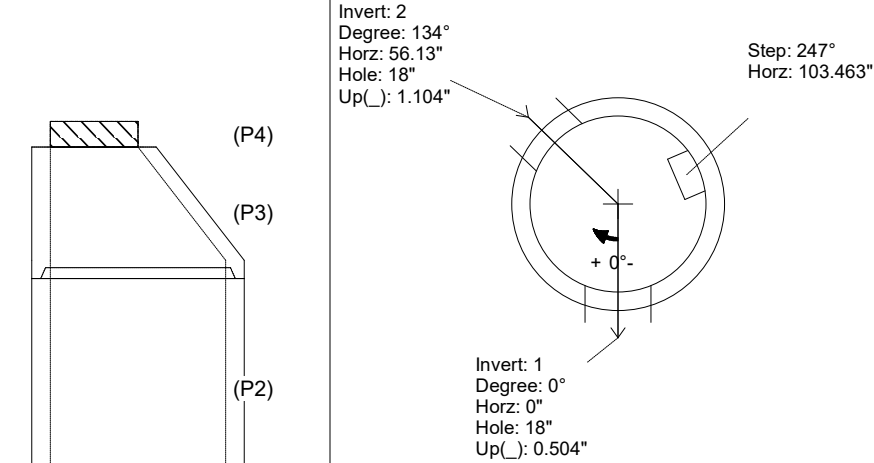

UPSIDE-DOWN VIEW (int. dimensions)

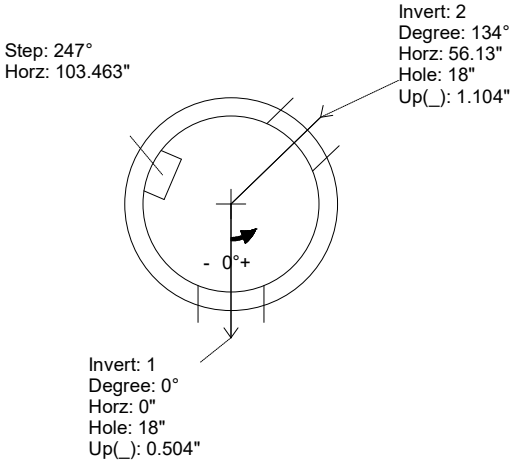

INSIDE WALL DIMENSIONS

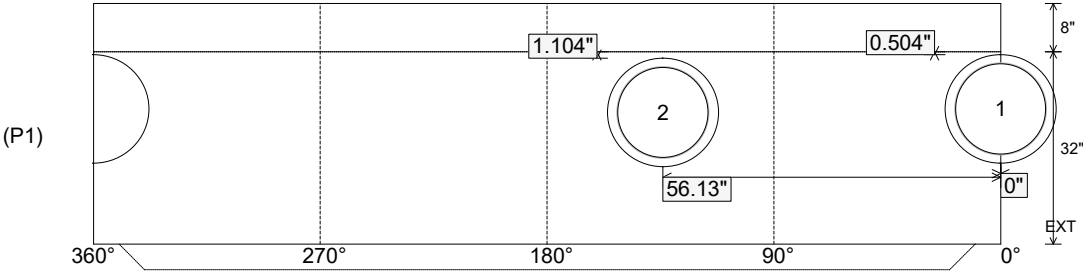

Coating (Int): Coating (Ext): Carboline Bitumastic 300M	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 8"	Height (Int): 32" Height (Ext): 40"	Weight (Net): 4905 lb Volume (Net): 1.25cu.yd
--	---------------------------------	--	--	--

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer Ph 2

Structure:

MH G1

Note:

This structure is to receive an external coating of carboline 300M (supplied by ICAST)
