





<u>Structure Notes:</u> 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.	STRUCTURE SUMMARY: P2) 24" x 24" - CASTING HEIGHT - 0" 0 lb P1) 24" x 24" - BOX BASE 6inW, 6inF, Variable Ht F/n - 39" 2660 lb 1) CASTING - TRASHRACKS LSQ-24 Sq. Top Mount Trash Rack 108 lb 1) 24" x 24" - Conseal CS-102 1.00" 0 lb 1) Hole - 26 0 lb 1) Hole - 10 0 lb 2) Weir n/n - 18"x6" 0 lb ----- Structure Total: 2768 lb
--	---

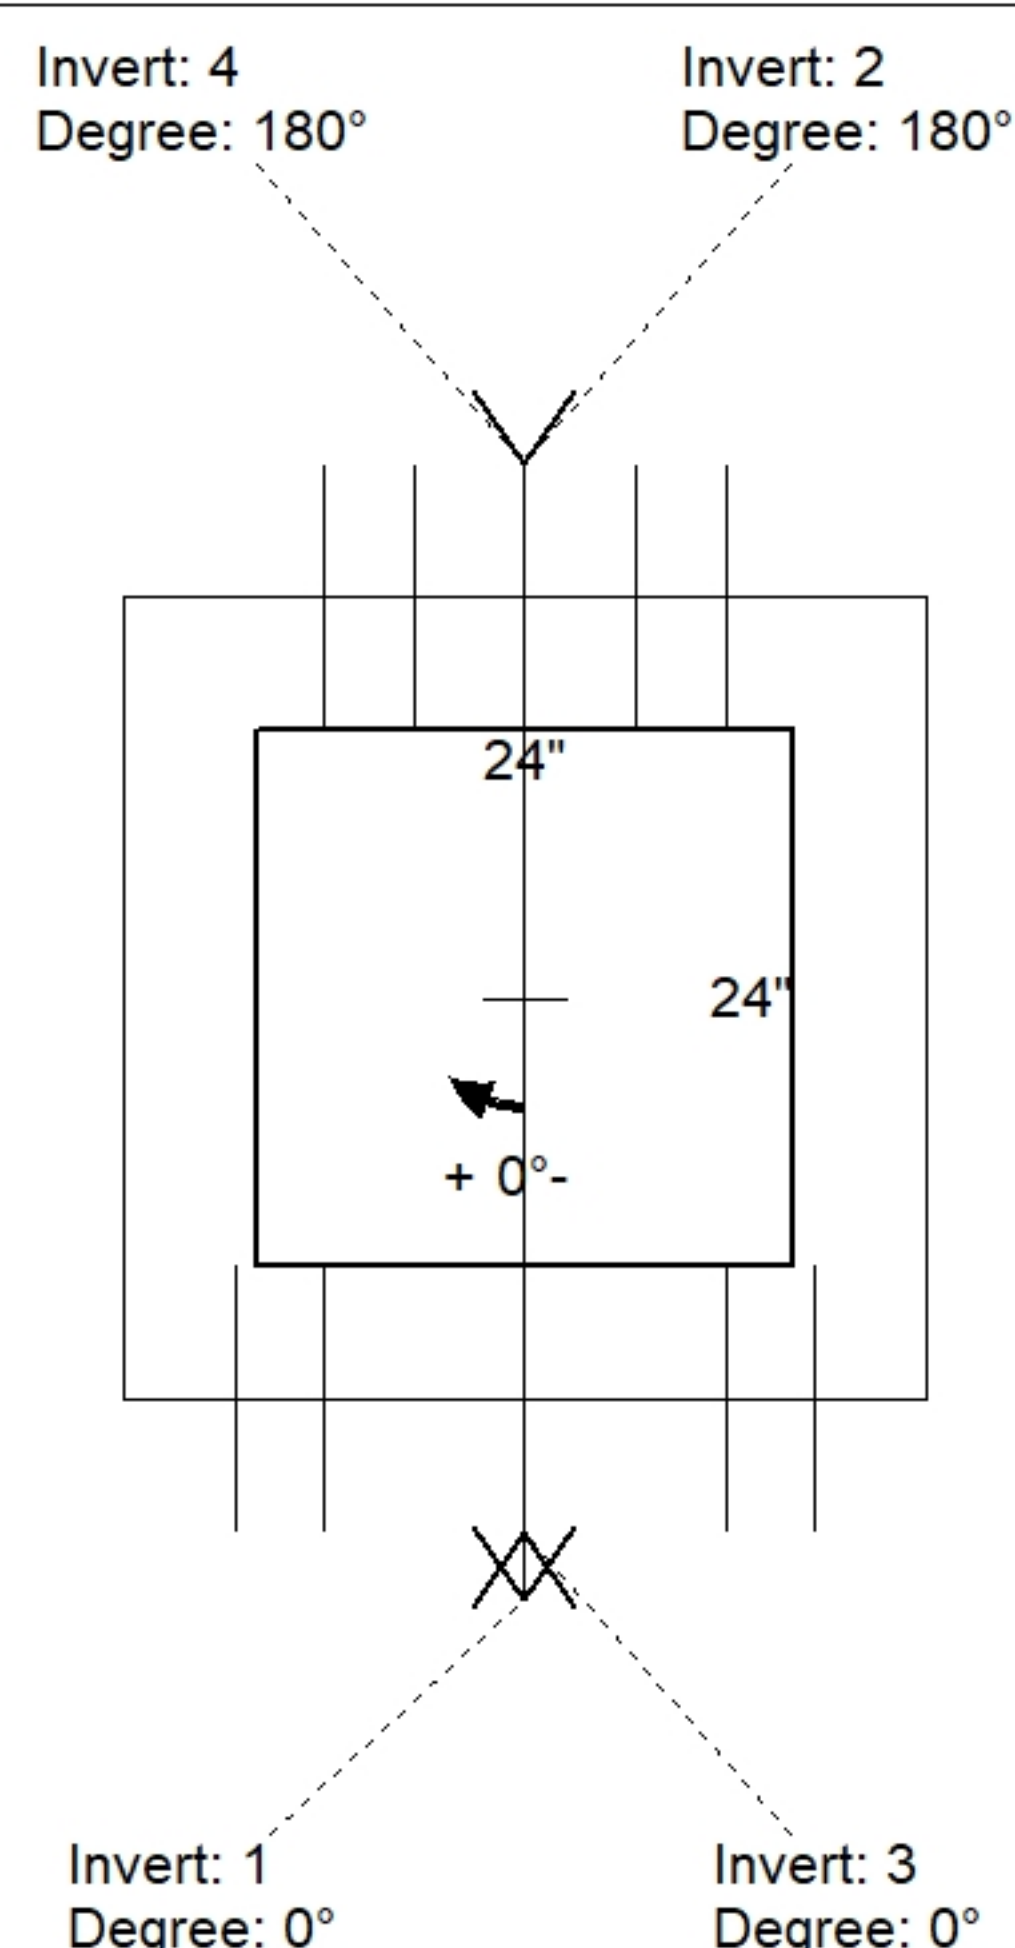

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	335.6'							
Reducer								
Invert 1	332.35'	0°	18" RCP B WALL	23"	26"	Hole 26	-2.5"	P1
Invert 2	332.35'	180°	6" PVC SCH40	6.625"	10"	Hole 10	-0.297"	P1
Invert 3	335.1'	0°	18" x 6" Weir	18" x 6"	18" x 6"	Weir 18"x6"	33"	P1
Invert 4	335.1'	180°	18" x 6" Weir	18" x 6"	18" x 6"	Weir 18"x6"	33"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

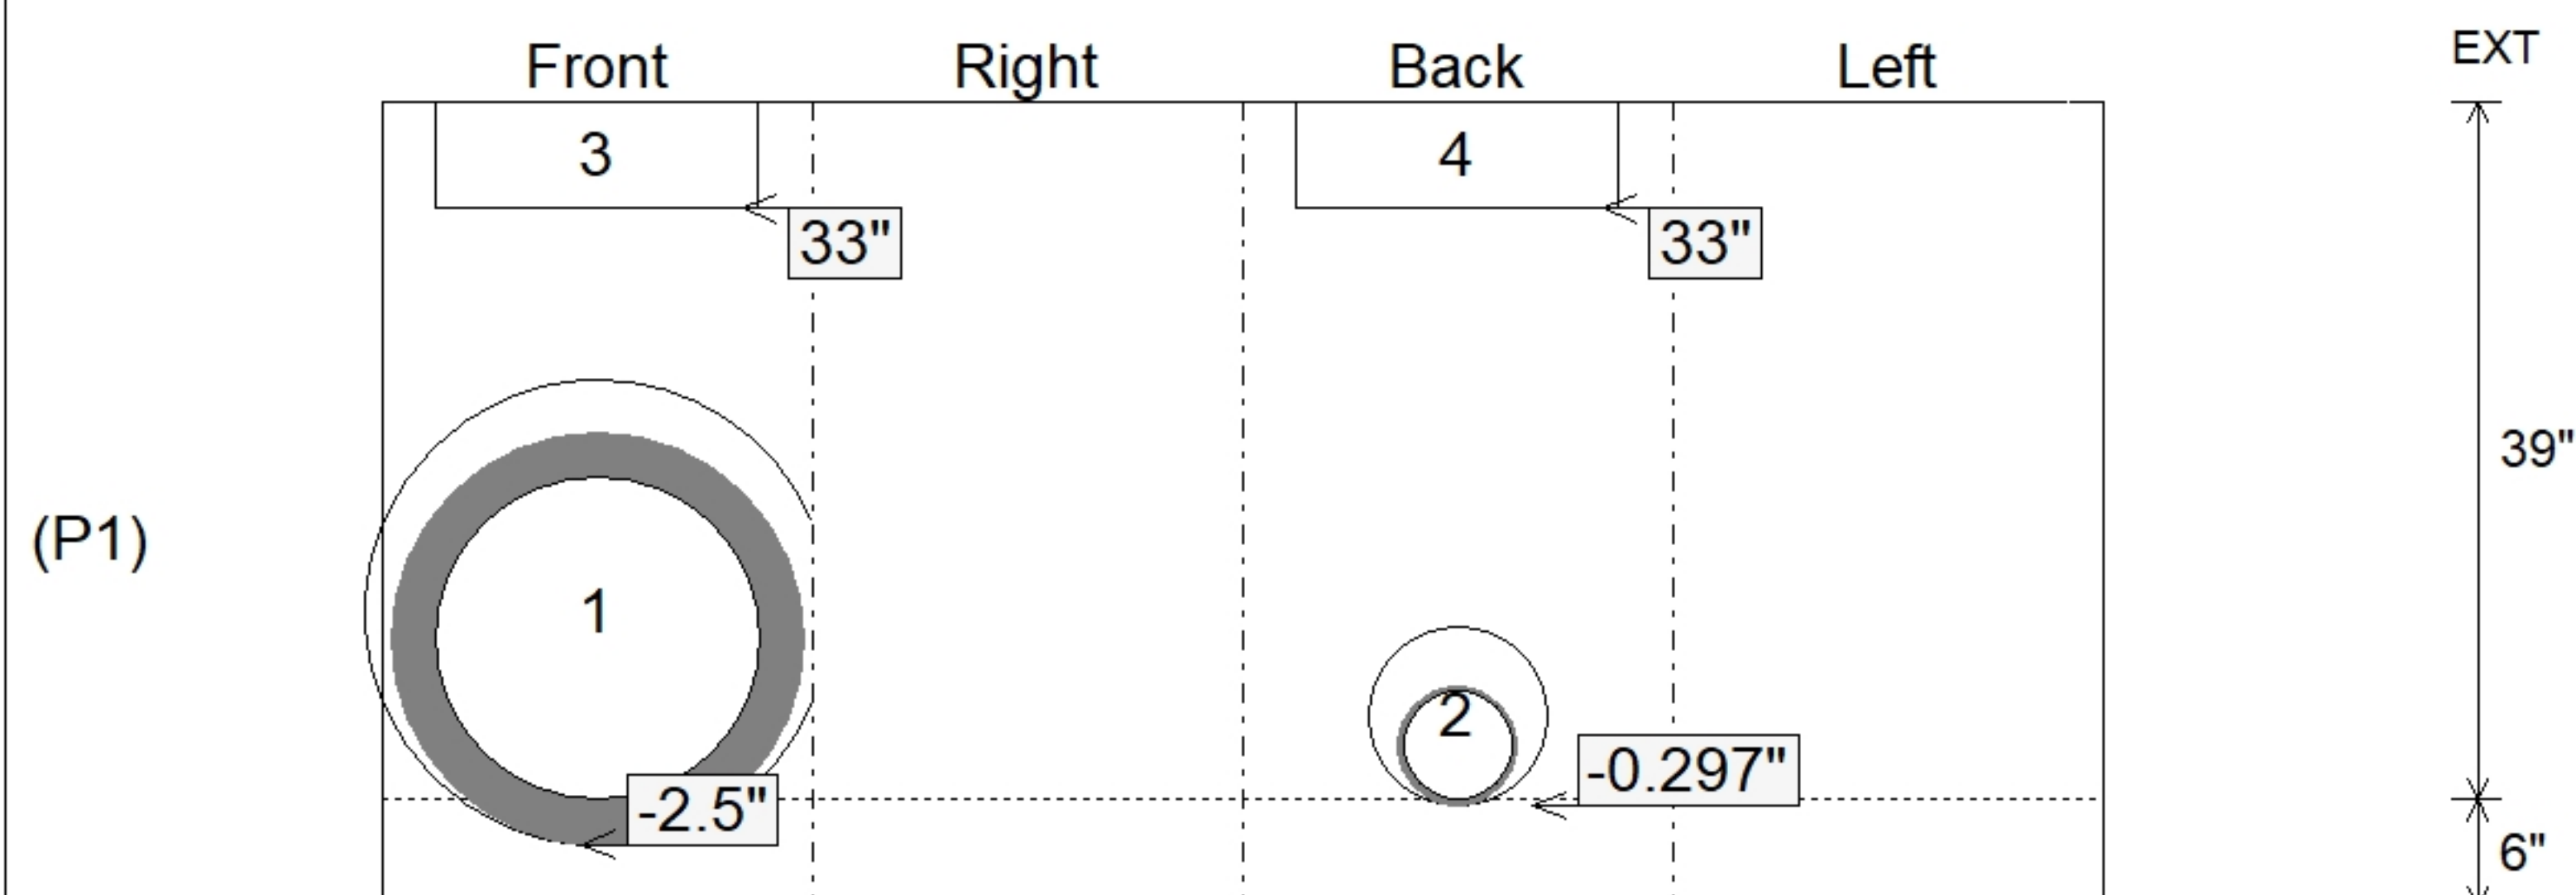

SUBMITTAL
APPROVED BY:
