



Job Name: 25-3664-Hallmark Communities Job Location: Nicholasville, KY Contractor: The Allen Company, Inc.				Plant: 100 9/9/2026 2:13:43 PM		Tech: Jared - A PC: Erica Bradley						
Structure ID: 5A												
P1 MH048BA24CDARED				MH BASE w/ConBlock-CDA Red								
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING w/ConBlock-CDA Red - 4" P2) 48" - MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red - 12" P1) 48" - MH BASE w/ConBlock-CDA Red - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 2) MH Step ML-10-TDS-NCR - 10"						0 lb 270 lb 1580 lb 2911 lb 0 lb 0 lb 1440 lb 258 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 6475 lb		Structure Notes: . 1. HOE MC-315 F/C SANITARY PROVIDED BY OTHERS. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 1009.2' Rim to Invert: 3.75' Slack: 0" Sump: 2" Step Position: 0°												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	1005.45'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"		
Invert 2	1005.55'	250°	126.536"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												


RIGHT-SIDE UP VIEW (int. dimensions)

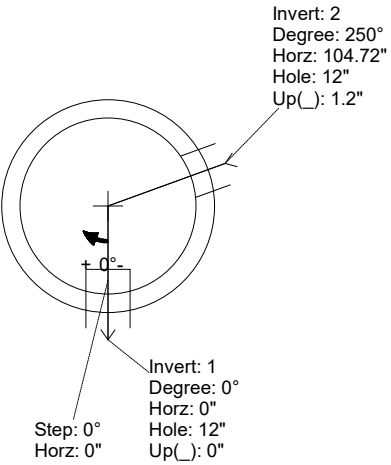

UPSIDE-DOWN VIEW (int. dimensions)

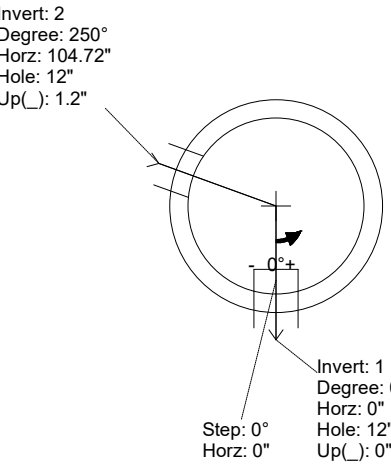


INSIDE WALL DIMENSIONS




Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2911 lb Volume (Net): 0.74cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 25-3664-Hallmark Communities Job Location: Nicholasville, KY Contractor: The Allen Company, Inc.					Plant: 100 9/9/2026 2:13:43 PM		Tech: Jared - A PC: Erica Bradley					
Structure ID: 5A												
P1 MH048BA24CDARED					MH BASE w/ConBlock-CDA Red							
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING w/ConBlock-CDA Red - 4" P2) 48" - MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red - 12" P1) 48" - MH BASE w/ConBlock-CDA Red - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 2) MH Step ML-10-TDS-NCR - 10"					0 lb 270 lb 1580 lb 2911 lb 0 lb 0 lb 1440 lb 258 lb 0 lb 0 lb 16 lb 0 lb ----- 6475 lb		Structure Notes: . 1. HOE MC-315 F/C SANITARY PROVIDED BY OTHERS. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 1009.2' Rim to Invert: 3.75' Slack: 0" Sump: 2" Step Position: 0"					INVERT CHANNEL DRAWING FULL HEIGHT INVERT							
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	1005.45'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"		
Invert 2	1005.55'	250°	126.536"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												


RIGHT-SIDE UP VIEW (int. dimensions)

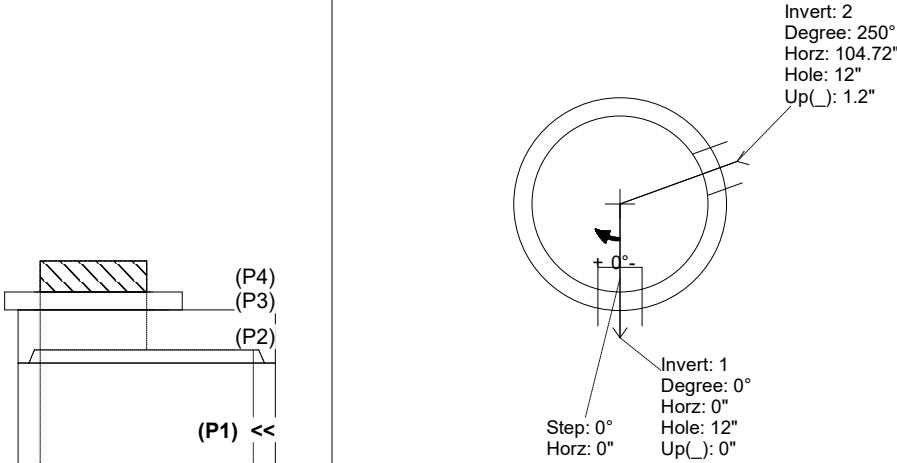

UPSIDE-DOWN VIEW (int. dimensions)

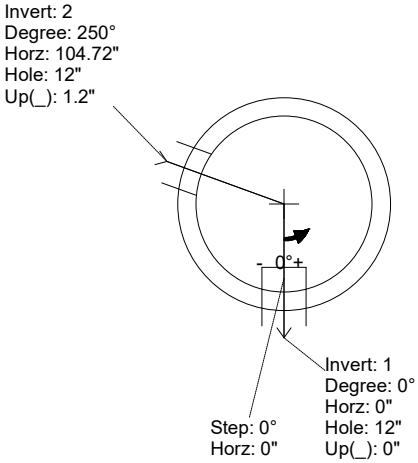

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2911 lb Volume (Net): 0.74cu.yd
----------------------------------	---------------------------------	--	--	--
