

Contractor: The Allen Company, Inc.

Plant: 100



Type: SAN.MH w/ConBlock-CDA Red
Size: 48"

Rim to Invert: 5'

Floor Height: 6"


Slack: 1"

1. HOE MC-315 F/C SANITARY PROVIDED BY OTHERS.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
 - CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 6782 lb

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	1011.75'							
Reducer								
Invert 1	1006.75'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	1006.85'	203°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

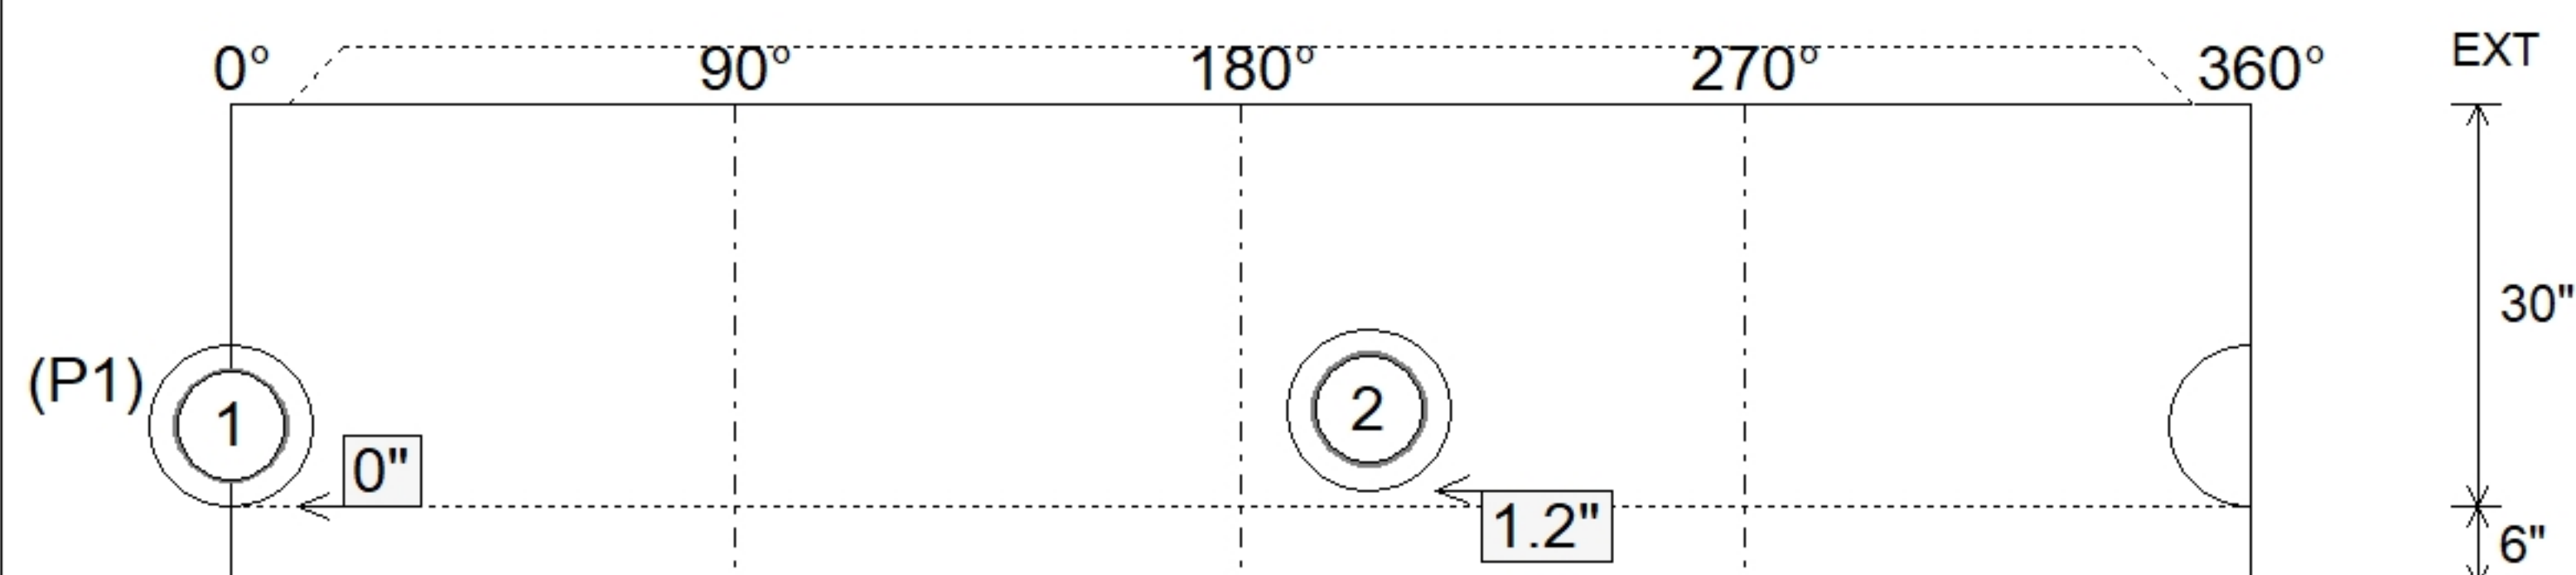

Submittal Drawing
9/11/2026 8:09:20 AM

SUBMITTAL
APPROVED BY:

