


Job Name: 25-3664-Hallmark Communities
Job Location: Nicholasville, KY
Contractor: The Allen Company, Inc.

Plant: 100
9/9/2026 2:28:05 PM

Tech: Jared - A
PC: Erica Bradley



Structure ID: CI6

P2 BX3648-08R-VH

BOX RISER 8inW, Variable Ht

- P4) 24" x 24" - CASTING HEIGHT - 5"
P3) 36" x 48" - CB FT REDUCER 24"X24" HOLE - 8"
P2) 36" x 48" - BOX RISER 8inW, Variable Ht - 32"
P1) 36" x 48" - BOX BASE 8inW, 8inF - 60"
1) CASTING - HOE KY-465 SET (CBI TY F)
2) 36" x 48" - Conseal CS-102 1.00"
1) 24" x 24" - Conseal CS-102 1.00"
2) Hole - 38
1) Hole - 12



- Structure Notes: .
1. HOE KY-465 SET (CBI TY F) PROVIDED BY OTHERS.
2. KYTC CBI TYPE F / ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. NO STEPS.
6. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W
- RISER/WALLS (As .18)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 15300 lb


Rim: 1004.4' Rim to Invert: 8.75' Slack: 0" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

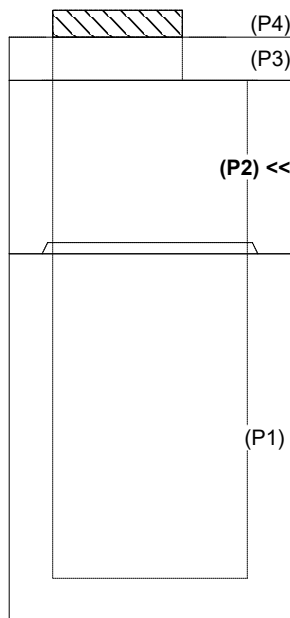

INSIDE WALL DIMENSIONS



Coating (Int): Seam Up: Flat Wall Thickness: 8" Height (Int): 32" Weight (Net): 4296 lb
Coating (Ext): Seam Dn: Groove Floor Height: 0" Height (Ext): 32" Volume (Net): 1.1cu.yd
