

Contractor: Citgo Waterworks

TECH: J. Horsley - F

Plant: 100



Size: 60"


Rim to Invert: 7.39'

Floor Height: 8"


Slack: 0.934"

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS.
4. CASTING SUPPLIED BY OTHERS.
5. CARBOLINE 300M >>EXTERIOR COATING ONLY<<
REINFORCING PER ASTM A615 (GRADE 60).
 - CONE (As .12)
 - RISER/WALLS (As .12)
 - TRANSITION SLAB (As .31) #5 BARS AT 6" C.C.E.W.
 - RISER/WALLS (As .18)
 - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.


P4)	24" - CASTING HEIGHT - 4.75"	0 lb
P3)	48" - ECC CONE w/ 24" HOLE NO STEP - 24"	1550 lb
P2)	60" - MH Transition Slab 48" Hole - 13"	1928 lb
P1)	60" - MH BASE Custom Ht - 48"	7413 lb
1)	JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1)	JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1)	60" - MH INVERT CHANNEL - FULL HEIGHT	2692 lb
1)	SPECIAL EXTERNAL COATING - CARBOLINE 300M	0 lb
1)	60" - Conseal CS-102 1.00" (Double)	0 lb
1)	48" - Conseal CS-102 1.00" (Double)	0 lb
1)	24" - Conseal CS-102 1.00" (Double)	0 lb
1)	Kor-N-Seal2 - S206-22	6 lb
1)	PSX - 12-06 NYLO	8 lb
1)	PSX - 14M DD	8 lb
	163.59 SqFt) Carboline Bitumastic 300M [EXT]	0 lb
	Structure Total:	13605 lb

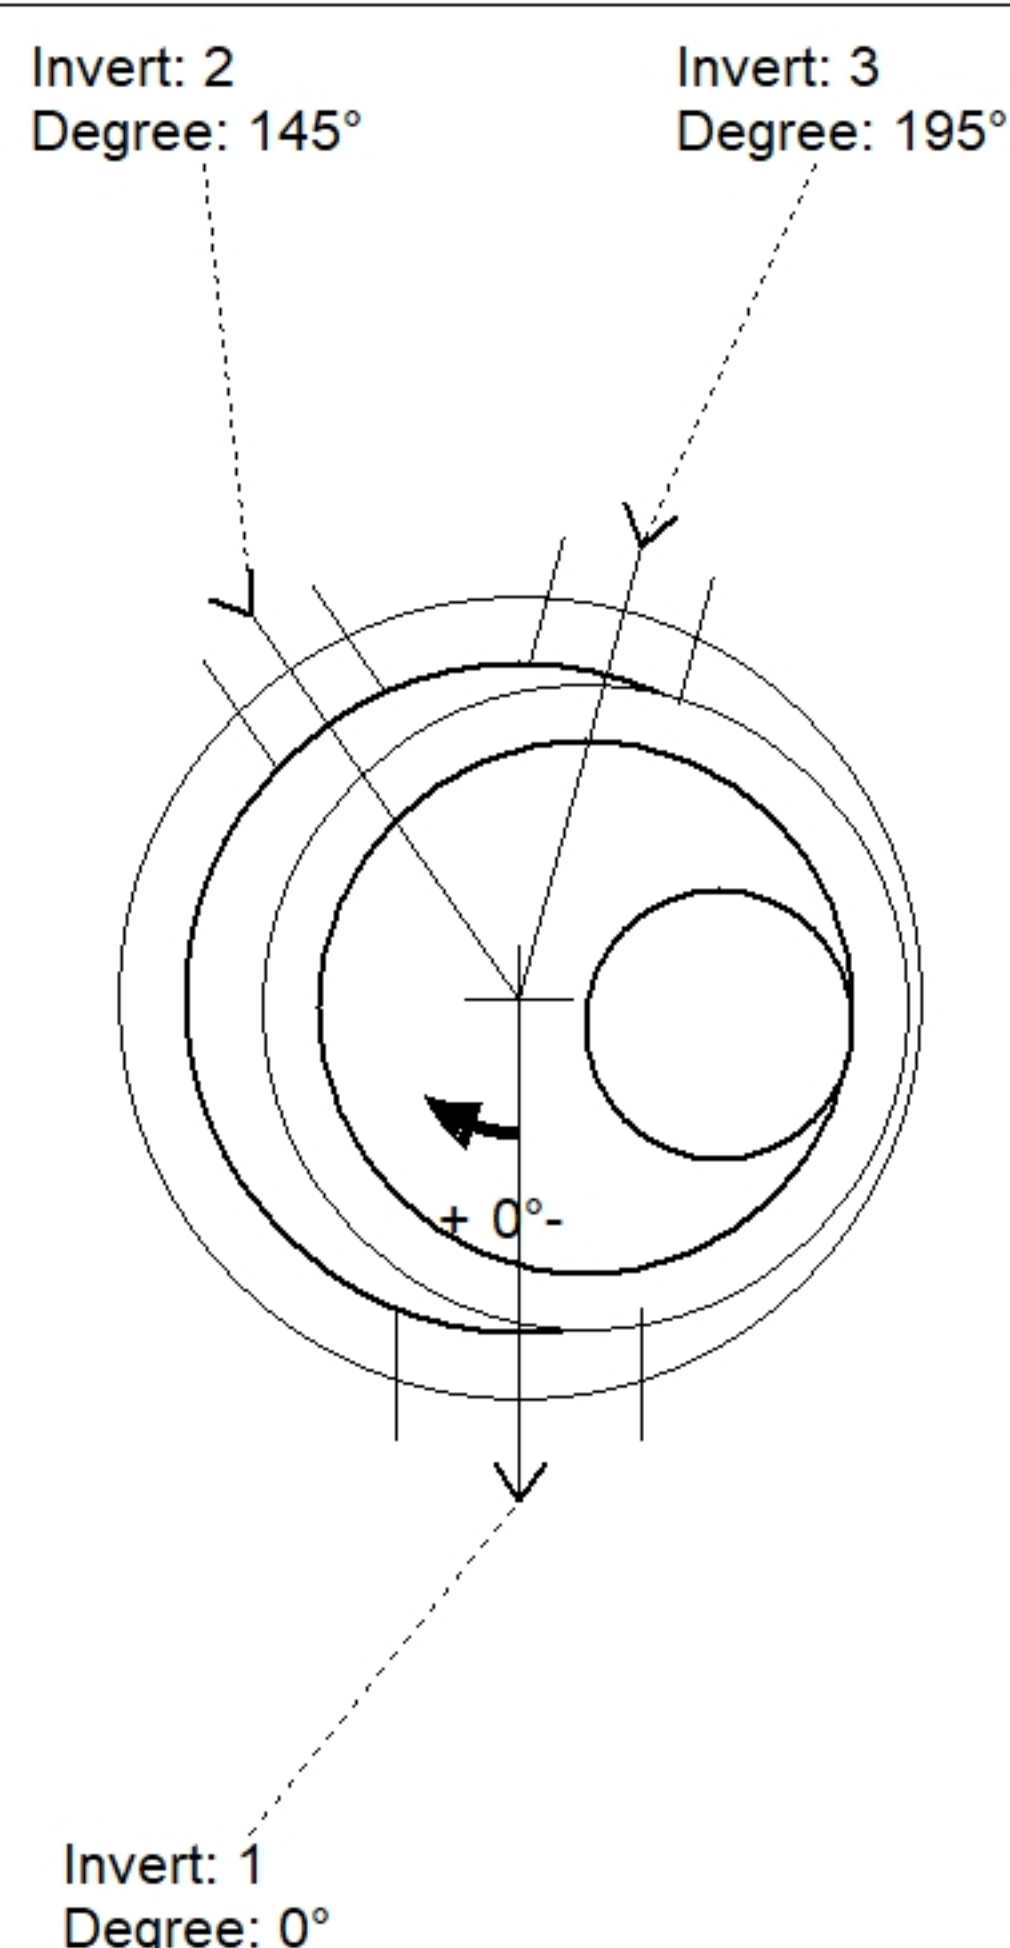

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	696.33'							
Reducer	692.773'							
Invert 1	688.94'	0°	18" PVC SDR35	18.75"	22"	Kor-N-Seal2 S206-22	0.004"	P1
Invert 2	689.04'	145°	6" DI	6.875"	12"	PSX 12-06 NYLO	0.204"	P1
Invert 3	689.04'	195°	10" DI	11.1"	14"	PSX 14M DD	1.204"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

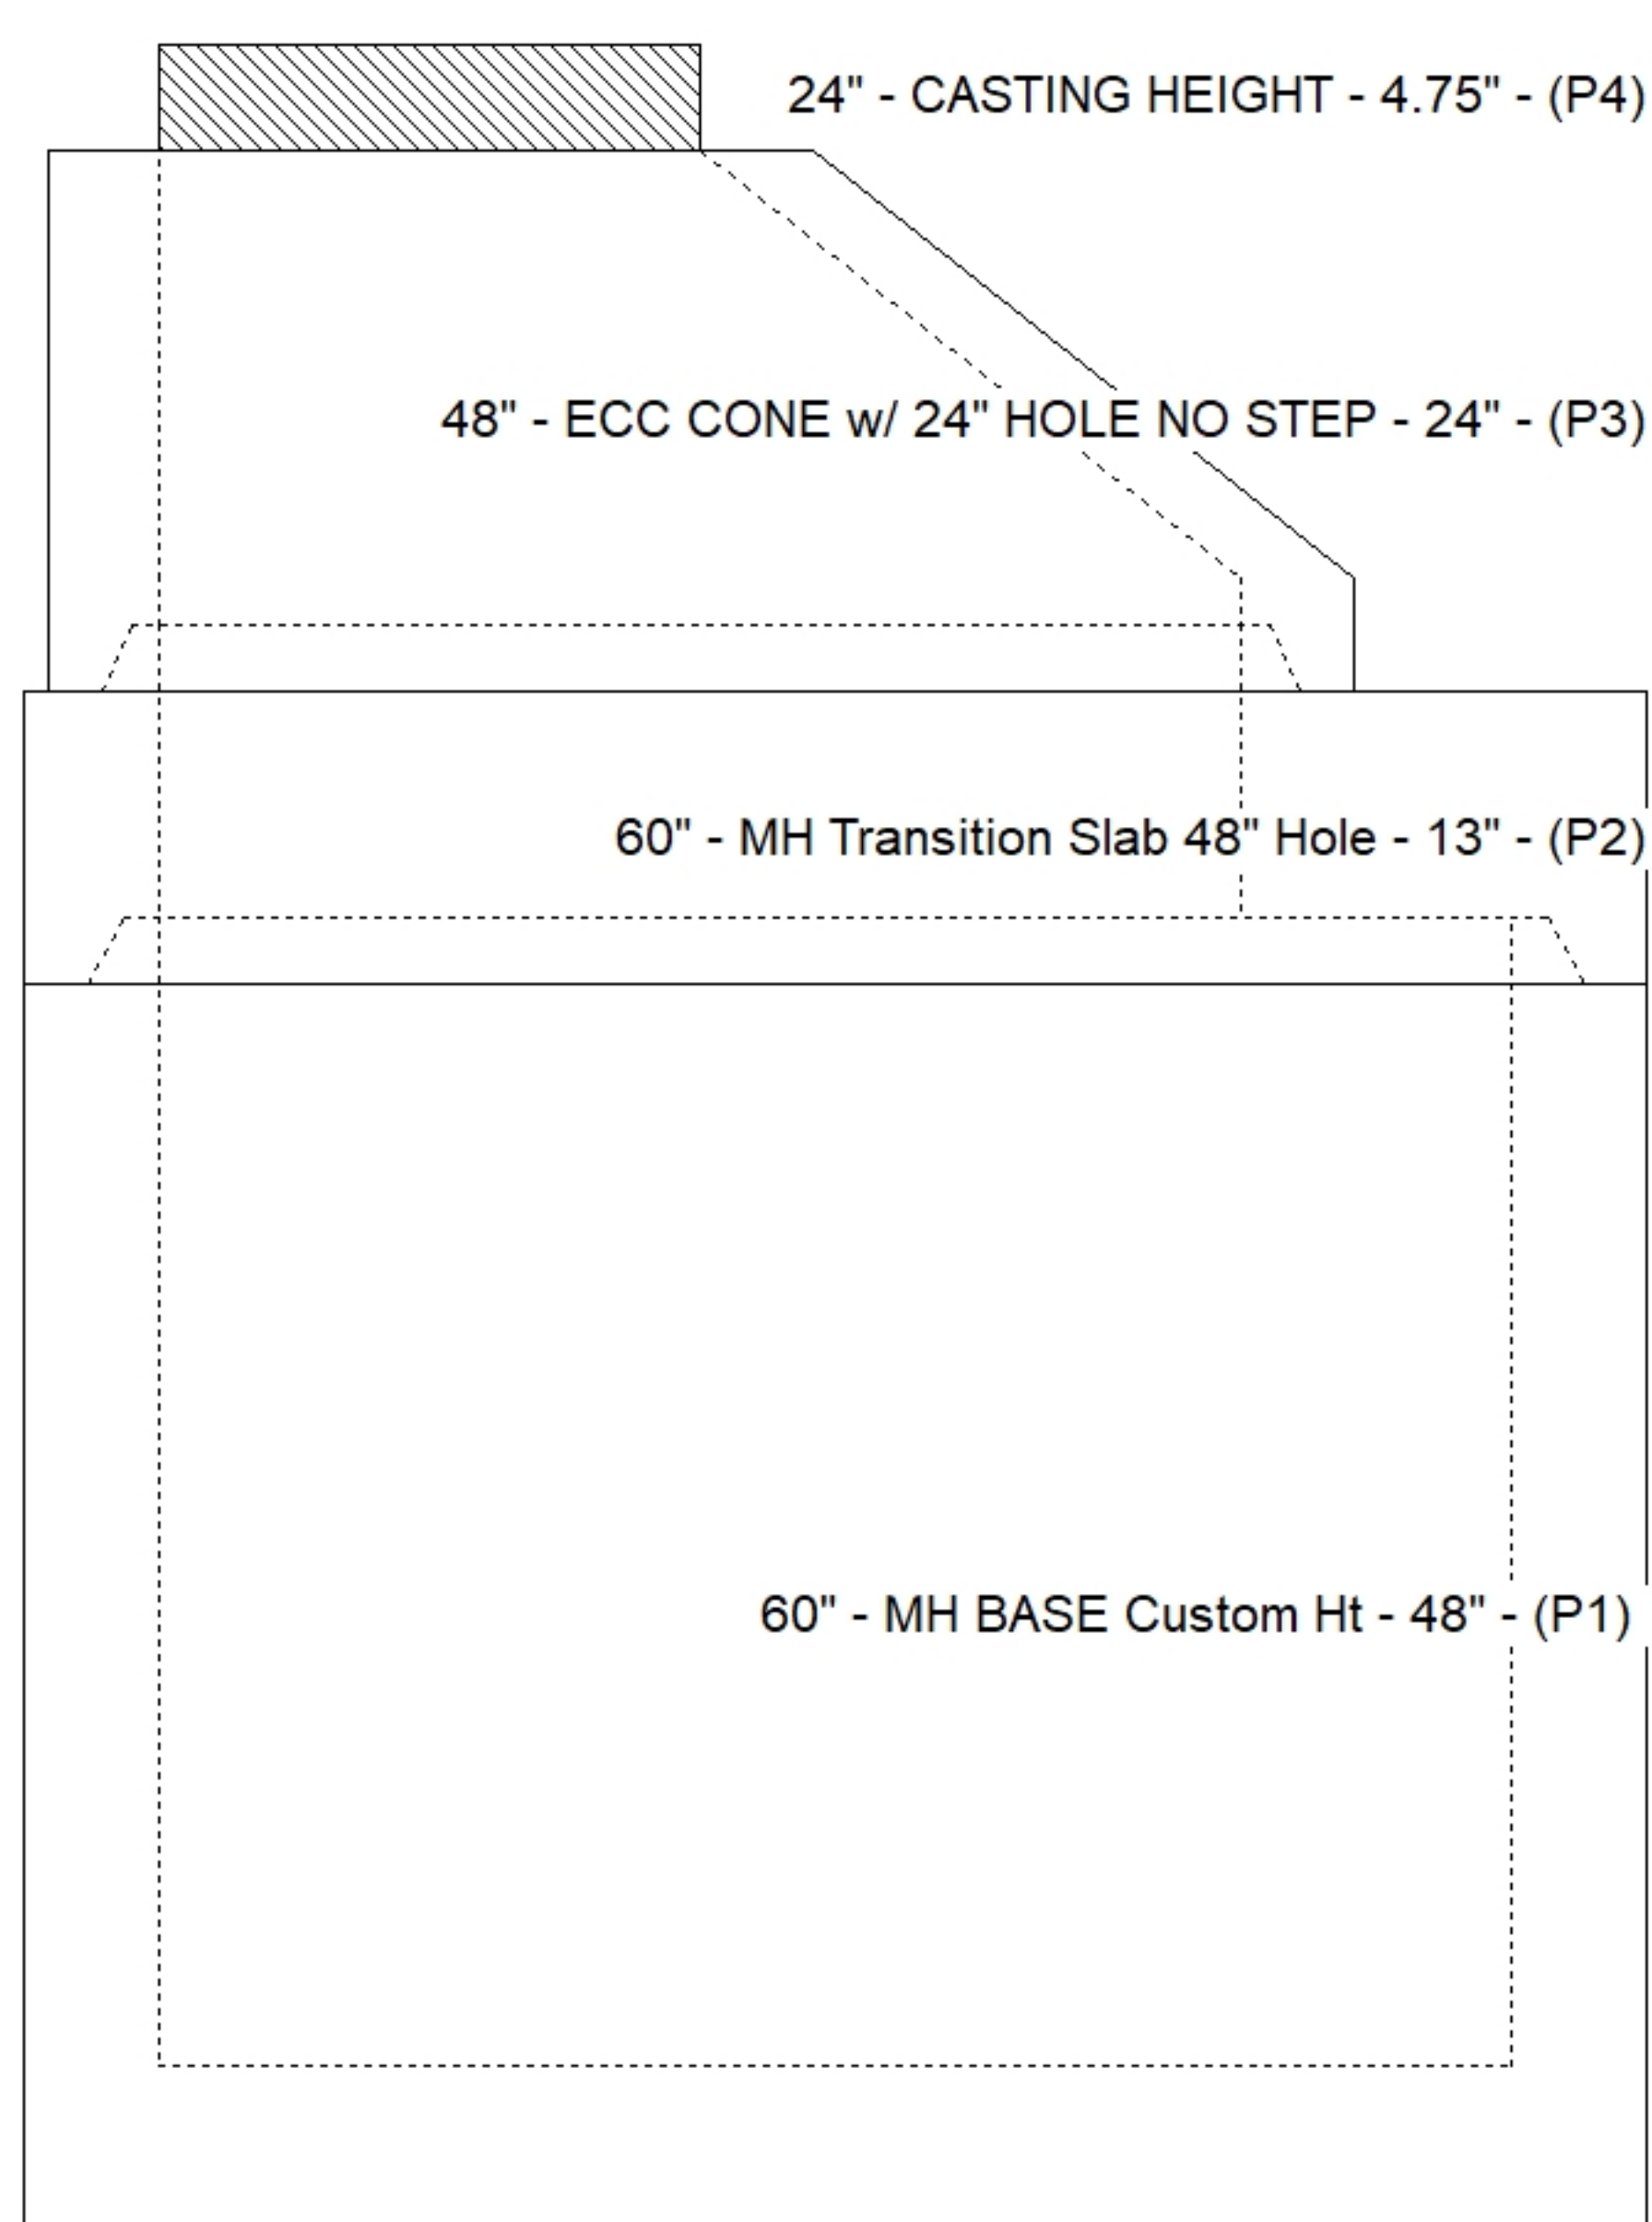

Default - Interior Dimensions

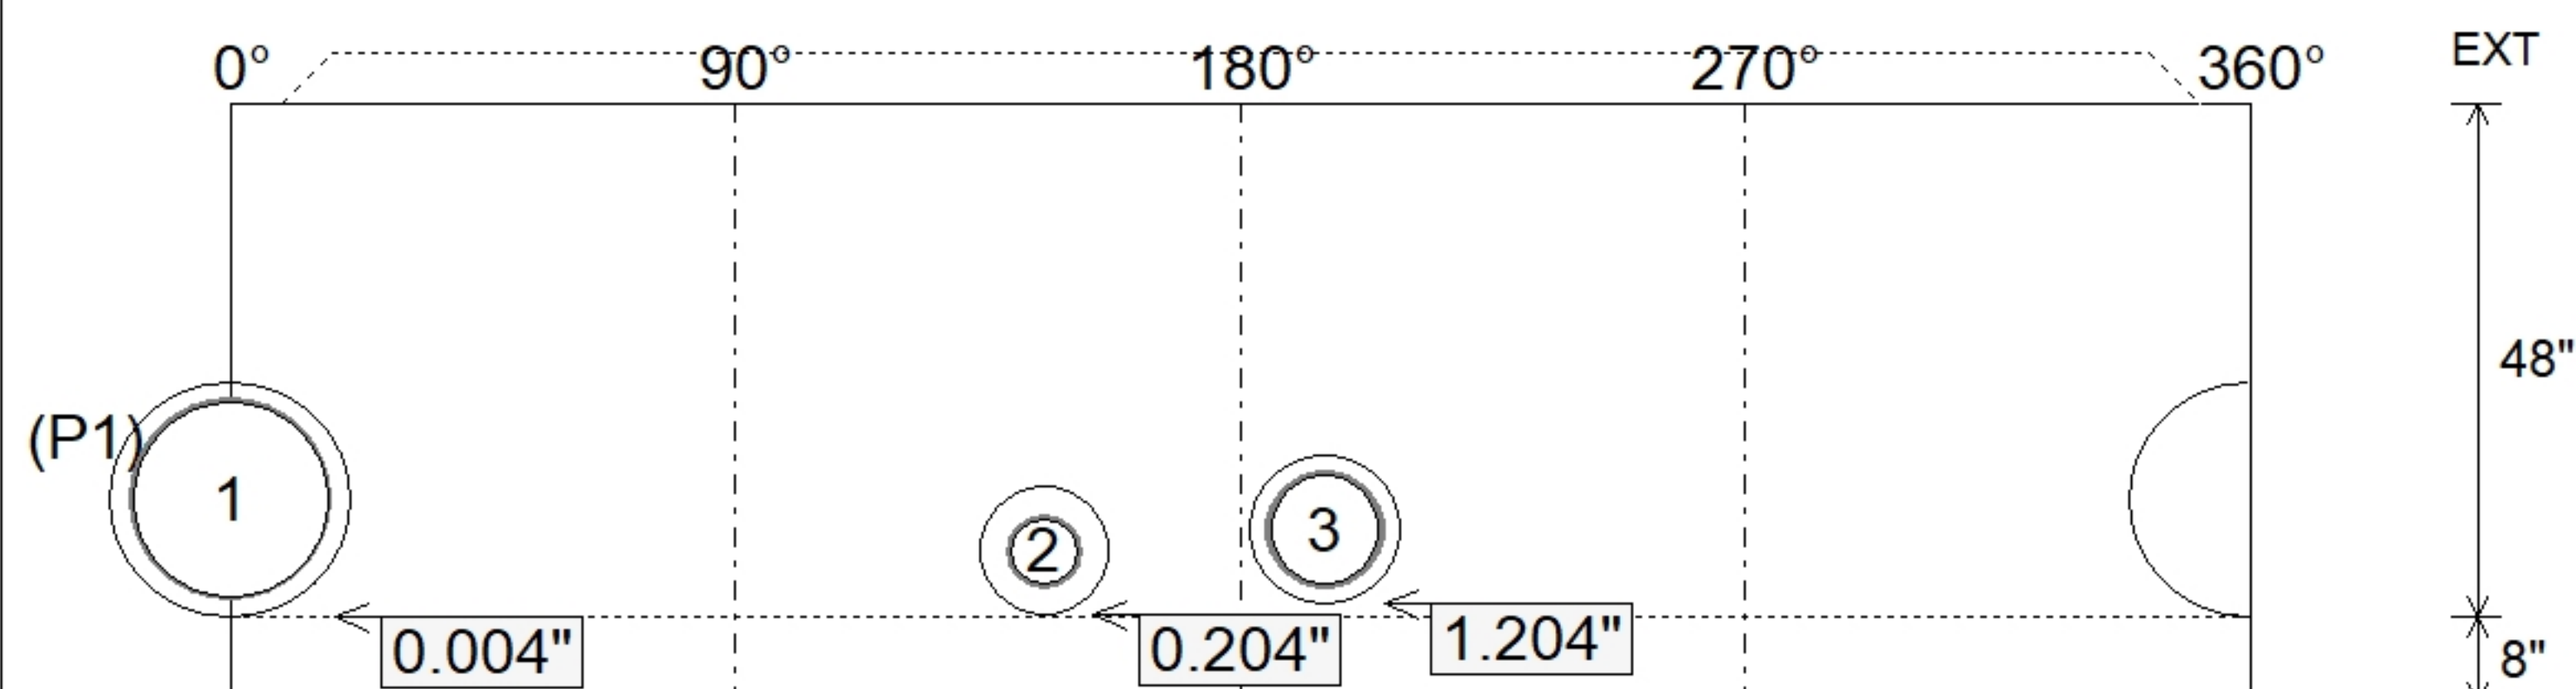

Submittal Drawing
7/2/2026 12:02:27 PM

SUBMITTAL
APPROVED BY:
