

Job Name: 25-4272 Chestnut Street Utility Rehab  
 Job Location: Evansville, IN  
 Contractor: Bowen Engineering Corporation

Plant: Beaver Dam

Tech: J. Coppage

10/23/2025 3:08:18 PM

PC: A. Chambers



**Structure ID: 102**

**P3 MH060RS36**

**MH RISER**

- P5) 24" x 48" - CASTING HEIGHT - 8"
- P4) 60" - MH FLAT TOP w/24"x48" Hole - 13"
- P3) 60" - MH RISER - 36"
- P2) 60" - MH RISER - 60"
- P1) 60" - MH BASE Custom Ht - 55"
- 1) CASTING - HOE R-3287-5 SET (F/G/H)
- 3) 60" - Conseal CS-102 1.00"
- 1) 24" x 48" - Conseal CS-102 1.00"
- 2) Hole - 40
- 12) MH Step ML-10-TDS-NCR - 10"

0 lb  
 2272 lb  
 3758 lb  
 6264 lb  
 7111 lb  
 442 lb  
 0 lb  
 0 lb  
 0 lb  
 0 lb  
 -----  
 Structure Total: 19847 lb



Structure Notes:

1. JR HOE R-3287-5 PROVIDED BY ICAST.
2. PER ASTM C913 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).  
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..  
 - RISER/WALLS (As .18)  
 - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.


Rim: 378.98' Rim to Invert: 14.3' Slack: 3.1" Sump: 3.5" Step Position: 104°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (L)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

**RIGHT-SIDE UP VIEW (int. dimensions)**

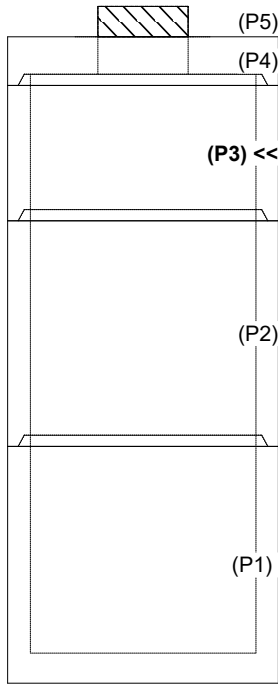

**INSIDE WALL DIMENSIONS**



Coating (Int):  
 Coating (Ext):

Seam Up: Tongue  
 Seam Dn: Groove

Wall Thickness: 6"  
 Floor Height: 0"

Height (Int): 36"  
 Height (Ext): 36"

Weight (Net): 3758 lb  
 Volume (Net): 0.96cu.yd
