

Contractor: CITCO Water


Plant: 100



Slack: 0"

P3) 36" x 36" - HATCH (CAST FLUSH) - 0"	100 lb
P2) 72" x 192" - CB FLAT TOP 8"W w/2 HATCHES w/ConBlock-CDA Red - 8"	10813 lb
P1) 72" x 192" - BOX BASE 8inW, 8inF, Variable Ht w/ConBlock-CDA Red - 72"	39249 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) ADMIXTURE CONBLOCK CDA RED	0 lb
1) SECONDARY POUR - WALLS	0 lb
1) 36" x 36" - SGL 1"x14.5' Butyl (2x)	0 lb
2) Hole - 10	0 lb

Structure Total:	50162 lb

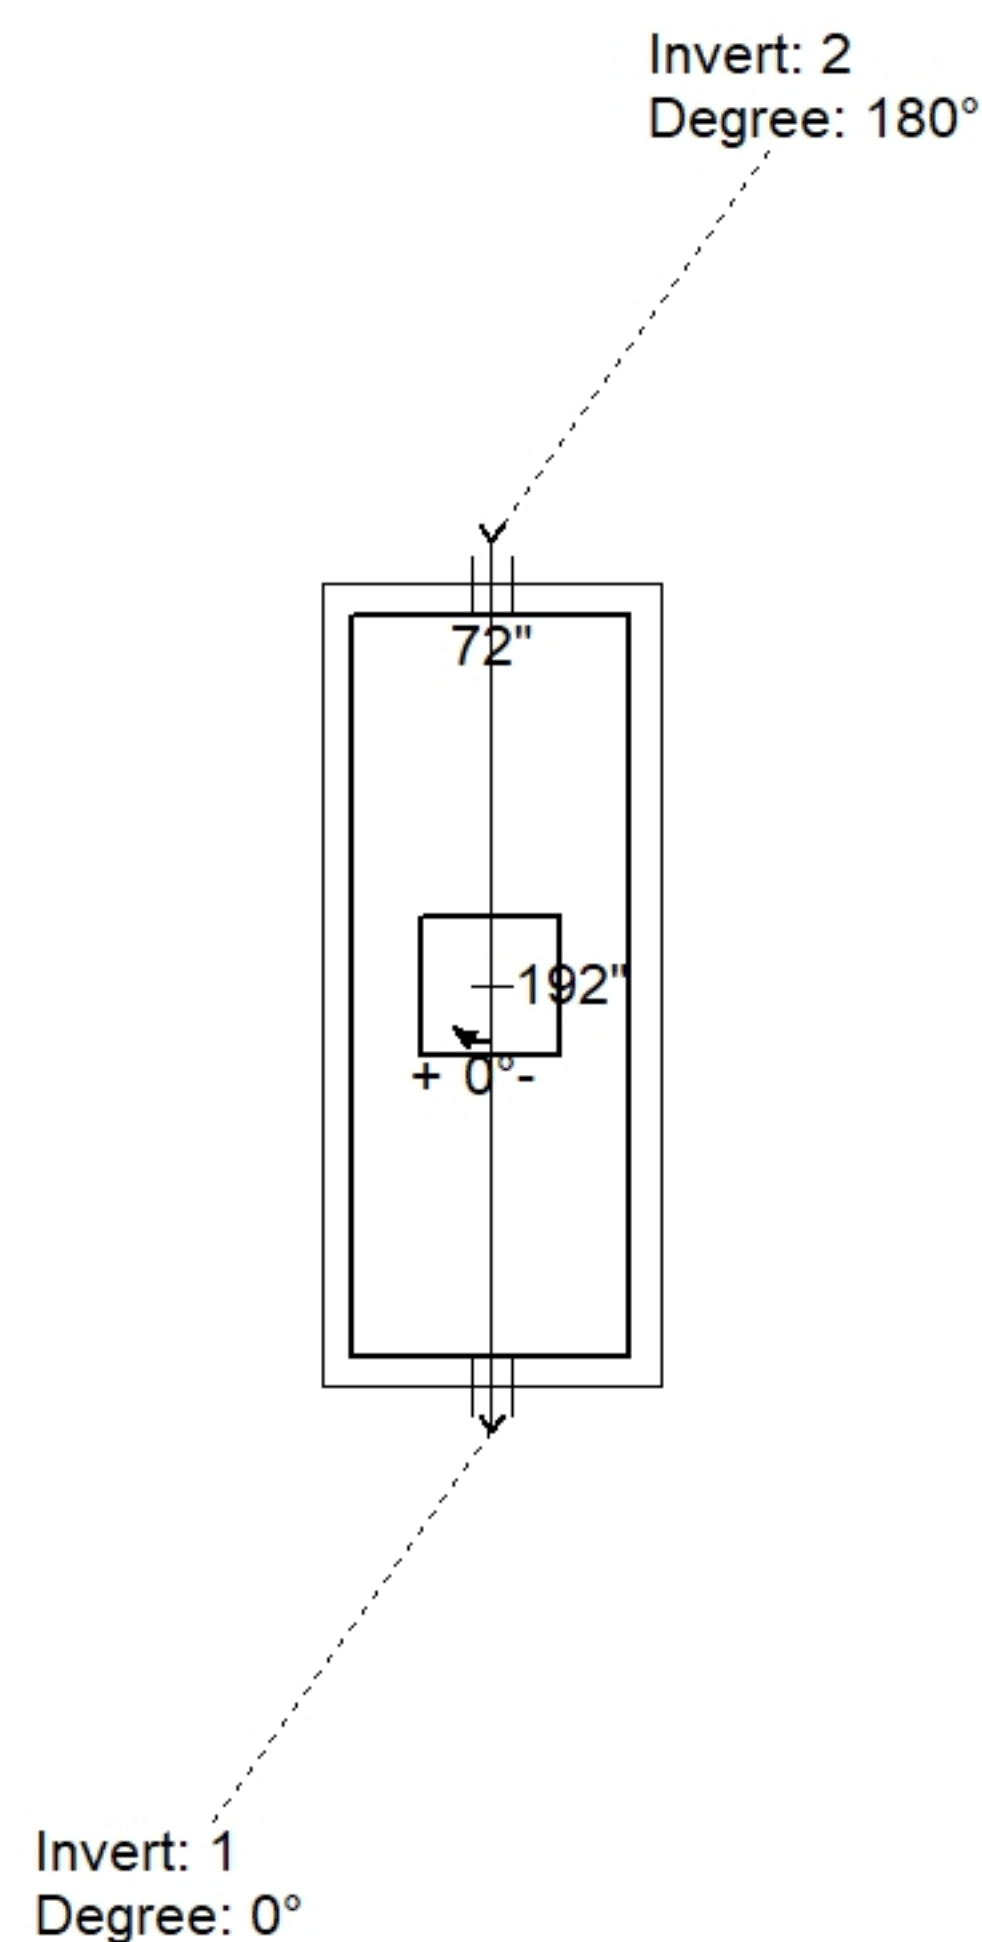


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	6.667'							
Reducer								
Invert 1	1.25'	0°	6" DI	6.875"	10"	Hole 10	13"	P1
Invert 2	1.25'	180°	6" DI	6.875"	10"	Hole 10	13"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

36" x 36" - HATCH (CAST FLUSH) - 0" - (P3)

72" x 192" - CB FLAT TOP 8"W w/2 HATCHES w/ConBlock-CDA Red - 8" - (P2)

72" x 192" - BOX BASE 8inW, 8inF, Variable Ht w/ConBlock-CDA Red - 72" - (P1)

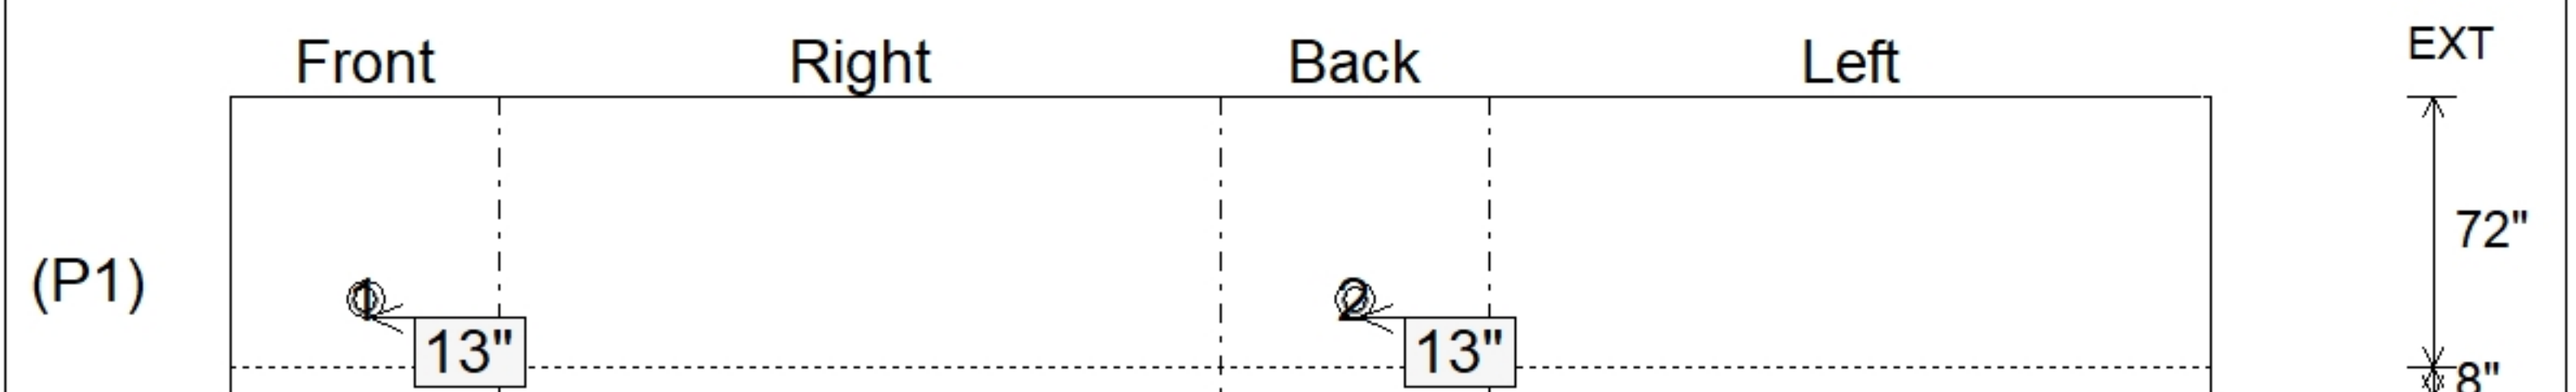

SUBMITTAL
APPROVED BY:
