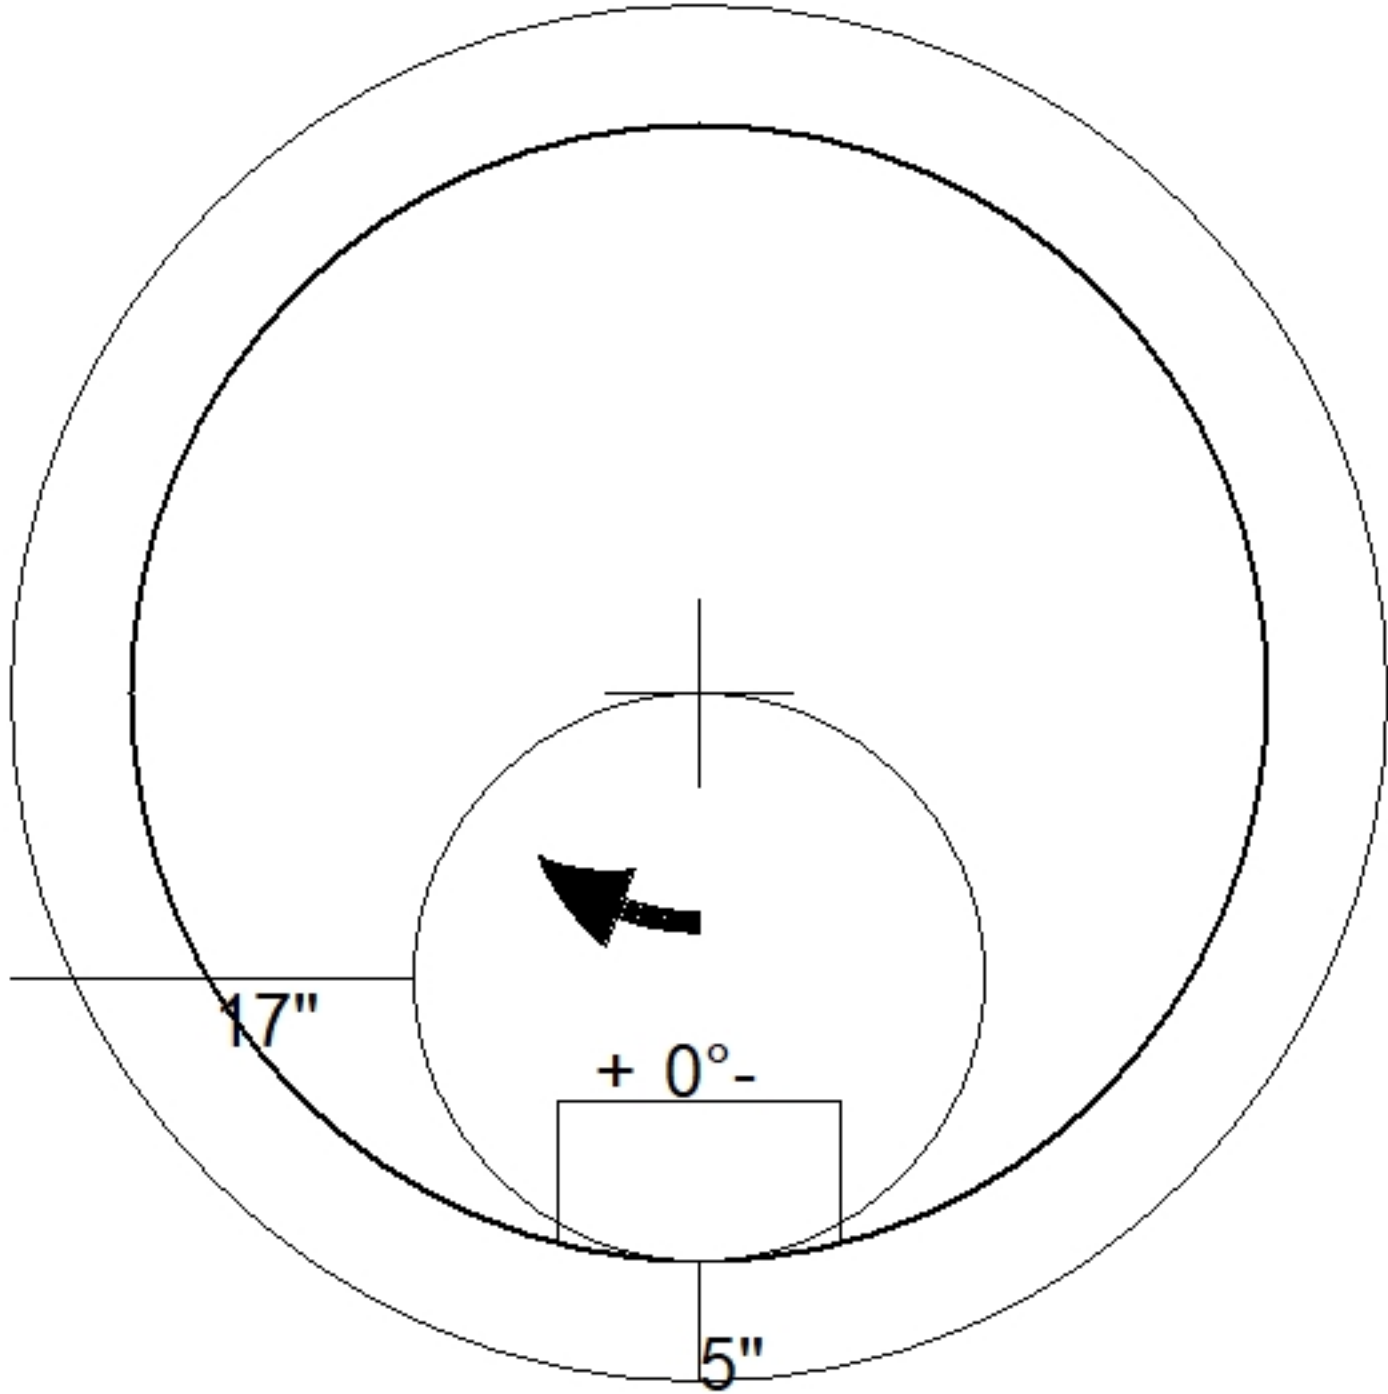
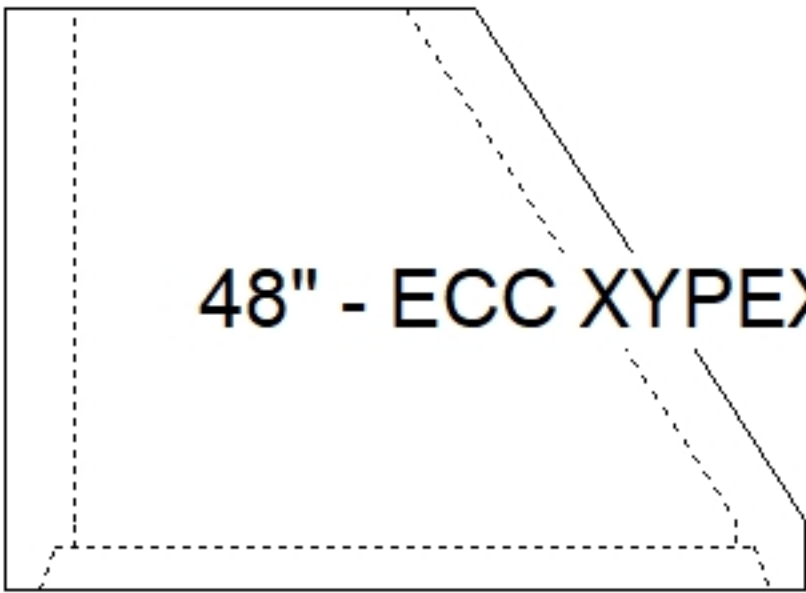


Job Name: 25-4288 - Project Wave Job Location: Franklin, KY 42134 Contractor: Cumberland Pipeline LLC		Plant: 100 9/2/2026 8:40:48 AM	Tech: PC: Erica Bradley	
Structure ID: A10				
P4 MH048CN42X		ECC XYPEX CONE w/ 24" HOLE F/G		
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC XYPEX CONE w/ 24" HOLE F/G - 42" P3) 48" - MH RISER w/DROP/XYPEX T/G - 72" P2) 48" - MH RISER w/DROP/XYPEX T/G - 72" P1) 48" - MH BASE w/DROP/XYPEX T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - JBS 1150 F/C SANITARY 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 1) Drop Tee - 6" PVC 1) Drop Elbow - 6" PVC 18) MH Step ML-10-TDS-NCR - 10"		0 lb 3116 lb 5016 lb 5030 lb 3316 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 16 lb 0 lb 0 lb 0 lb ----- 18184 lb	Structure Notes: 1. JBS-1150 F/C SANITARY PROVIDED BY ICAST . 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. EXTERIOR DROP @ 90 DEGREES. . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
 48" - ECC XYPEX CONE w/ 24" HOLE F/G - 42" - (P4)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 42"	Weight (Net): 3116 lb Volume (Net): 0.8cu.yd
