



Floor (Bot): 717.38'
Overall Height: 15.583'
Slack: 0.44"

P5) 24" - CASTING HEIGHT - 7"	0 lb
P4) 48" - ECC XYPEX CONE w/ 24" HOLE - 30"	1981 lb
P3) 48" - MH RISER w/XYPEX - 60"	4192 lb
P2) 48" - MH RISER w/XYPEX - 60"	4192 lb
P1) 48" - MH BASE w/XYPEX - 24"	2911 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT	1440 lb
1) CASTING - JBS 1150 F/C SANITARY	250 lb
3) 48" - Conseal CS-102 1.00" (Double)	0 lb
1) 24" - Conseal CS-102 1.00" (Double)	0 lb
2) PSX - 12-06 NYLO	16 lb
15) MH Step ML-10-TDS-NCR - 10"	0 lb


Structure Total:	14981 lb

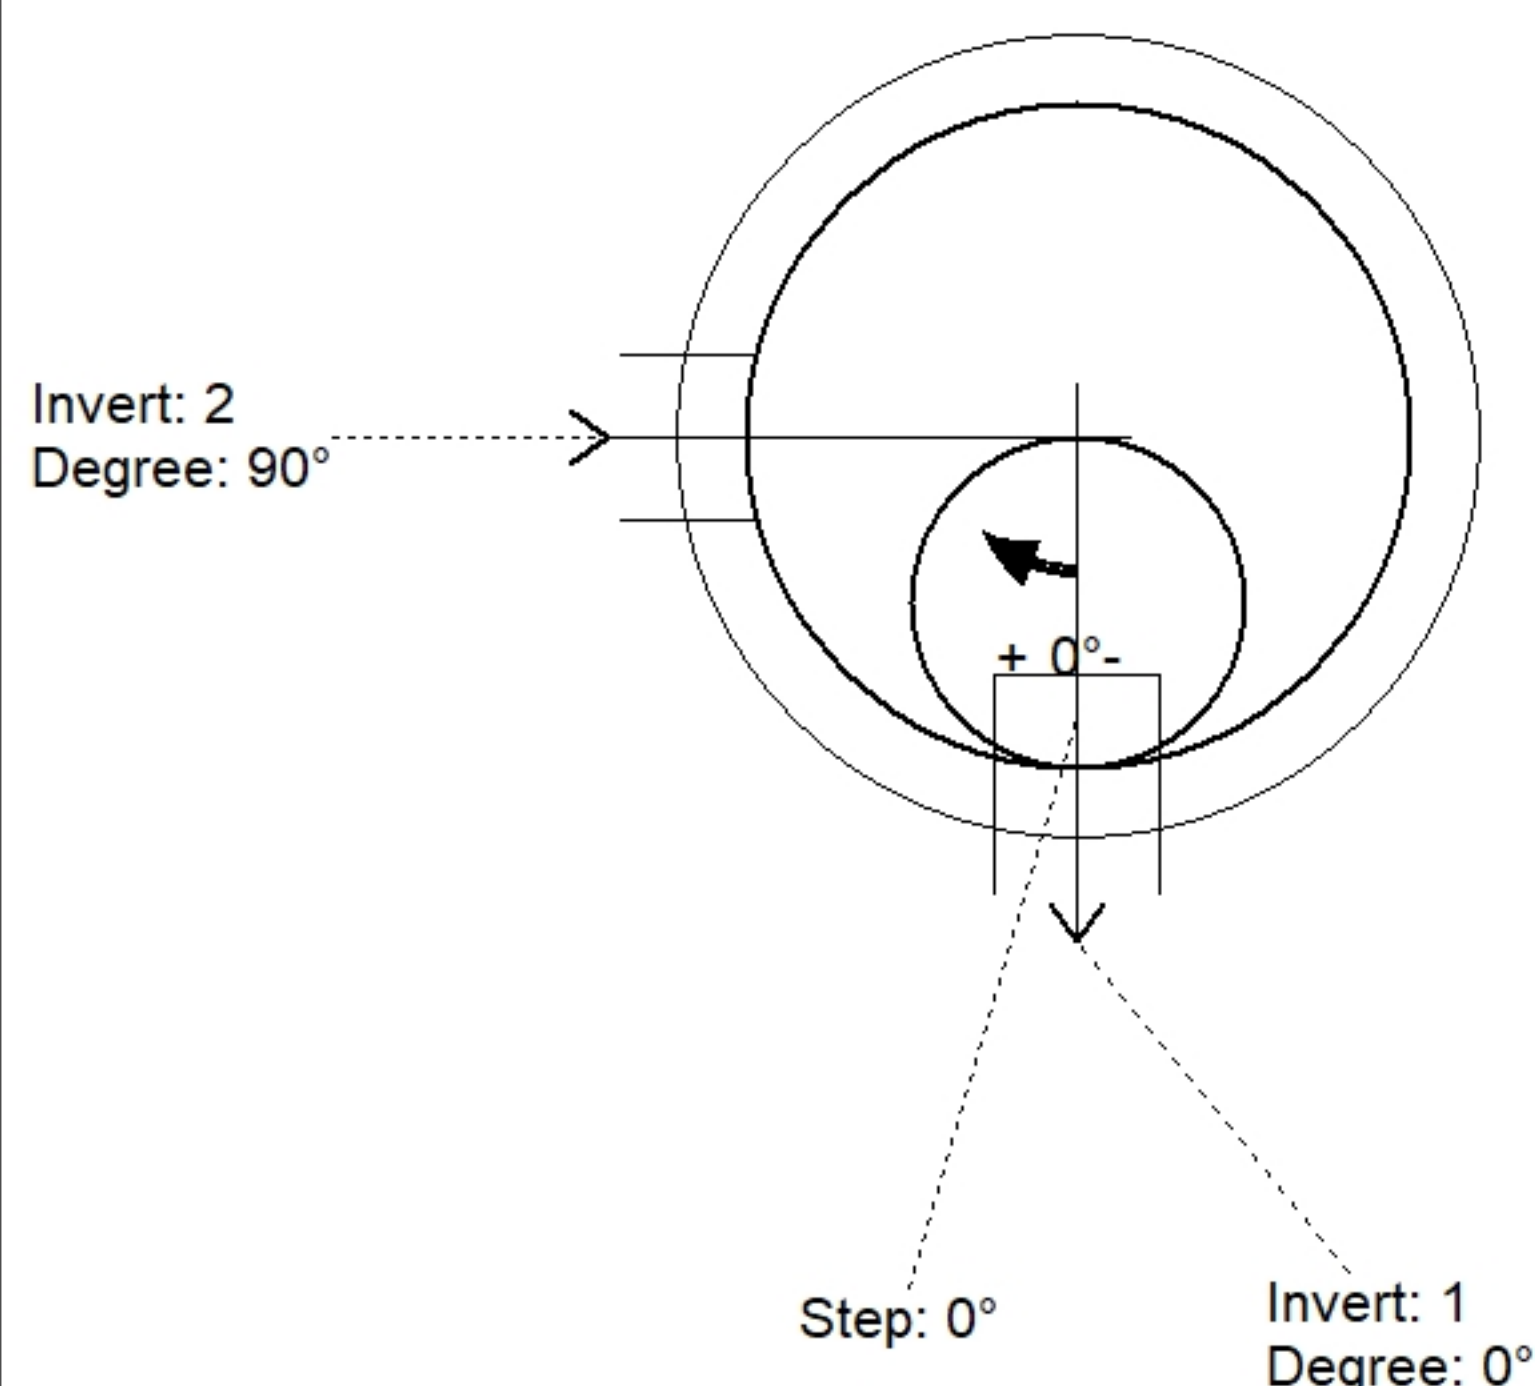

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	733'							
Reducer								
Invert 1	718.13'	0°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	0"	P1
Invert 2	718.23'	90°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

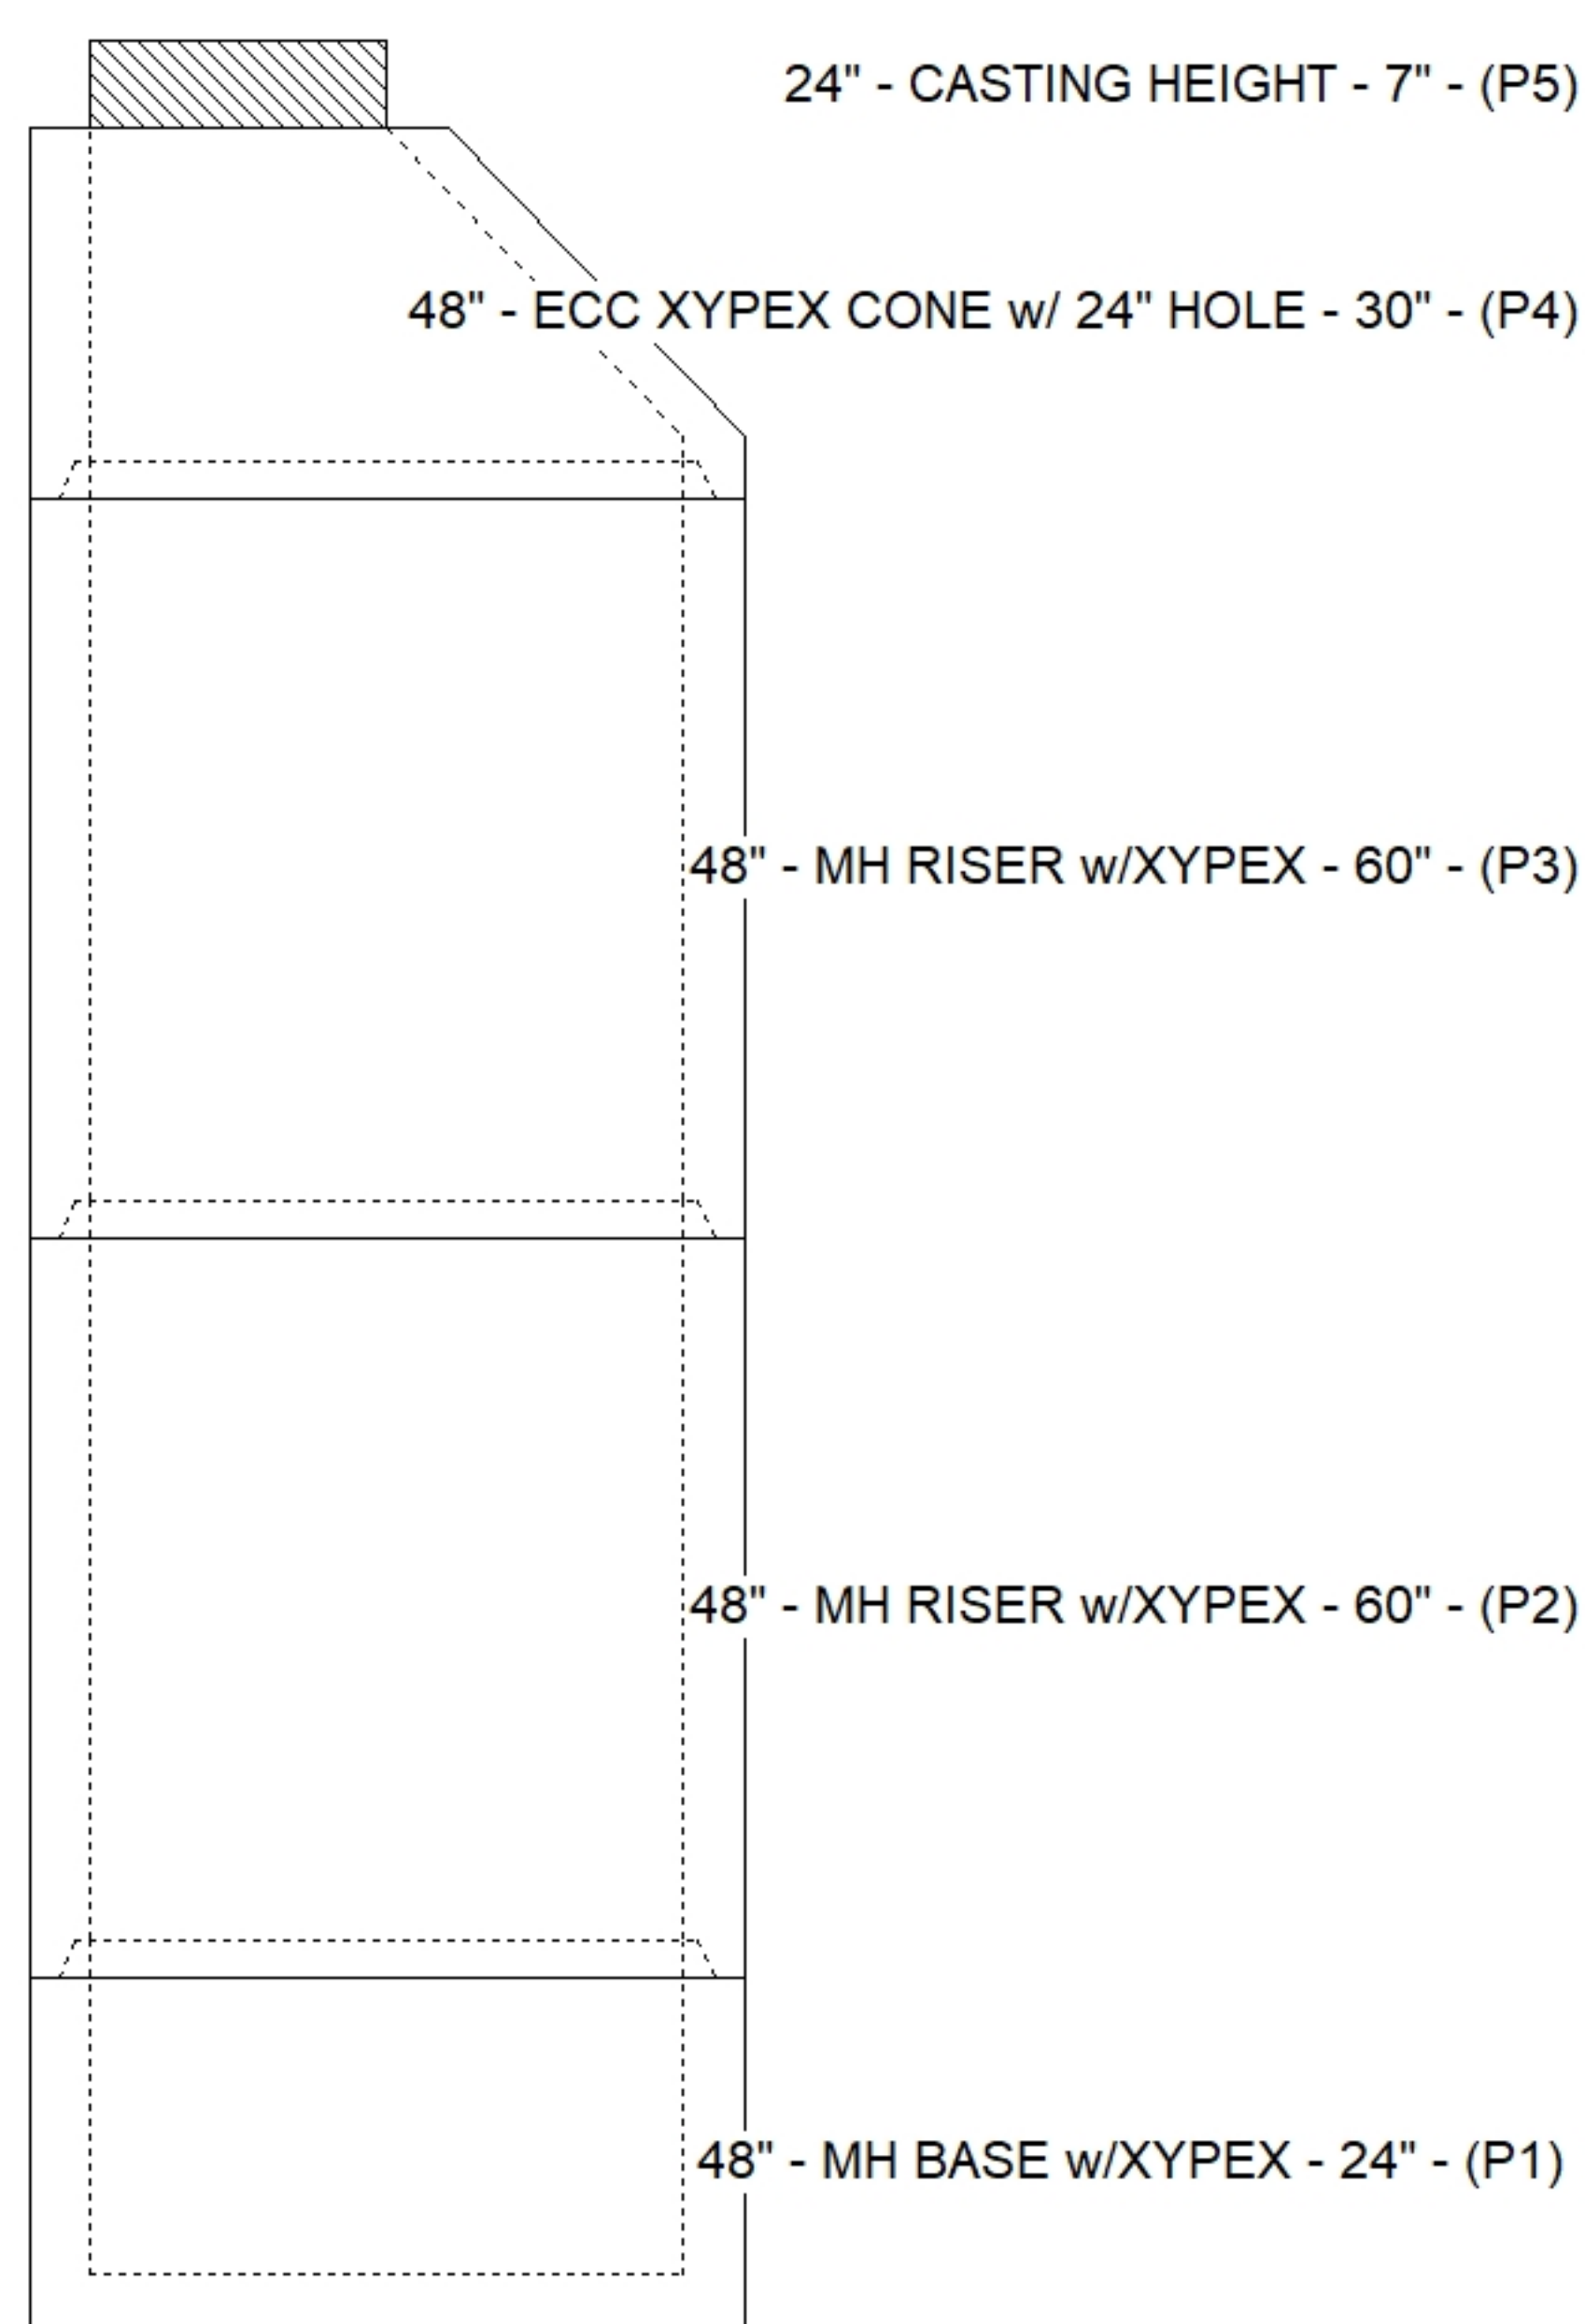

Default - Interior Dimensions

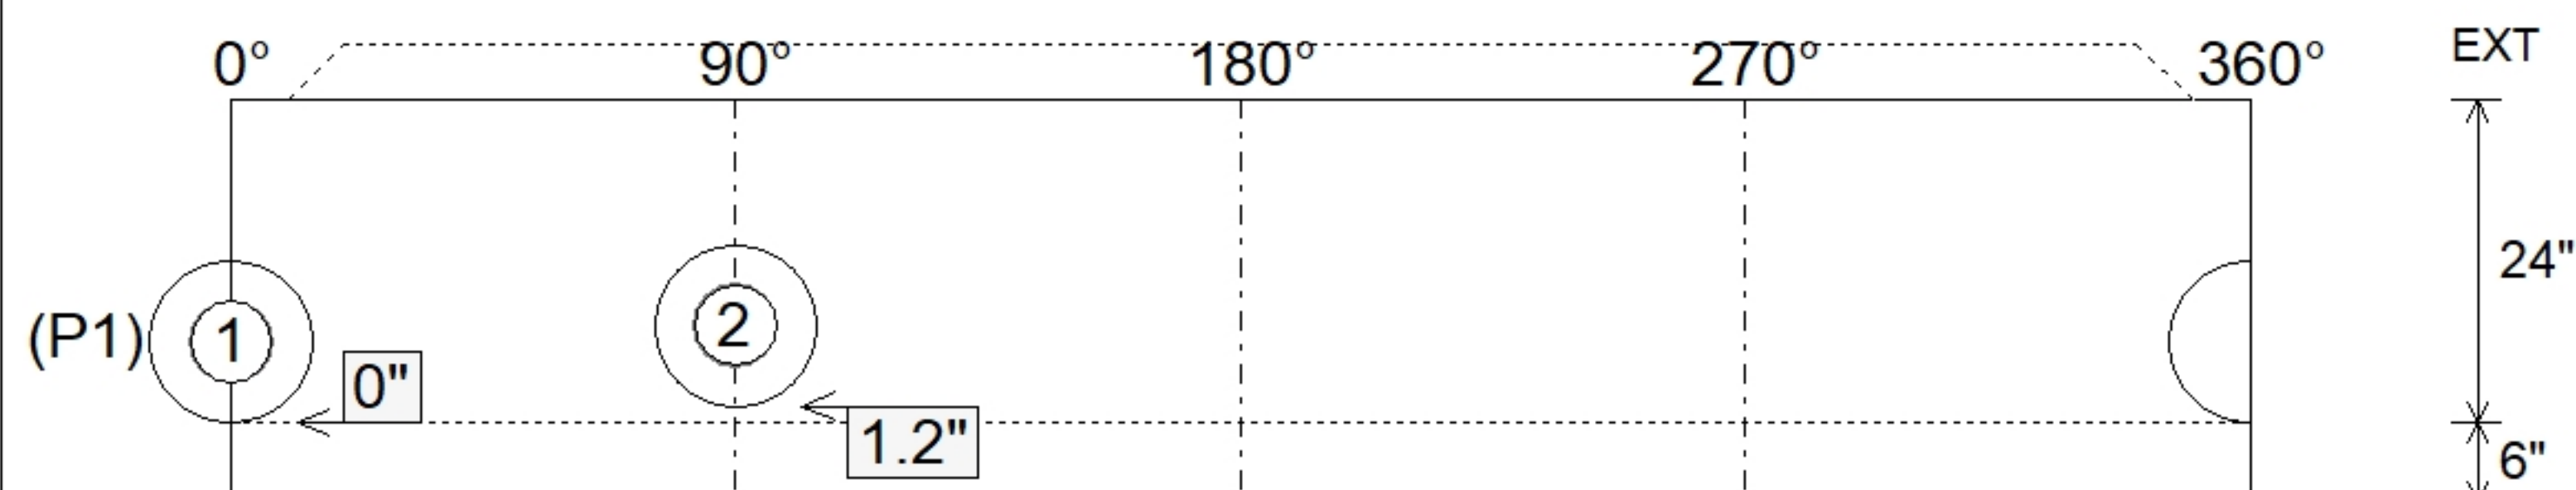

SUBMITTAL
APPROVED BY:
