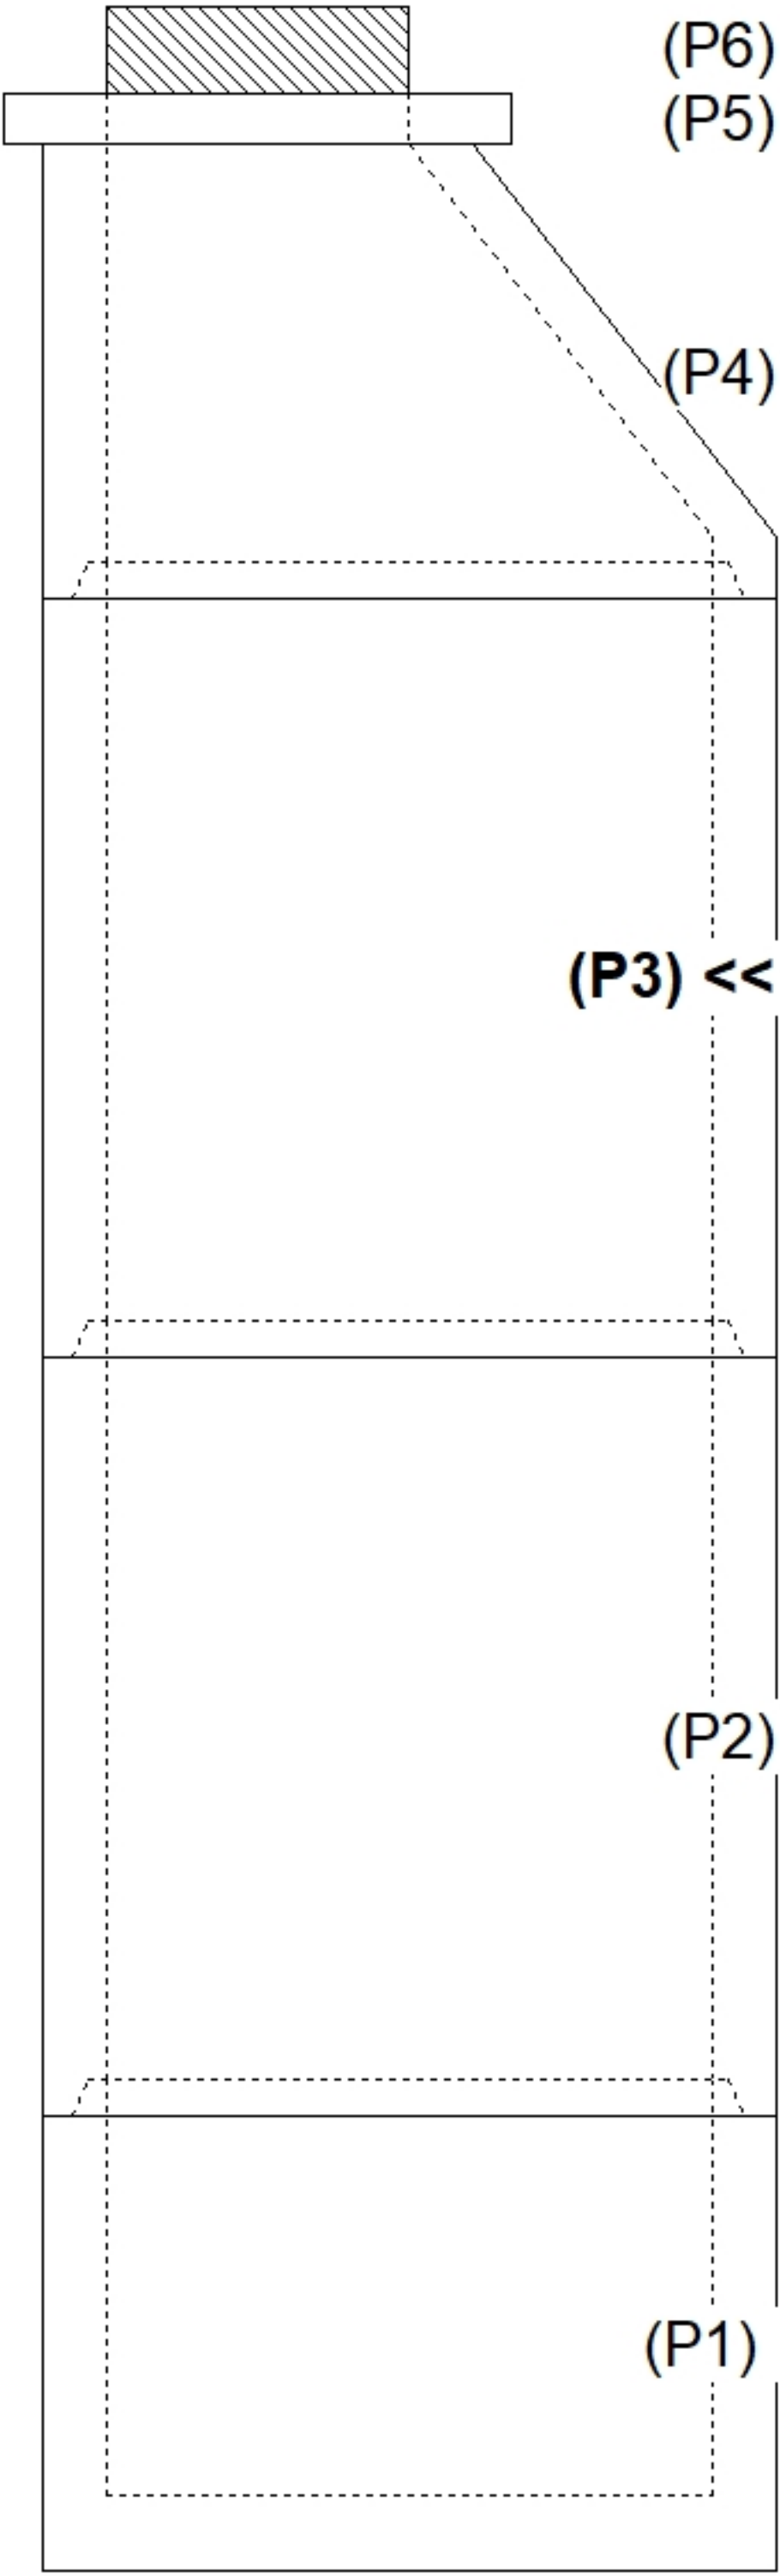
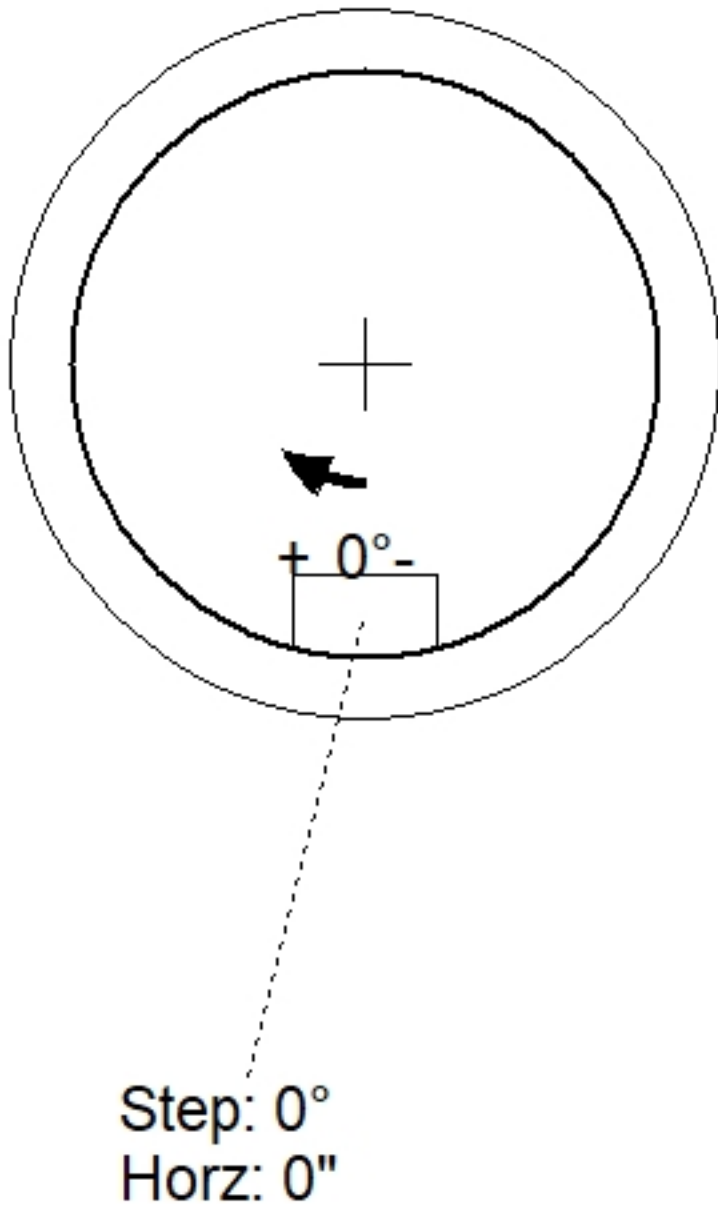
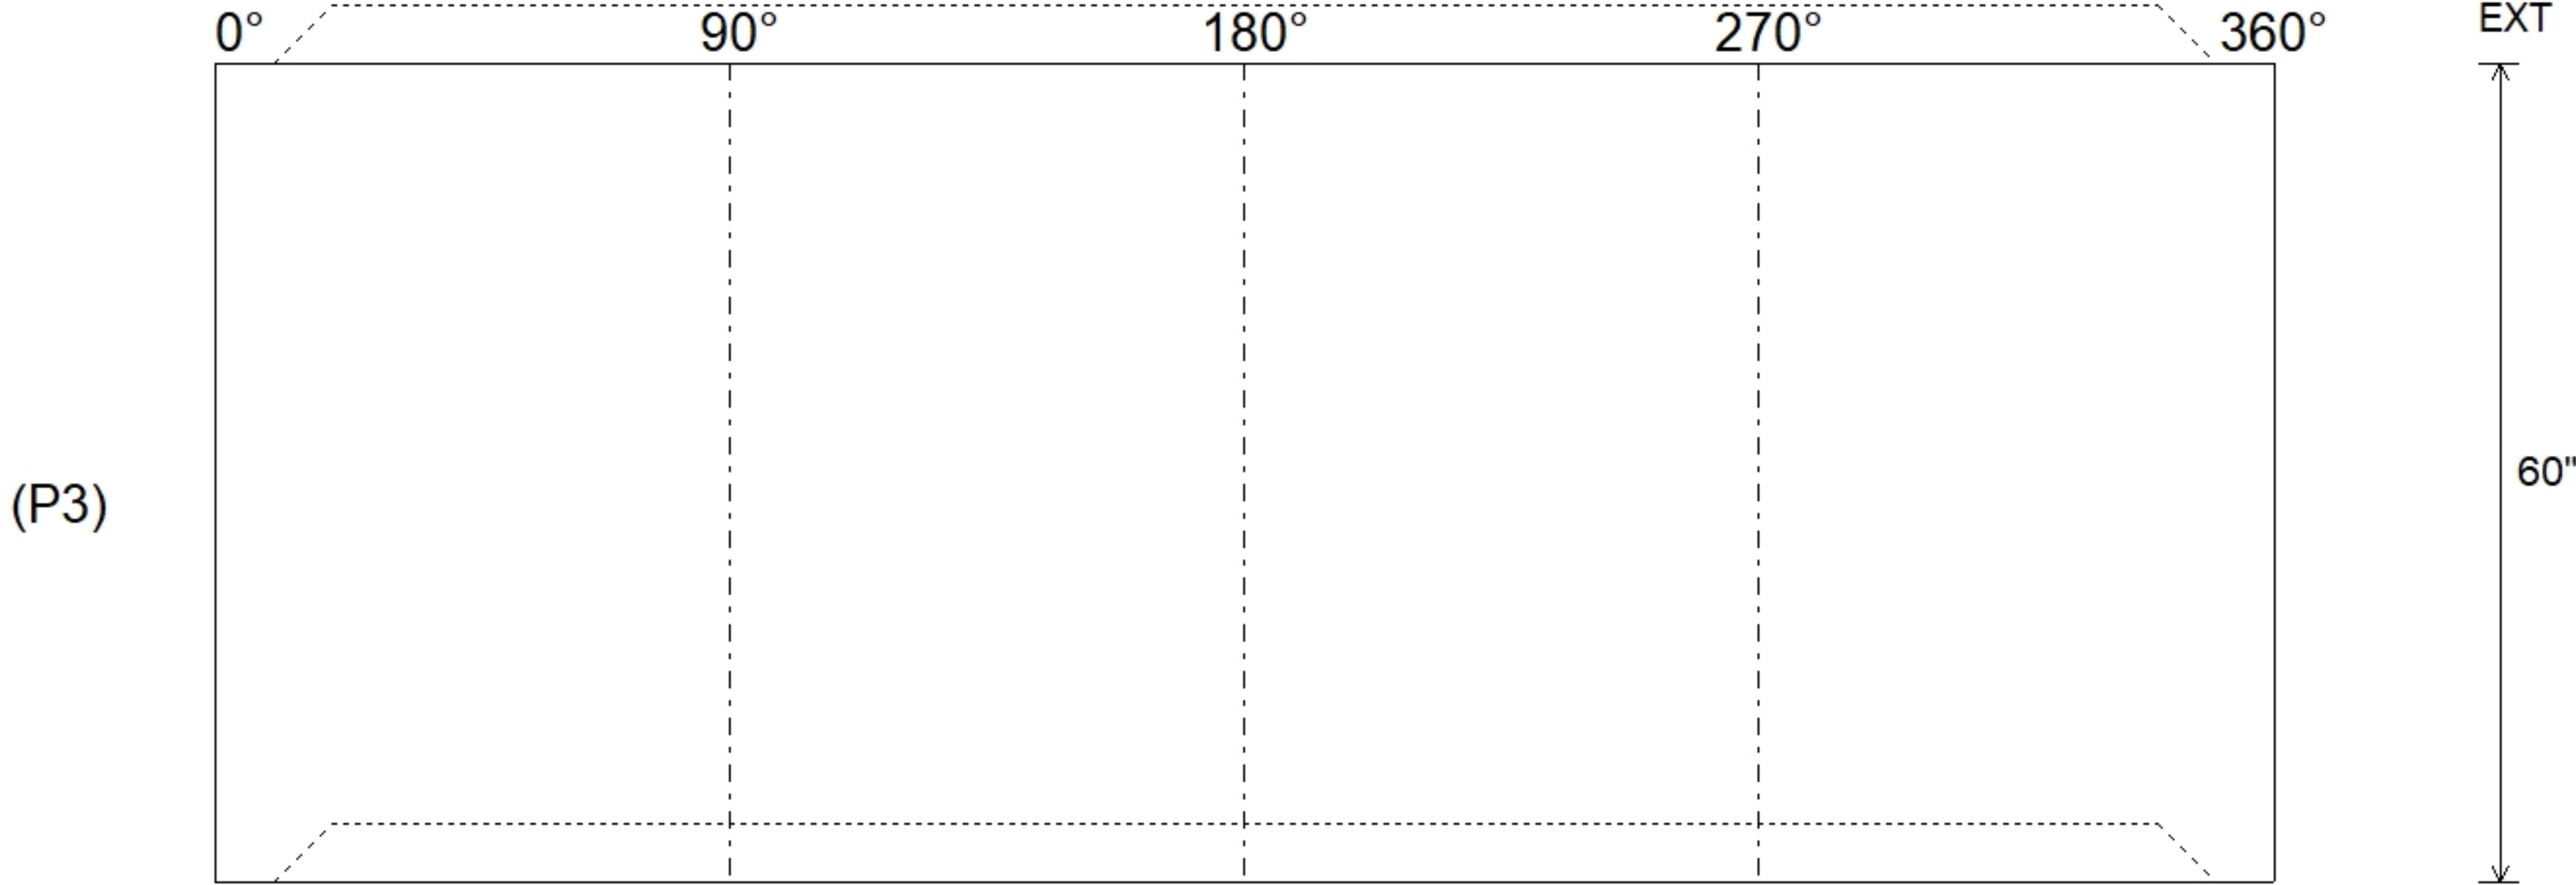


Job Name: 25-4288 - Project Wave Job Location: Franklin, KY 42134 Contractor: Cumberland Pipeline LLC					Plant: 100 9/2/2026 8:41:28 AM		Tech: PC: Erica Bradley				
Structure ID: A5											
P3		MH048RS60X		MH RISER w/XYPEX T/G							
P6) 24" - CASTING HEIGHT - 7" P5) 24" - XYPEX GRADE RING F/F - 4" P4) 48" - ECC XYPEX CONE w/ 24" HOLE F/G - 36" P3) 48" - MH RISER w/XYPEX T/G - 60" P2) 48" - MH RISER w/XYPEX T/G - 60" P1) 48" - MH BASE w/XYPEX T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - JBS 1150 F/C SANITARY 3) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 1) PSX - 12-06 NYLO 15) MH Step ML-10-TDS-NCR - 10"					0 lb 270 lb 2251 lb 4192 lb 4192 lb 3282 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 16 lb 8 lb 0 lb ----- 15900 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. JBS 1150 FRAME & COVER "SANITARY" SUPPLIED BY ICAST				
Rim: 717.99' Rim to Invert: 16.38' Slack: 1.56" Sump: 2"					Structure Total: 15900 lb Step Position: 0°						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)   INSIDE WALL DIMENSIONS  EXT 60"											
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 60" Height (Ext): 60"		Weight (Net): 4192 lb Volume (Net): 1.07cu.yd	
