



Job Name: 25-4288 - Project Wave Job Location: Franklin, KY 42134 Contractor: Cumberland Pipeline LLC					Plant: 100 7/10/2026 8:12:54 AM		Tech: Jared - A PC: Erica Bradley			
Structure ID: A5.1										
P1 MH048BA30X			MH BASE w/XYPEX							
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC XYPEX CONE w/ 24" HOLE - 42" P1) 48" - MH BASE w/XYPEX - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - JBS 1150 F/C SANITARY 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 6) MH Step ML-10-TDS-NCR - 10"					0 lb 3116 lb 3330 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 8153 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. JBS 1150 FRAME & COVER "SANITARY" SUPPLIED BY ICAST			
Rim: 711.44' Rim to Invert: 6.64' Slack: 2.68" Sump: 2" Step Position: 0°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	704.8'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	704.9'	180°	91.106"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)



UPSIDE-DOWN VIEW (int. dimensions)




INSIDE WALL DIMENSIONS

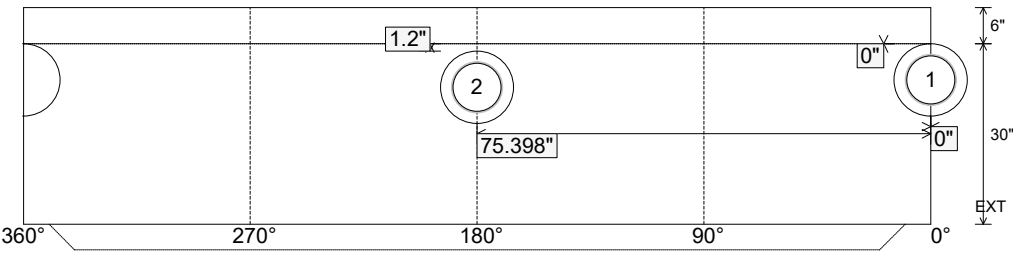


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3330 lb Volume (Net): 0.85cu.yd
----------------------------------	---------------------------------	--	--	--


Job Name: 25-4288 - Project Wave Job Location: Franklin, KY 42134 Contractor: Cumberland Pipeline LLC				Plant: 100 7/10/2026 8:12:54 AM		Tech: Jared - A PC: Erica Bradley				
Structure ID: A5.1										
P1 MH048BA30X				MH BASE w/XYPEX						
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC XYPEX CONE w/ 24" HOLE - 42" P1) 48" - MH BASE w/XYPEX - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - JBS 1150 F/C SANITARY 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 6) MH Step ML-10-TDS-NCR - 10" Structure Total: 8153 lb						0 lb 3116 lb 3330 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 0 lb 16 lb 0 lb Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. JBS 1150 FRAME & COVER "SANITARY" SUPPLIED BY ICAST INVERT CHANNEL DRAWING FULL HEIGHT INVERT				
Rim: 711.44' Rim to Invert: 6.64' Slack: 2.68" Sump: 2" Step Position: 0°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	704.8'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	704.9'	180°	91.106"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

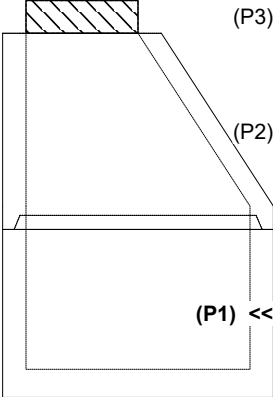


RIGHT-SIDE UP VIEW (int. dimensions)

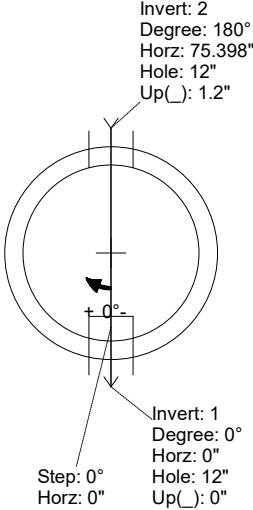

UPSIDE-DOWN VIEW (int. dimensions)

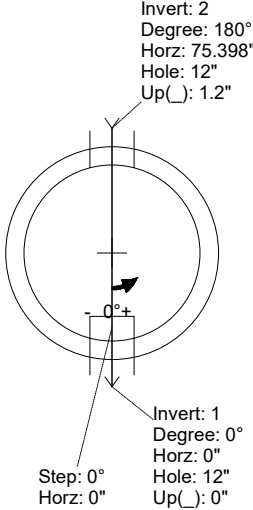

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3330 lb Volume (Net): 0.85cu.yd
----------------------------------	---------------------------------	--	--	--
