


Job Name: 25-4288 - Project Wave Job Location: Franklin, KY 42134 Contractor: Cumberland Pipeline LLC					Plant: 100 7/10/2026 8:14:21 AM		Tech: Jared - A PC: Erica Bradley				
Structure ID: A5.5											
P2 MH048RS60X			MH RISER w/XYPEX								
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC XYPEX CONE w/ 24" HOLE - 36" P2) 48" - MH RISER w/XYPEX - 60" P1) 48" - MH BASE w/XYPEX - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - JBS 1150 F/C SANITARY 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 10) MH Step ML-10-TDS-NCR - 10"						0 lb 2251 lb 4192 lb 2911 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 16 lb 0 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. JBS 1150 FRAME & COVER "SANITARY" SUPPLIED BY ICAST			
Structure Total:						11060 lb					
Rim: 725.13' Rim to Invert: 10.47' Slack: 0.64" Sump: 2" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

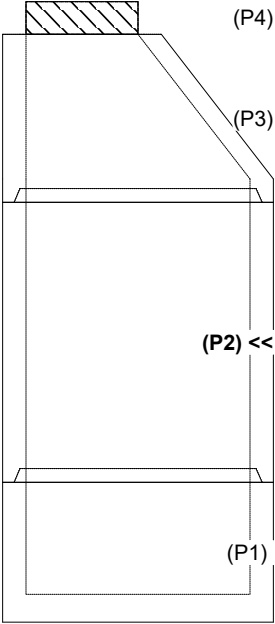


(P4)

(P3)

(P2) <<


(P1)

RIGHT-SIDE UP VIEW (int. dimensions)



Step: 0°
Horz: 0°

INSIDE WALL DIMENSIONS

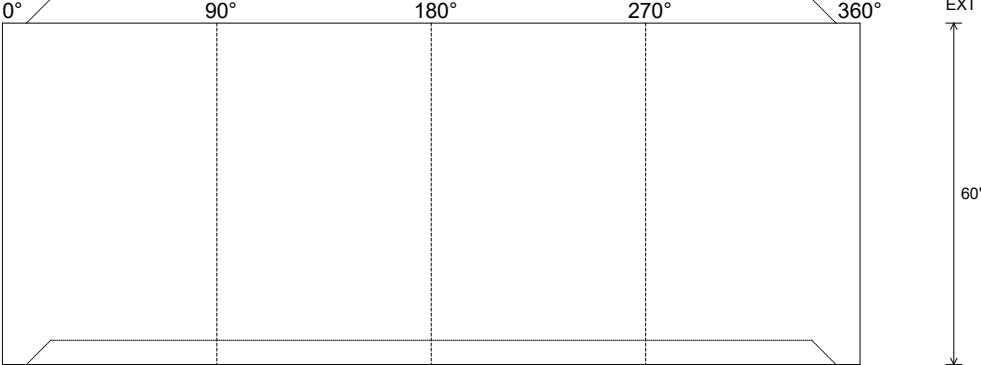

(P2)

0° 90° 180° 270° 360°

EXT
60"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 60" Height (Ext): 60"	Weight (Net): 4192 lb Volume (Net): 1.07cu.yd
----------------------------------	------------------------------------	--	--	--
