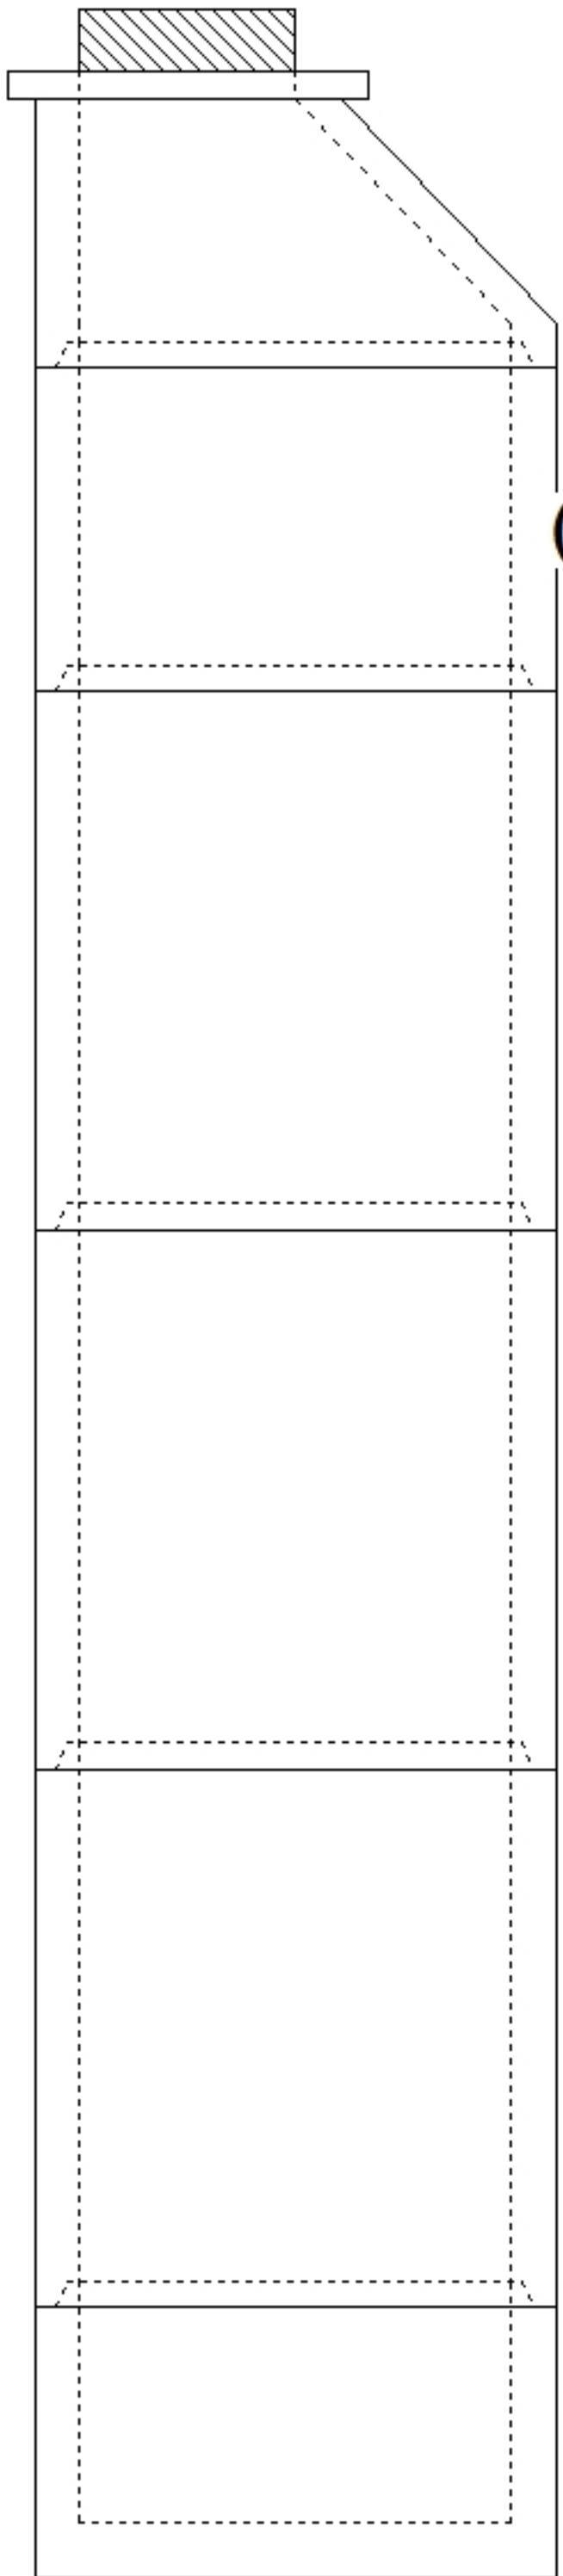
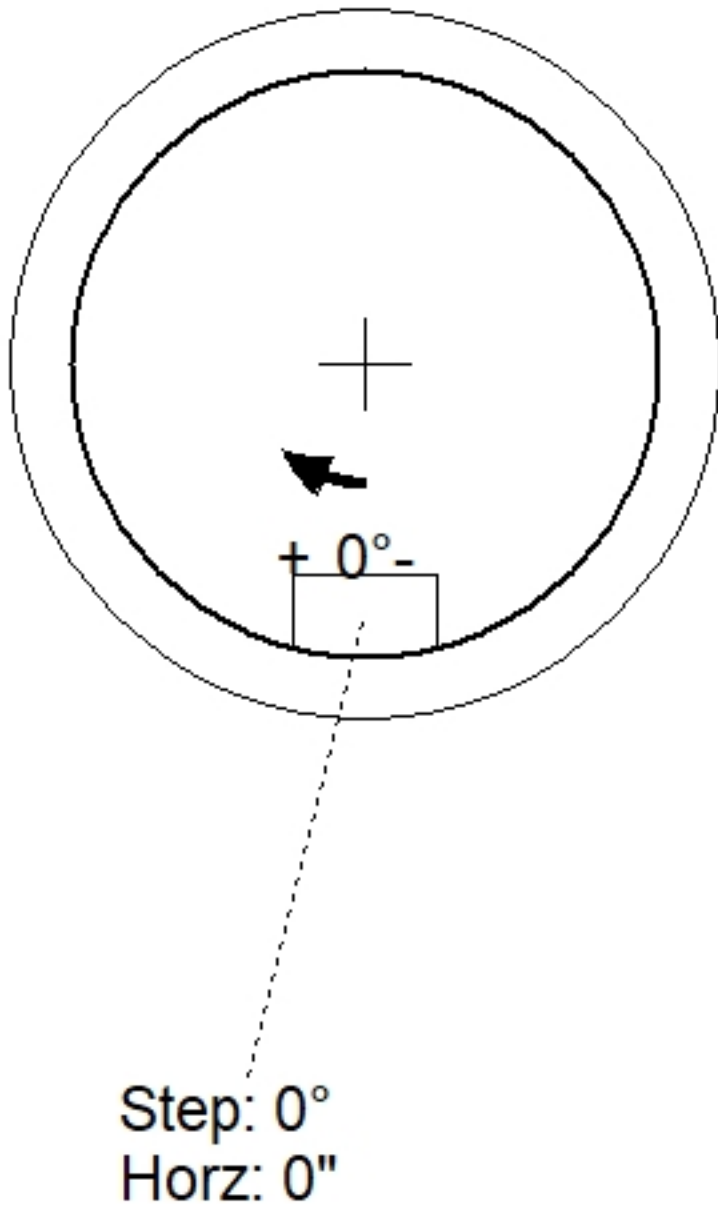
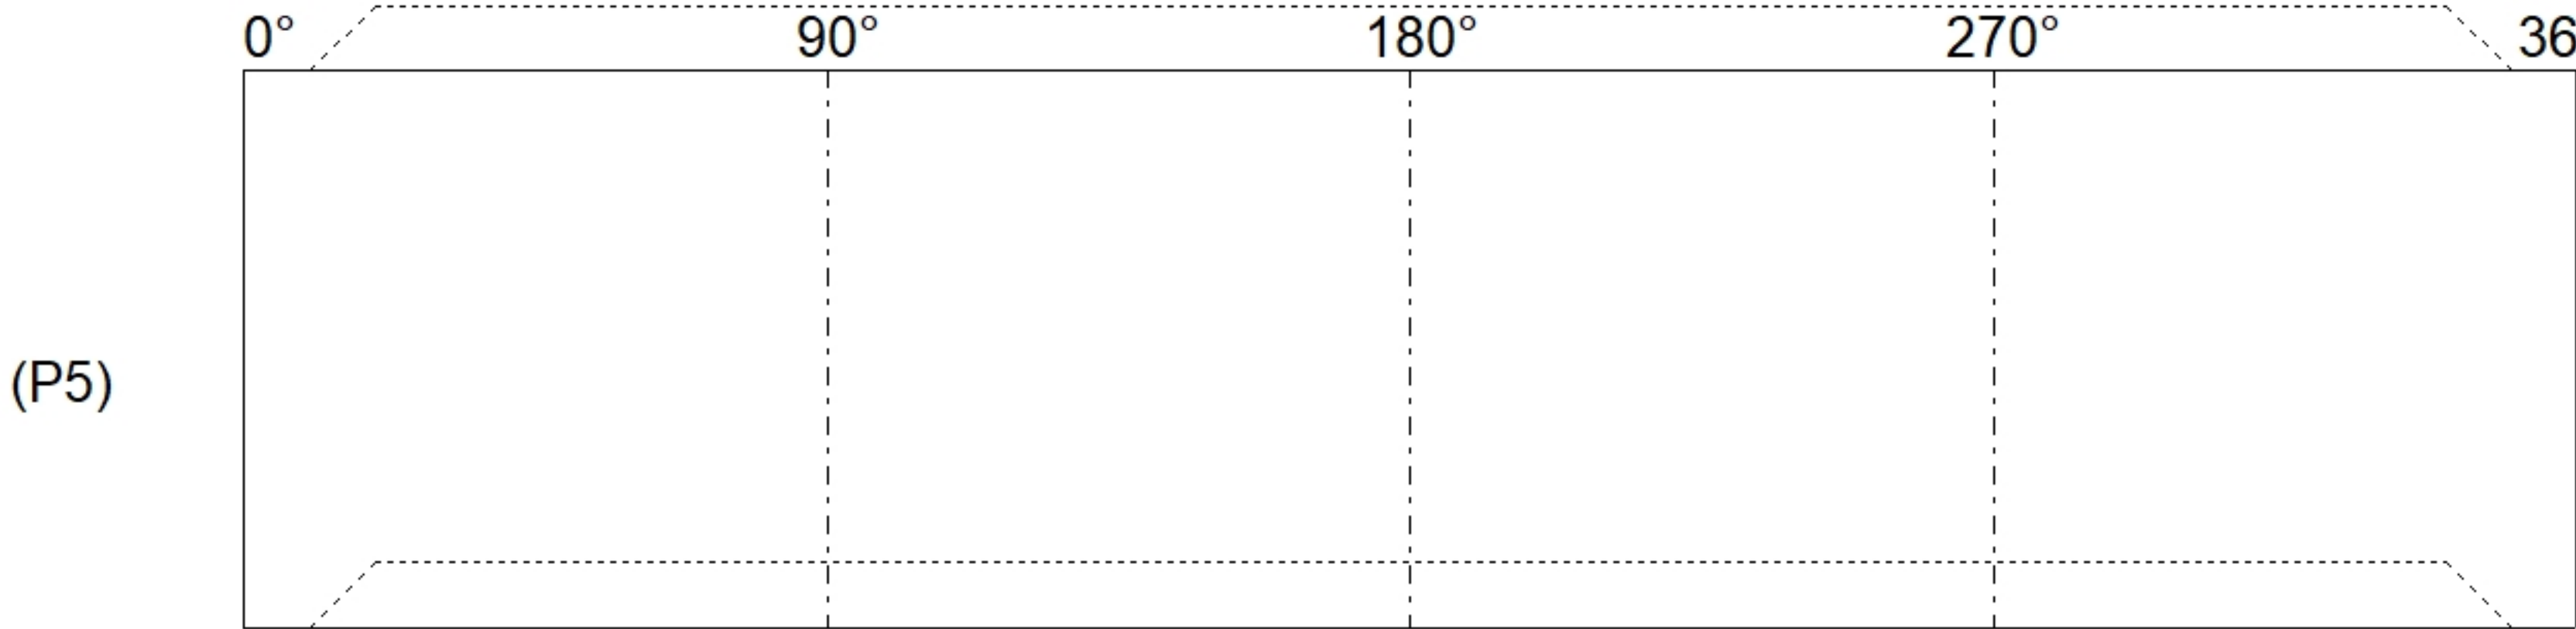



Job Name: 25-4288 - Project Wave Job Location: Franklin, KY 42134 Contractor: Cumberland Pipeline LLC					Plant: 100 9/2/2026 8:41:33 AM		Tech: PC: Erica Bradley				
Structure ID: A6											
P5		MH048RS36X		MH RISER w/XYPEX T/G							
P8) 24" - CASTING HEIGHT - 7" P7) 24" - XYPEX GRADE RING F/F - 3" P6) 48" - ECC XYPEX CONE w/ 24" HOLE F/G - 30" P5) 48" - MH RISER w/XYPEX T/G - 36" P4) 48" - MH RISER w/XYPEX T/G - 60" P3) 48" - MH RISER w/XYPEX T/G - 60" P2) 48" - MH RISER w/XYPEX T/G - 60" P1) 48" - MH BASE w/XYPEX T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - JBS 1150 F/C SANITARY 5) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 23) MH Step ML-10-TDS-NCR - 10"						0 lb 202 lb 1981 lb 2515 lb 4192 lb 4192 lb 4192 lb 2911 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 16 lb 0 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. JBS 1150 FRAME & COVER "SANITARY" SUPPLIED BY ICAST			
Rim: 725.92' Rim to Invert: 23.2' Slack: 0.4" Sump: 2" Structure Total: 21890 lb						Step Position: 0°					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 36" Height (Ext): 36"		Weight (Net): 2515 lb Volume (Net): 0.64cu.yd	
