





Floor (Bot): 704.953'  
Overall Height: 21.083'  
Slack: 2.8"

|                                                  |                 |
|--------------------------------------------------|-----------------|
| P6) 24" - CASTING HEIGHT - 7"                    | 0 lb            |
| P5) 48" - ECC XYPEX CONE w/ 24" HOLE - 30"       | 1981 lb         |
| P4) 48" - MH RISER w/XYPEX - 60"                 | 4192 lb         |
| P3) 48" - MH RISER w/XYPEX - 60"                 | 4192 lb         |
| P2) 48" - MH RISER w/XYPEX - 60"                 | 4192 lb         |
| P1) 48" - MH BASE w/XYPEX - 30"                  | 3330 lb         |
| 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212      | 0 lb            |
| 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)    | 0 lb            |
| 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT | 1440 lb         |
| 1) CASTING - JBS 1150 F/C SANITARY               | 250 lb          |
| 4) 48" - Conseal CS-102 1.00" (Double)           | 0 lb            |
| 1) 24" - Conseal CS-102 1.00" (Double)           | 0 lb            |
| 2) PSX - 12-08 NYLO                              | 16 lb           |
| 20) MH Step ML-10-TDS-NCR - 10"                  | 0 lb            |
| <b>Structure Total:</b>                          | <b>19592 lb</b> |

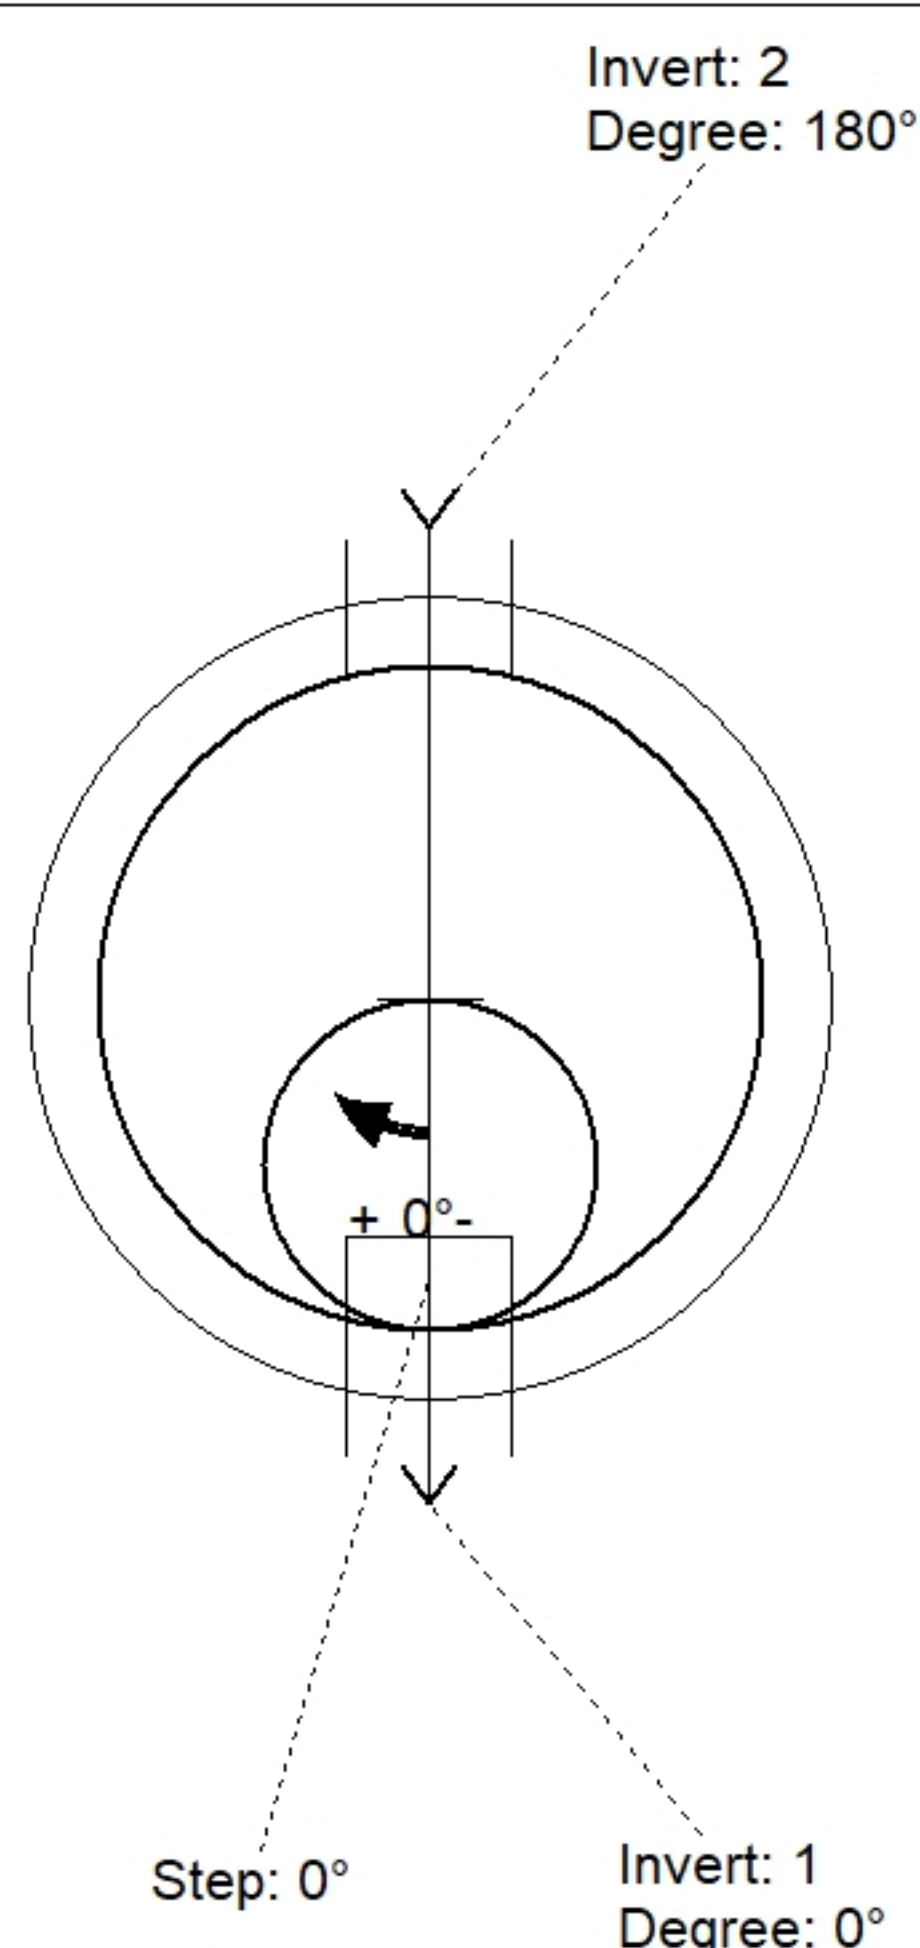

| Position | Elev    | Angle | Pipe         | Pipe OD | Hole | Connector      | Up (⌵) | Ref |
|----------|---------|-------|--------------|---------|------|----------------|--------|-----|
| Rim      | 726.27' |       |              |         |      |                |        |     |
| Reducer  |         |       |              |         |      |                |        |     |
| Invert 1 | 705.62' | 0°    | 8" PVC SDR35 | 8.5"    | 12"  | PSX 12-08 NYLO | 0"     | P1  |
| Invert 2 | 705.72' | 180°  | 8" PVC SDR35 | 8.5"    | 12"  | PSX 12-08 NYLO | 1.2"   | P1  |
| Invert 3 |         |       |              |         |      |                |        |     |
| Invert 4 |         |       |              |         |      |                |        |     |
| Invert 5 |         |       |              |         |      |                |        |     |
| Invert 6 |         |       |              |         |      |                |        |     |
| Invert 7 |         |       |              |         |      |                |        |     |
| Invert 8 |         |       |              |         |      |                |        |     |

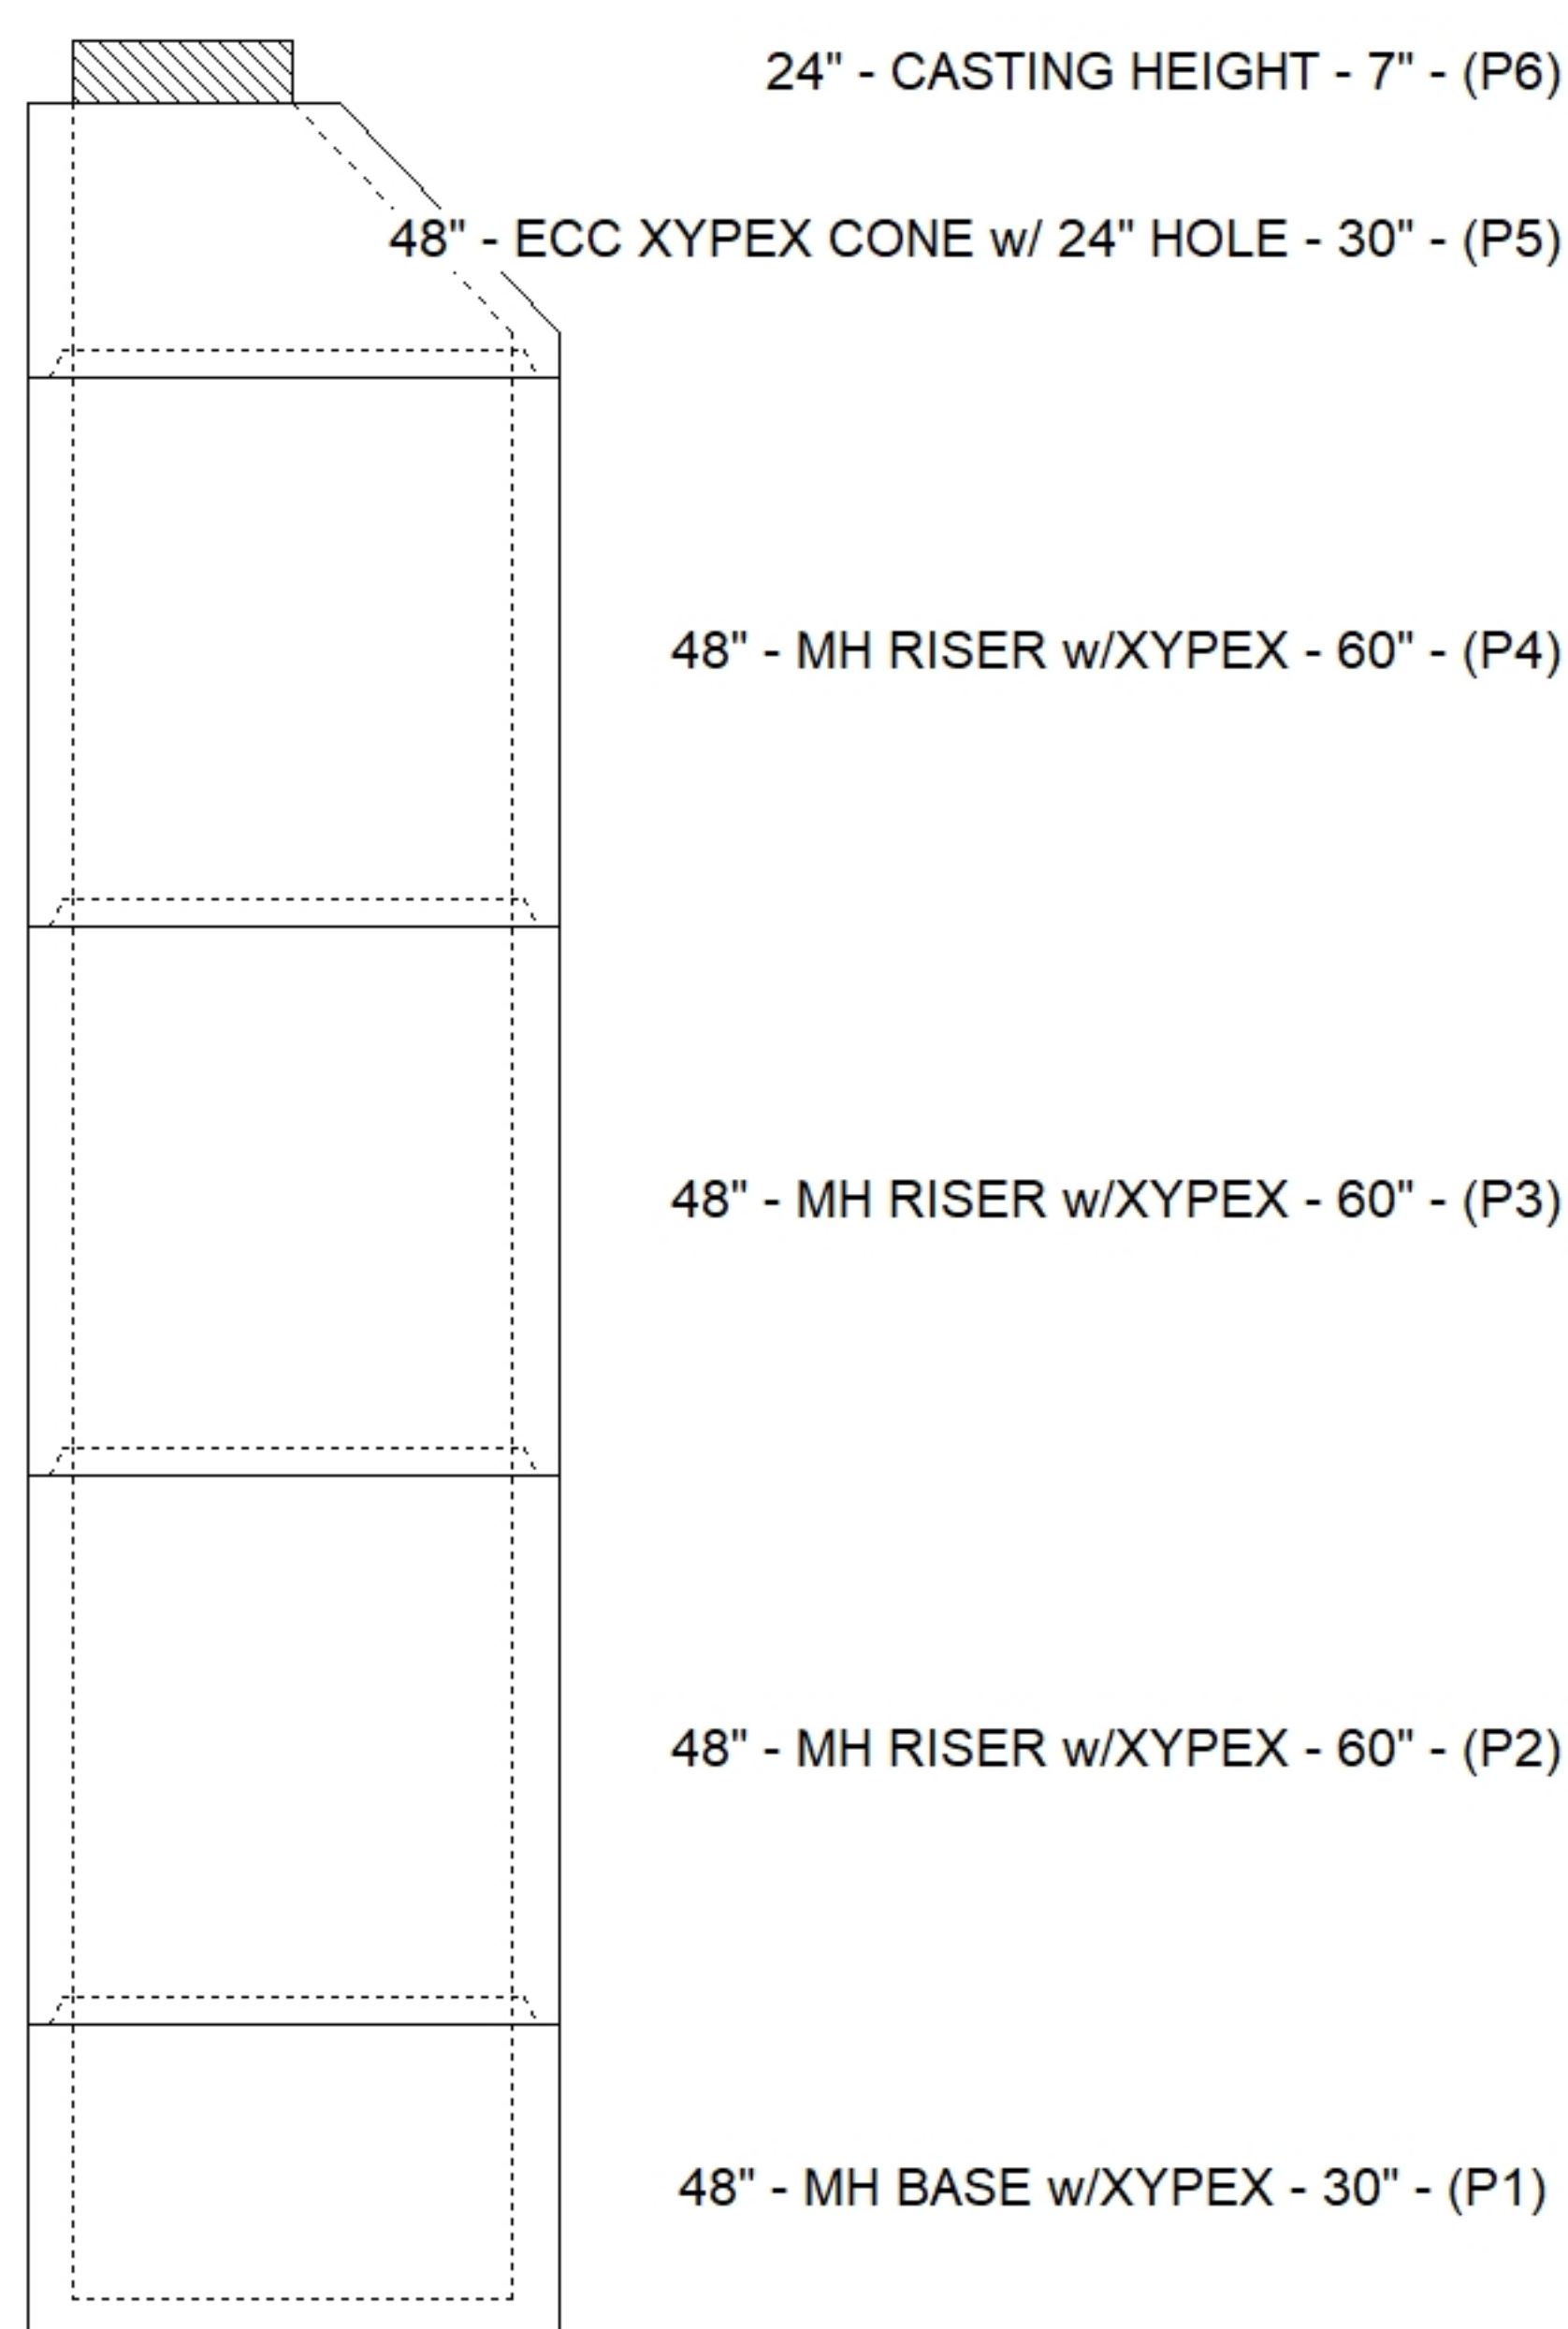

SUBMITTAL  
APPROVED BY:
