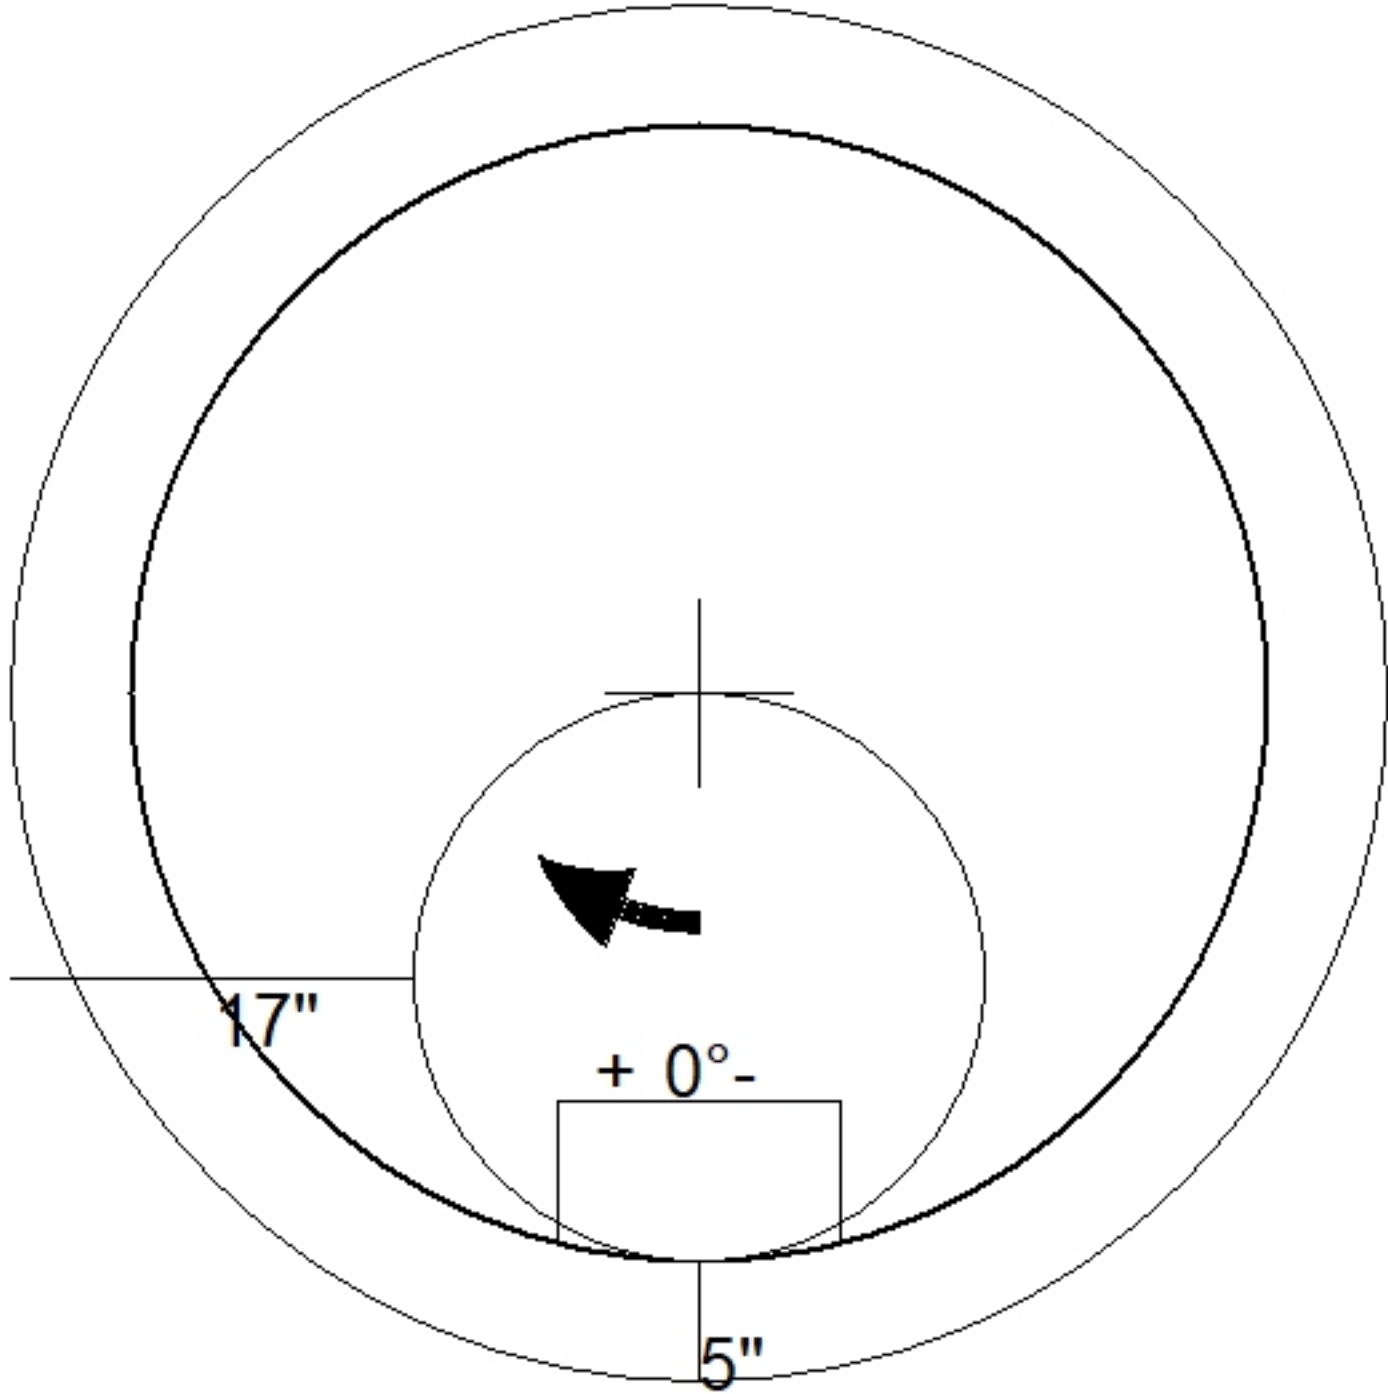
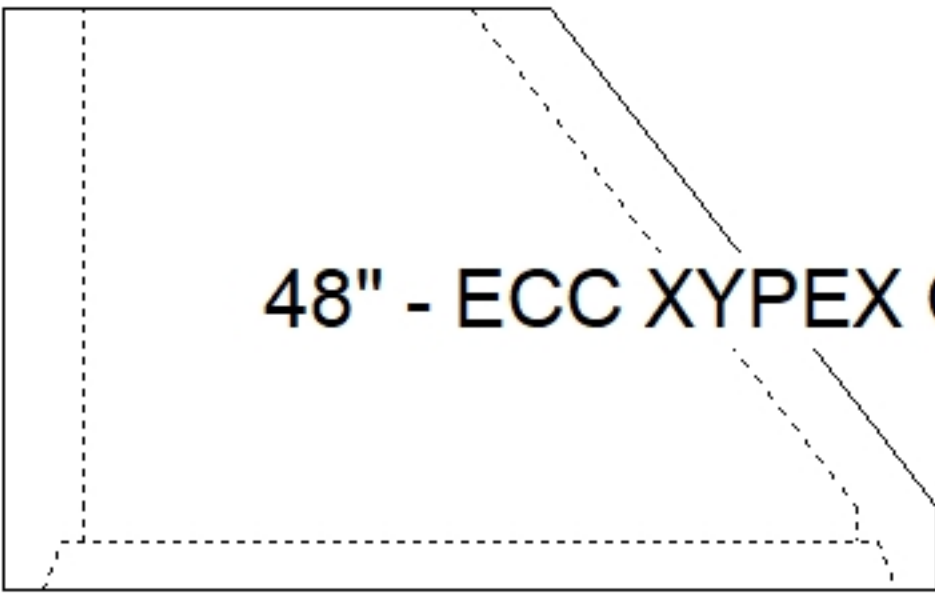


Job Name: 25-4288 - Project Wave Job Location: Franklin, KY 42134 Contractor: Cumberland Pipeline LLC		Plant: 100 9/2/2026 8:40:48 AM	Tech: PC: Erica Bradley	
Structure ID: A9				
P5 MH048CN36X		ECC XYPEX CONE w/ 24" HOLE F/G		
P6) 24" - CASTING HEIGHT - 7" P5) 48" - ECC XYPEX CONE w/ 24" HOLE F/G - 36" P4) 48" - MH RISER w/XYPEX T/G - 60" P3) 48" - MH RISER w/XYPEX T/G - 60" P2) 48" - MH RISER w/DROP/XYPEX T/G - 48" P1) 48" - MH BASE w/DROP/XYPEX T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - JBS 1150 F/C SANITARY 4) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 1) Drop Tee - 6" PVC 1) Drop Elbow - 6" PVC 19) MH Step ML-10-TDS-NCR - 10"		0 lb 2251 lb 4192 lb 4192 lb 3339 lb 2897 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 16 lb 0 lb 0 lb 0 lb ----- 18577 lb	Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. JBS 1150 FRAME & COVER "SANITARY" SUPPLIED BY ICAST 7. EXTERIOR DROP @ 90 DEGREES.	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 2251 lb Volume (Net): 0.57cu.yd
