



Job Name: 25-4288 - Project Wave Job Location: Franklin, KY 42134 Contractor: Cumberland Pipeline LLC					Plant: 100 7/10/2026 8:12:50 AM		Tech: Jared - A PC: Erica Bradley			
Structure ID: E1										
P1 MH048BA24X			MH BASE w/XYPEX							
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC XYPEX CONE w/ 24" HOLE - 30" P3) 48" - MH RISER w/XYPEX - 36" P2) 48" - MH RISER w/XYPEX - 60" P1) 48" - MH BASE w/XYPEX - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - JBS 1150 F/C SANITARY 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 13) MH Step ML-10-TDS-NCR - 10"					0 lb 1981 lb 2515 lb 4192 lb 2911 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 16 lb 0 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. JBS 1150 FRAME & COVER "SANITARY" SUPPLIED BY ICAST			
Rim: 697.78' Rim to Invert: 12.98' Slack: 0.76" Sump: 2" Step Position: 0°					Structure Total: 13304 lb					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	684.8'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	684.9'	248°	125.524"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

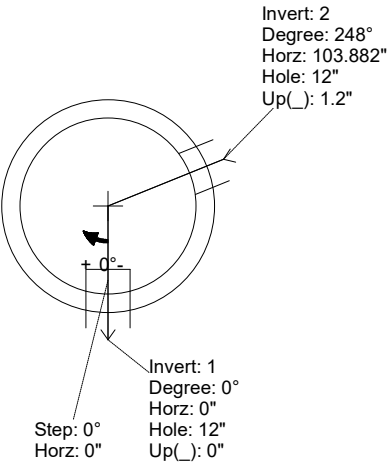

UPSIDE-DOWN VIEW (int. dimensions)

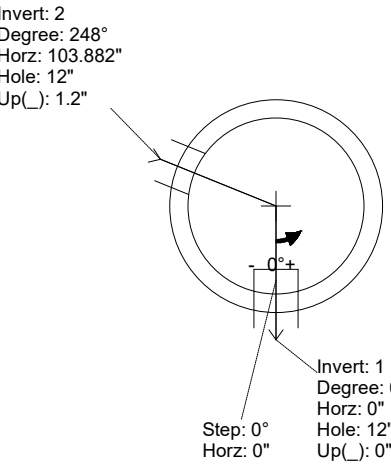


INSIDE WALL DIMENSIONS




Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2911 lb Volume (Net): 0.74cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 25-4288 - Project Wave Job Location: Franklin, KY 42134 Contractor: Cumberland Pipeline LLC				Plant: 100 7/10/2026 8:12:50 AM		Tech: Jared - A PC: Erica Bradley						
Structure ID: E1												
P1 MH048BA24X				MH BASE w/XYPEX								
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC XYPEX CONE w/ 24" HOLE - 30" P3) 48" - MH RISER w/XYPEX - 36" P2) 48" - MH RISER w/XYPEX - 60" P1) 48" - MH BASE w/XYPEX - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - JBS 1150 F/C SANITARY 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 13) MH Step ML-10-TDS-NCR - 10"						0 lb 1981 lb 2515 lb 4192 lb 2911 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 16 lb 0 lb ----- 13304 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. JBS 1150 FRAME & COVER "SANITARY" SUPPLIED BY ICAST INVERT CHANNEL DRAWING FULL HEIGHT INVERT				
Rim: 697.78' Rim to Invert: 12.98' Slack: 0.76" Sump: 2" Step Position: 0°												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	684.8'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"		
Invert 2	684.9'	248°	125.524"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												


RIGHT-SIDE UP VIEW (int. dimensions)

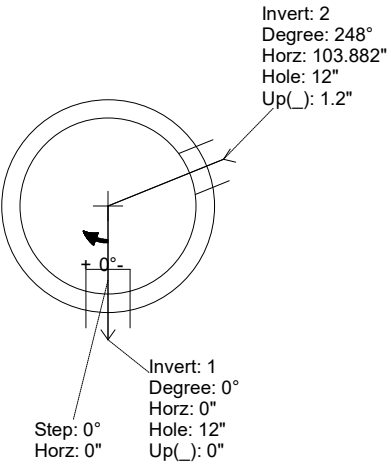

UPSIDE-DOWN VIEW (int. dimensions)

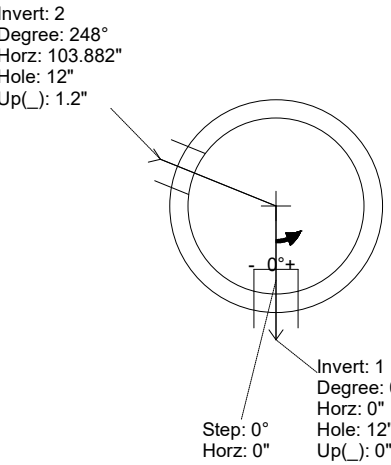

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2911 lb Volume (Net): 0.74cu.yd
----------------------------------	---------------------------------	--	--	--
