

Job Name: 25-4299 - Seneca High School	Plant: 100	Tech: J. Horsley	
Job Location: Louisville, KY	2/13/2026 1:01:35 PM	PC: J. Jarvis	
Contractor: Dan Cristiani Excavating Co. Inc.			

**Structure ID: B14**

**P1 BX2436-08BVF**

**BOX BASE 8inW, 8inF, Variable Ht F/n**

- P2) 24" x 36" - CASTING HEIGHT - 6"
- P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 21"
- 1) 24" x 36" - Conseal CS-102 1.00"
- 2) Hole - 14"

0 lb  
3306 lb  
0 lb  
0 lb  
-----  
Structure Total: 3306 lb



- Structure Notes:
1. PER LOUISVILLE MSD / ASTM C-913 SPECIFICATIONS
  2. CONCRETE: 4,000 PSI AT 28 DAYS
  3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
  4. NO STORM INVERT
  5. NO STEPS
  6. HOE 470 FRAME, GRATE, & CURB HOOD SUPPLIED BY OTHERS

Rim: 487.7'    Rim to Invert: 2.3'    Slack: 0.6"    Sump: 0"    Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ( )	Offset
Invert 1	485.4'	65°	22.191"	10" HDPE	11.4"	Hole 14	14"	15.447"	-0.7"	5"
Invert 2	485.4'	210°	24.619"	10" HDPE	11.4"	Hole 14	14"	16.166"	-0.7"	-9"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)

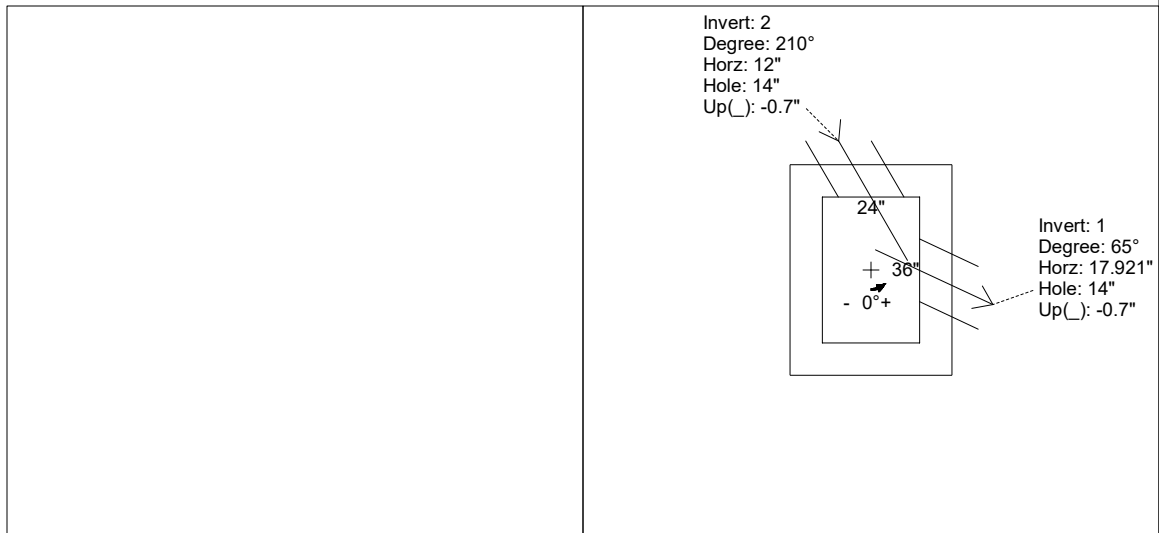

INSIDE WALL DIMENSIONS

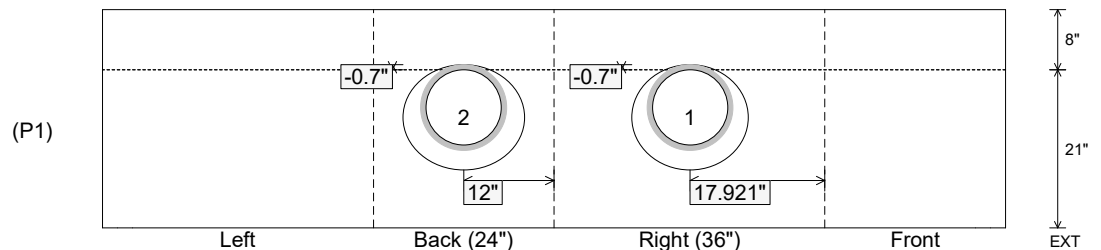

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 21" Height (Ext): 29"	Weight (Net): 3306 lb Volume (Net): 0.84cu.yd
----------------------------------	-------------------------------	--	--	--
