

Job Name: 25-4299 - Seneca High School Job Location: Louisville, KY Contractor: Dan Cristiani Excavating Co. Inc.	Plant: 100 2/17/2026 10:38:46 AM	Tech: J. Horsley PC: J. Jarvis	
-------------------------------------------------------------------------------------------------------------------------	-------------------------------------	-----------------------------------	------------------------------------------------------------------------------------

Structure ID: H10

P1 BX2424-08BAVF

BOX BASE 8inW, 8inF, Variable Ht F/n

P2) 24" x 24" - CASTING HEIGHT - 4"
P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 26"
1) 24" x 24" - Conseal CS-102 1.00"
1) Hole - 16

0 lb
3173 lb
0 lb
0 lb

Structure Total: 3173 lb



- Structure Notes:
1. PER LOUISVILLE MSD / ASTM C-913 SPECIFICATIONS
 2. CONCRETE: 4,000 PSI AT 28 DAYS
 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
 4. NO STORM INVERT
 5. NO STEPS
 6. HOE 280T FRAME & GRATE SUPPLIED BY OTHERS

Rim: 482' Rim to Invert: 2.55' Slack: 0.6" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	479.45'	270°	20"	12" HDPE	14.5"	Hole 16	16"	16"	-1.25"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)

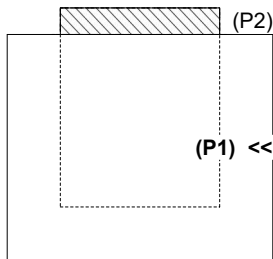

INSIDE WALL DIMENSIONS

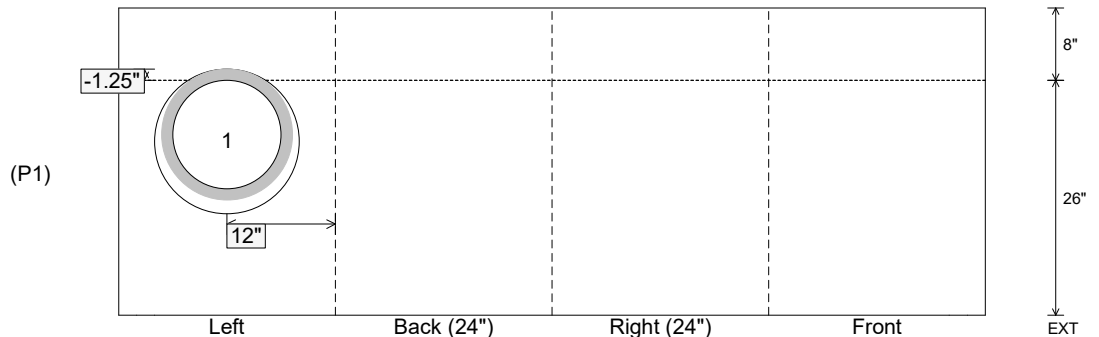

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 26" Height (Ext): 34"	Weight (Net): 3173 lb Volume (Net): 0.81cu.yd
----------------------------------	-------------------------------	----------------------------------------	----------------------------------------	--------------------------------------------------
