

Job Name: 25-4307 - Elkhorn Riser & Manhole	Plant: Beaver Dam	Tech: J. Coppage	
Job Location: Frankfort, KY	11/11/2025 10:46:53 AM	PC: J. Jarvis	
Contractor: Franklin BOE C/O Louisville Paving & Construction			

Structure ID: 2-54307a

P1 MH036RS36

MH RISER



P1) 36" - MH RISER - 36"	1518 lb
1) 36" - Conseal CS-102 1.00"	0 lb
Structure Total:	1518 lb

Structure Notes:
 1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


Rim: 3'	Rim to Invert: 0'	Slack: 0"	Sump: 0"	Step Position:
---------	-------------------	-----------	----------	----------------

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

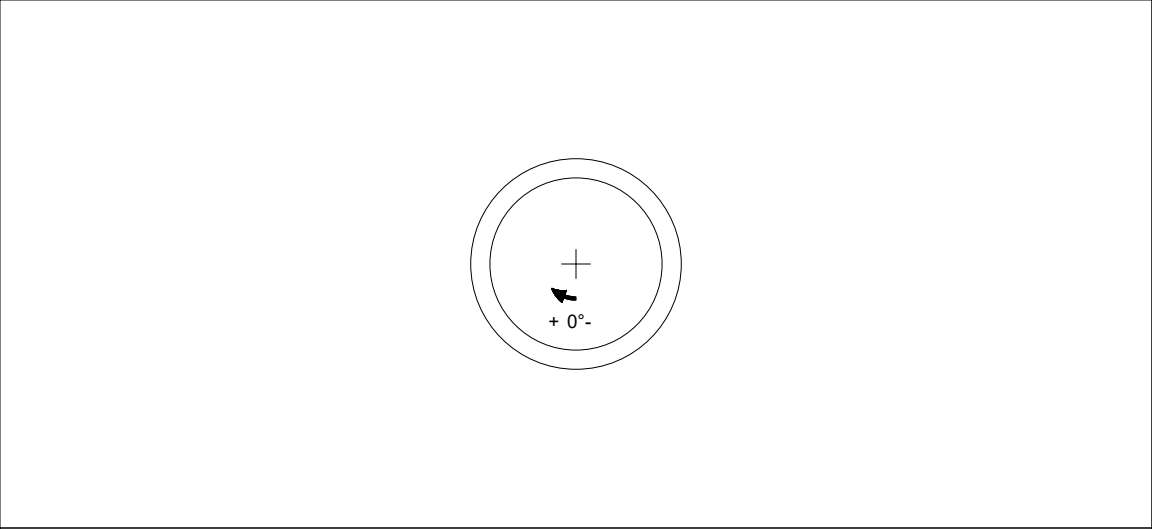

INSIDE WALL DIMENSIONS

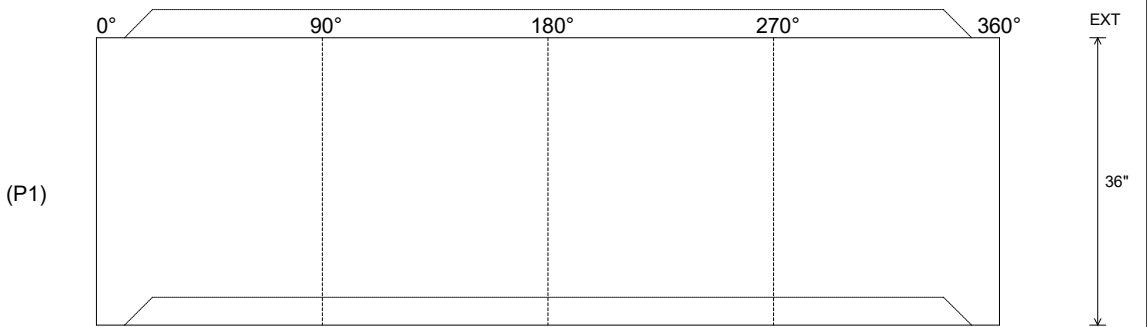

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 4" Floor Height: 0"	Height (Int): 36" Height (Ext): 36"	Weight (Net): 1518 lb Volume (Net): 0.39cu.yd
----------------------------------	------------------------------------	--	--	--
