



Structure ID: CB7

P1 MH048BAVF

MH BASE Custom Ht F/n

P3) 36" x 36" - CASTING HEIGHT - 3" P2) 48" - MH FLAT TOP w/36"x36" Hole F/F - 7" P1) 48" - MH BASE Custom Ht F/n - 33" 1) 48" - Conseal CS-102 1.00" 1) 36" x 36" - Conseal CS-102 1.00" 2) Hole - 24	0 lb 791 lb 3241 lb 0 lb 0 lb 0 lb ----- 4032 lb	Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. NO STEPS AND NO INVERT CHANNEL 5. CASTING SUPPLIED BY OTHERS (HOE 595 FRAME & GRATE)
---	---	---



Structure Total: 4032 lb

Rim: 702.95' Rim to Invert: 3.66' Slack: 0.92" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	699.29'	0°	0"	18" HDPE	21.2"	Hole 24	24"	25.133"	-1.6"	0"
Invert 2	699.29'	180°	91.106"	18" HDPE	21.2"	Hole 24	24"	25.133"	-1.6"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

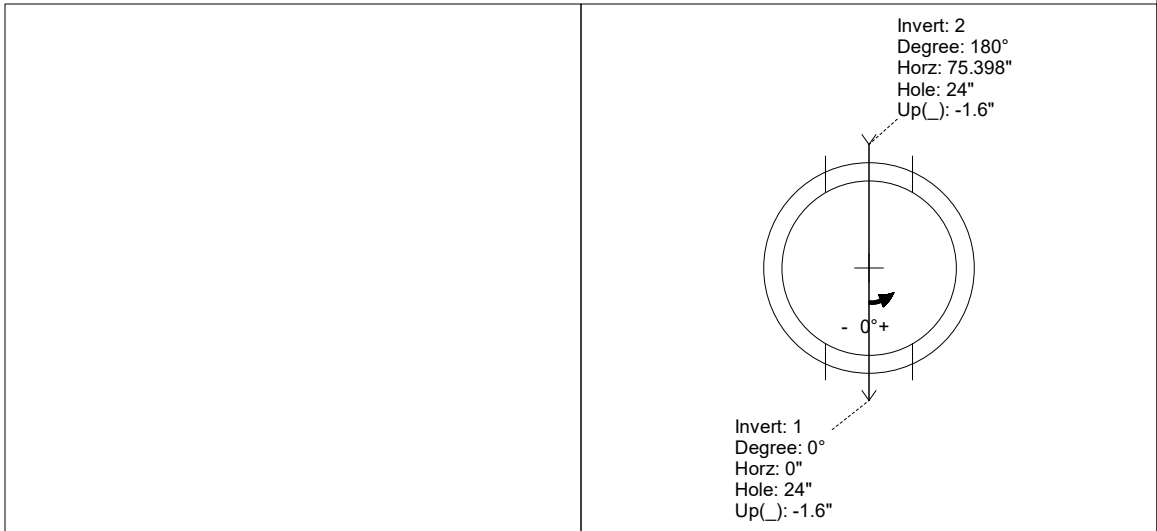

INSIDE WALL DIMENSIONS

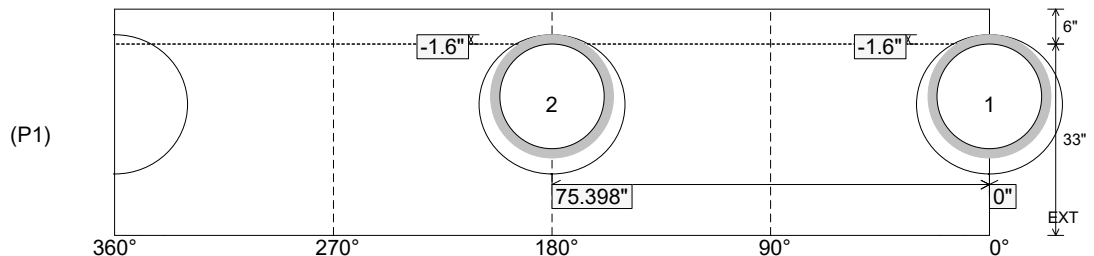

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 33" Height (Ext): 39"	Weight (Net): 3241 lb Volume (Net): 0.83cu.yd
----------------------------------	-------------------------------	--	--	--
