

Job Name: 25-4337 - Maywood Phase13
 Job Location: Bardstown, KY
 Contractor: Buzick Construction

Plant: 100

12/9/2025 11:21:30 AM

Tech: J. Horsley - F

PC: C. Goff



Structure ID: CI4

P1 MH060BAVF

MH BASE Custom Ht F/n

- P3) 24" x 36" - CASTING HEIGHT - 6"
- P2) 60" - MH FLAT TOP w/24"x36" Hole F/F - 8"
- P1) 60" - MH BASE Custom Ht F/n - 41"
- 1) 60" - Conseal CS-102 1.00"
- 1) 24" x 36" - Conseal CS-102 1.00"
- 1) Hole - 38
- 1) DOGHOUSE INVRTD - 40"x41"
- 3) MH Step ML-10-TDS-NCR - 10"

0 lb
 1546 lb
 5612 lb
 0 lb
 0 lb
 0 lb
 0 lb
 0 lb
 0 lb
 Structure Total: 7157 lb

Structure Notes:



1. PER ASTM C-478 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: PER ASTM A615
4. NO INVERT CHANNEL
5. CASTING SUPPLIED BY OTHERS (HOE 470 FRAME, GRATE, & CURB HOOD)

Rim: 701.25' Rim to Invert: 4.37' Slack: 0.94" Sump: 3.5" Step Position: 260°


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	696.88'	0°	0"	30" HDPE	35.1"	Hole 38	38"	41.151"	0.95"	0"
Invert 2	696.88'	160°	100.531"	30" RCP B WALL	37"	DOGHOUSE INVRTD 40"x41"	40" x 41"	43.784"	0"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)



INSIDE WALL DIMENSIONS

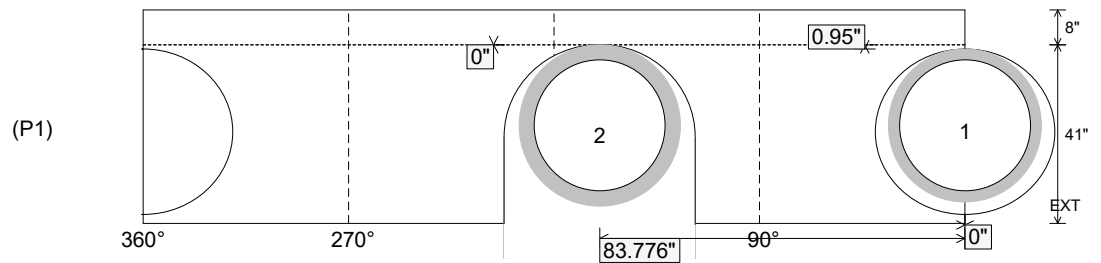

Coating (Int):
 Coating (Ext):

Seam Up: Flat
 Seam Dn: n/a

Wall Thickness: 6"
 Floor Height: 8"

Height (Int): 41"
 Height (Ext): 49"

Weight (Net): 5612 lb
 Volume (Net): 1.43cu.yd
