

Contractor: Ottenweller Contracting, LLC.

TECH: Jared - F

Plant: 100



Size: 120" x 120"

Rim to Invert: 11.25'


Floor Height: 10"

Slack: 0"


REINFORCING PER ATTACHED DRAWINGS & CAL'S.

STRUCTURE SUMMARY:


Structure Total: 78409 lb

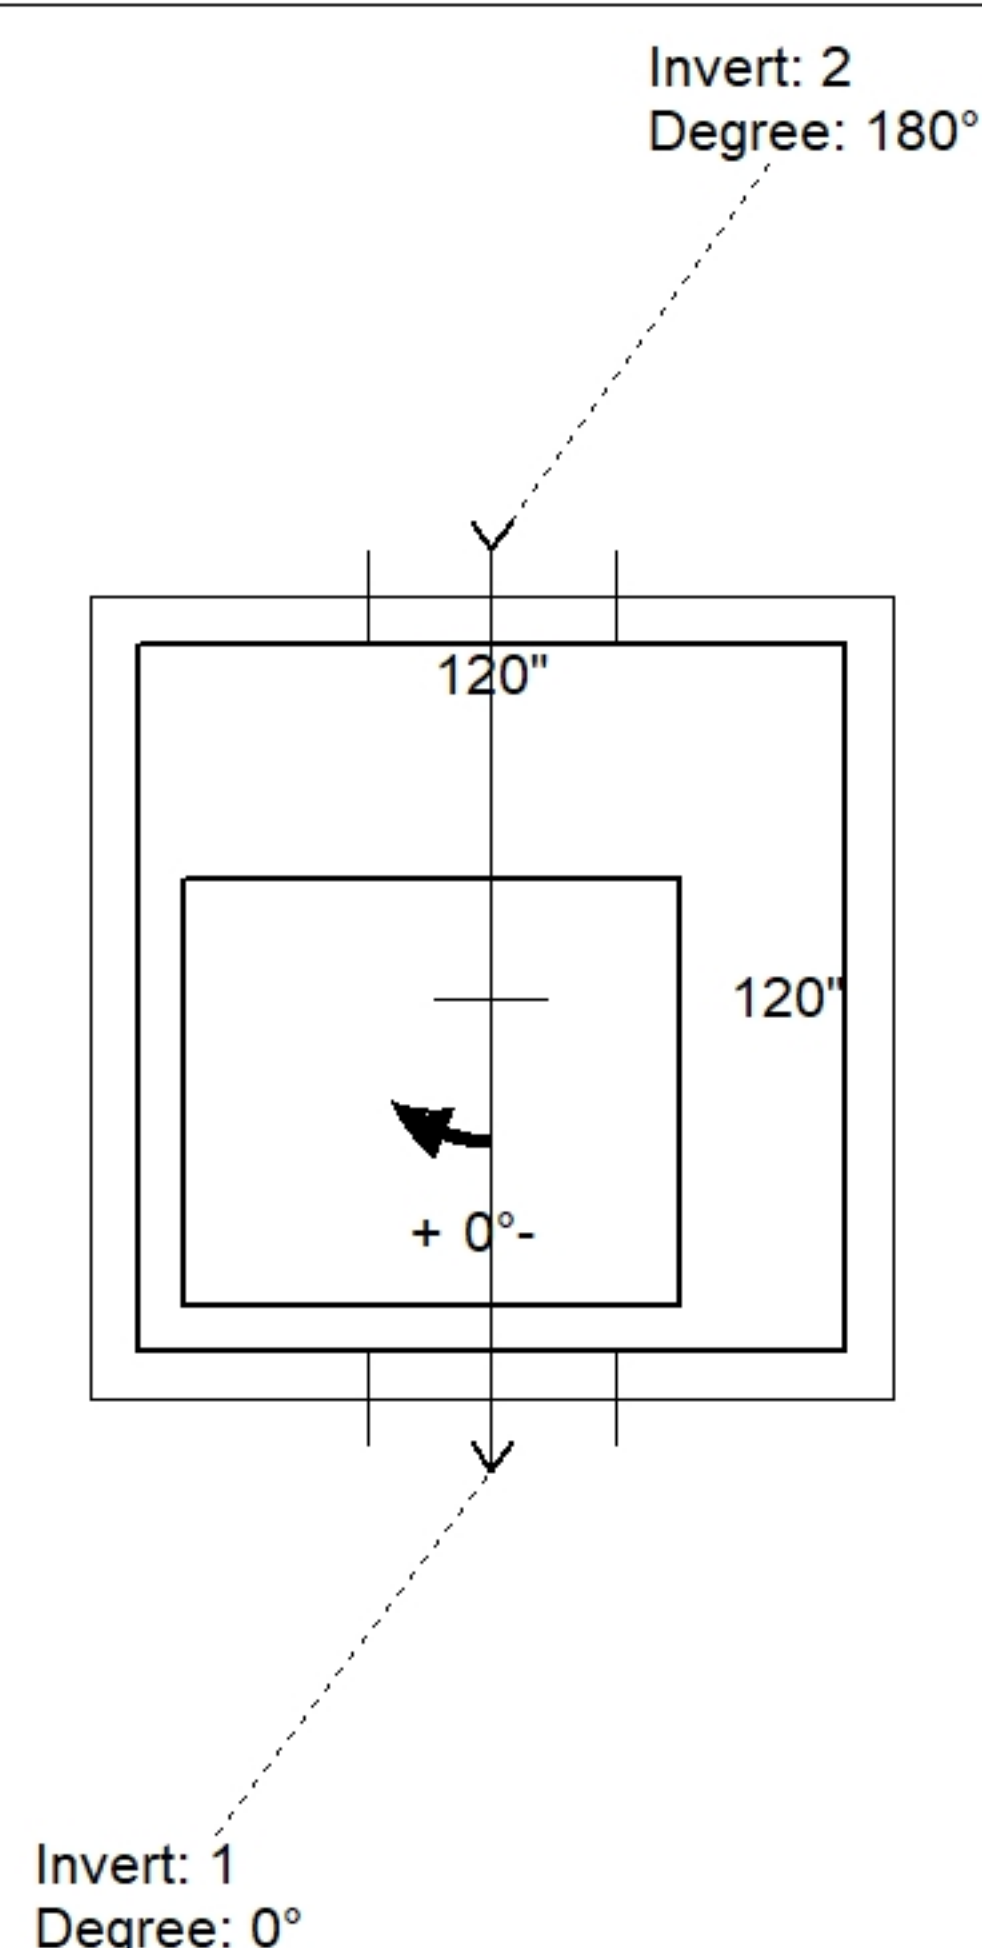

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	460'							
Reducer								
Invert 1	448.75'	0°	36" DI	38.5"	42"	Kor-N-Seal2 S206-42	21"	P1
Invert 2	448.75'	180°	36" DI	38.5"	42"	Kor-N-Seal2 S206-42	21"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

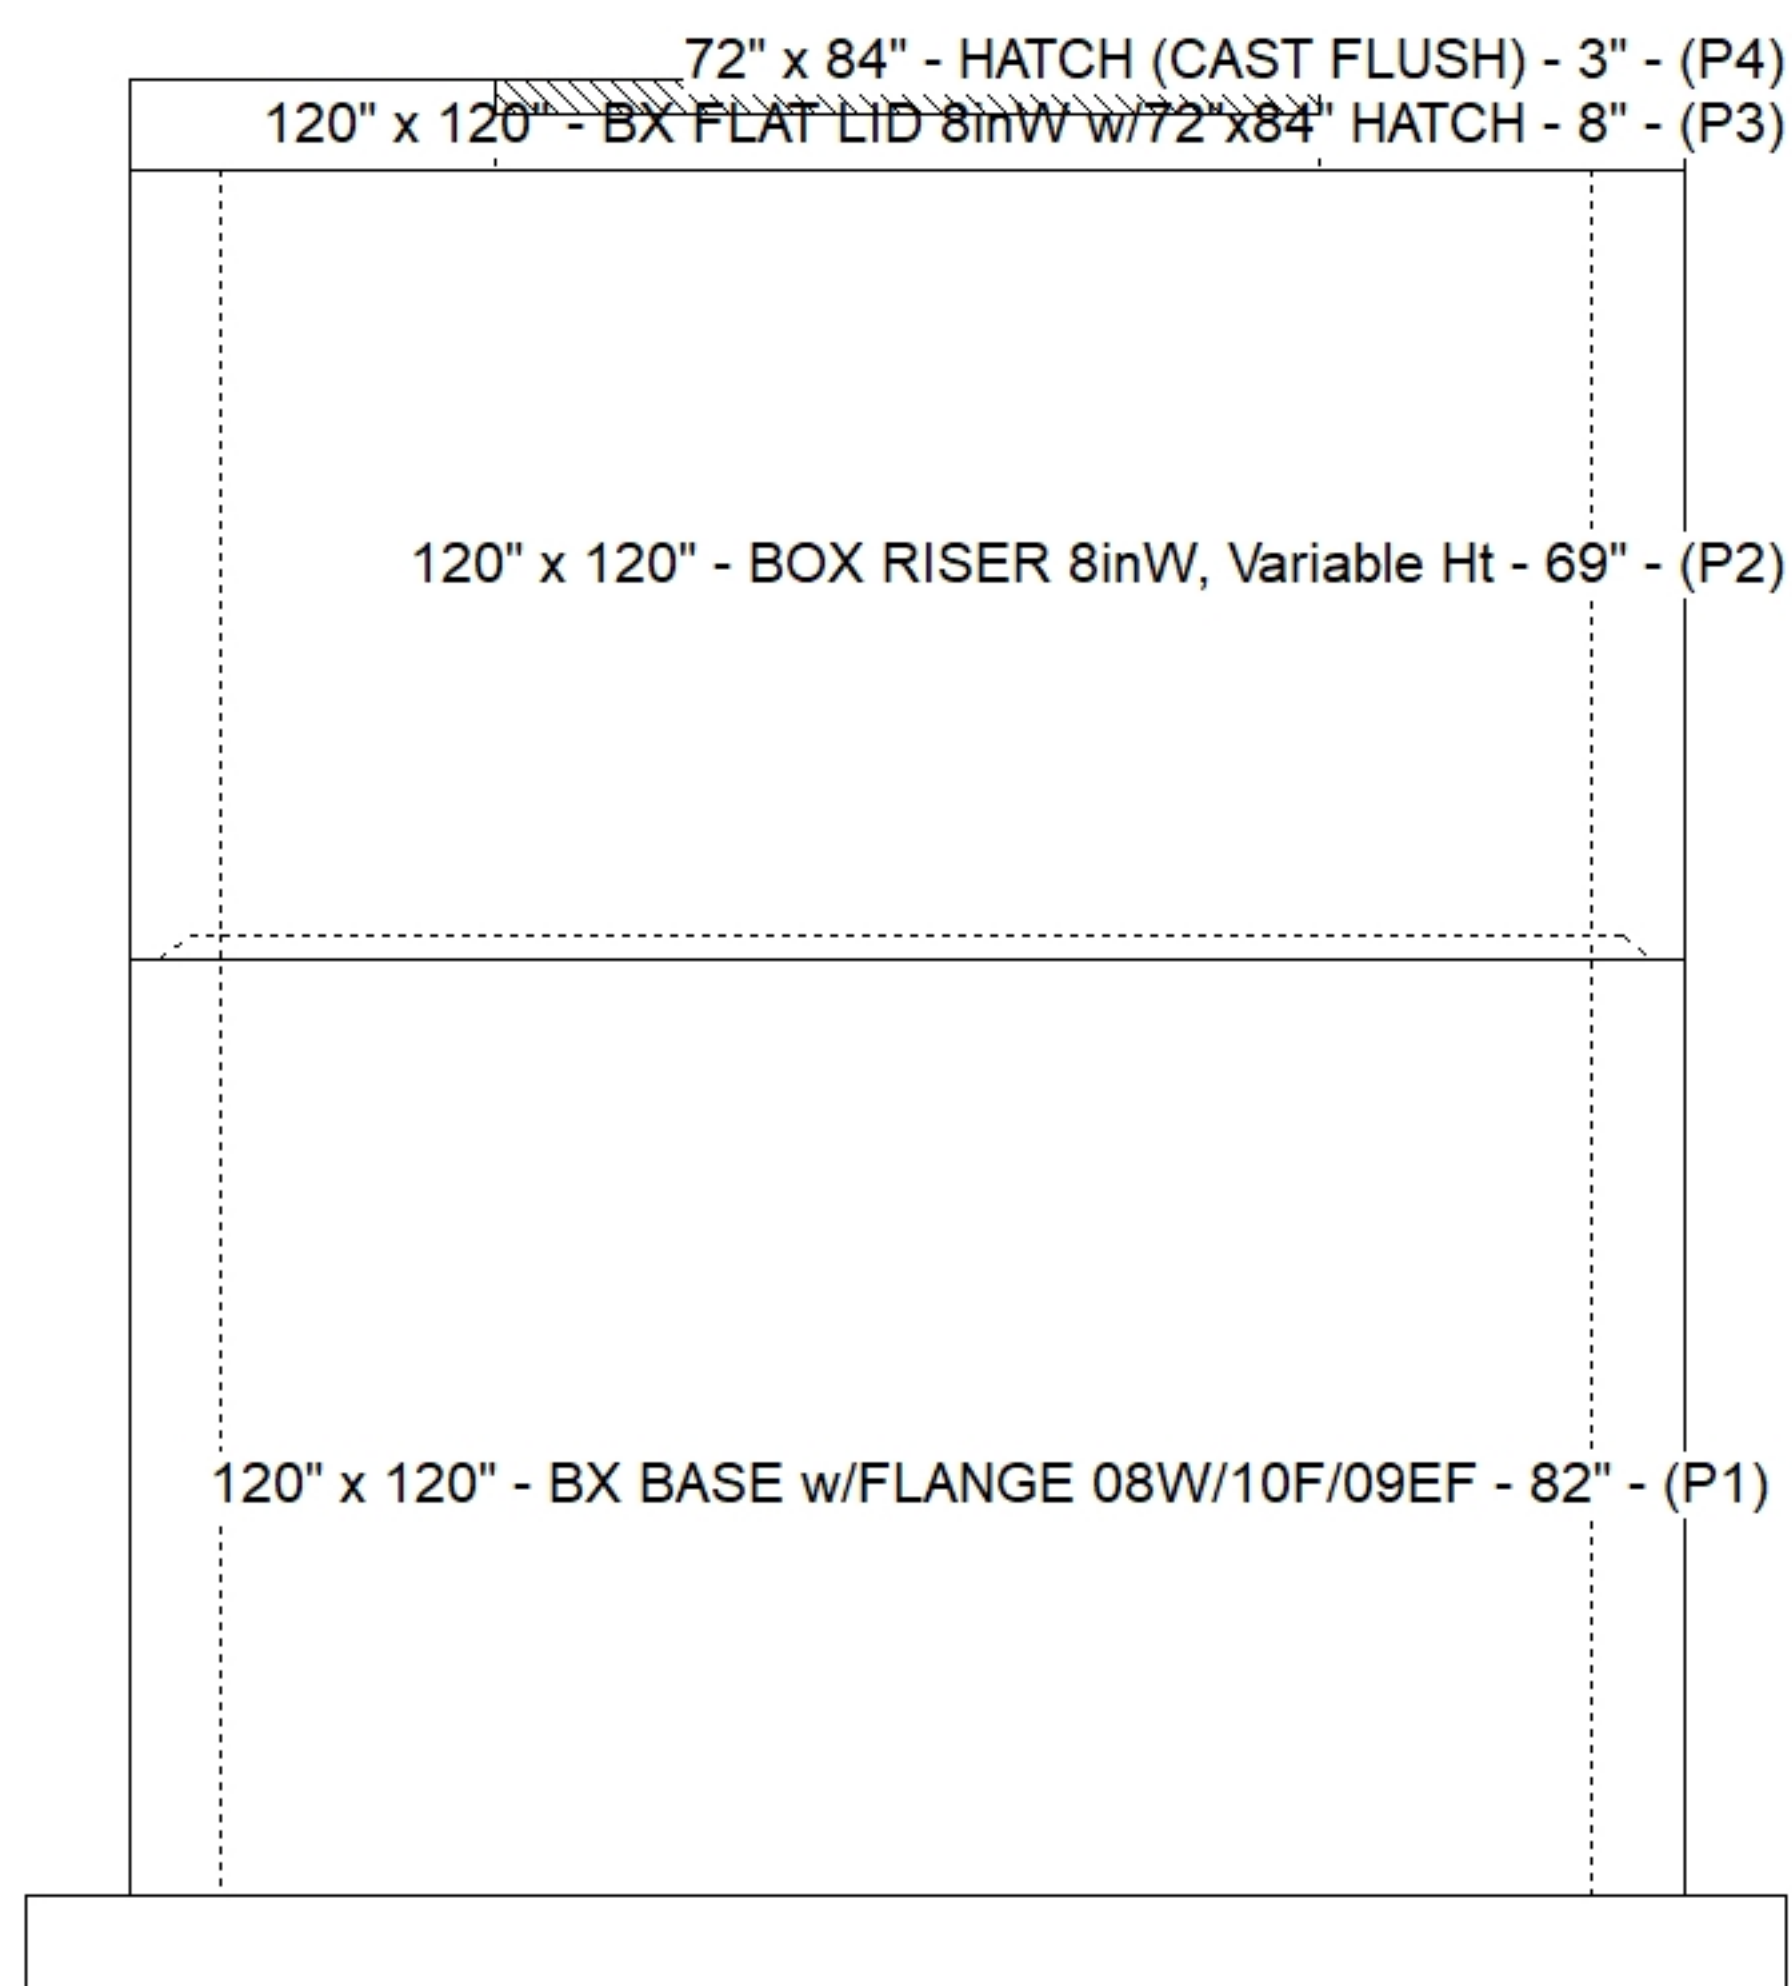

Default - Interior Dimensions

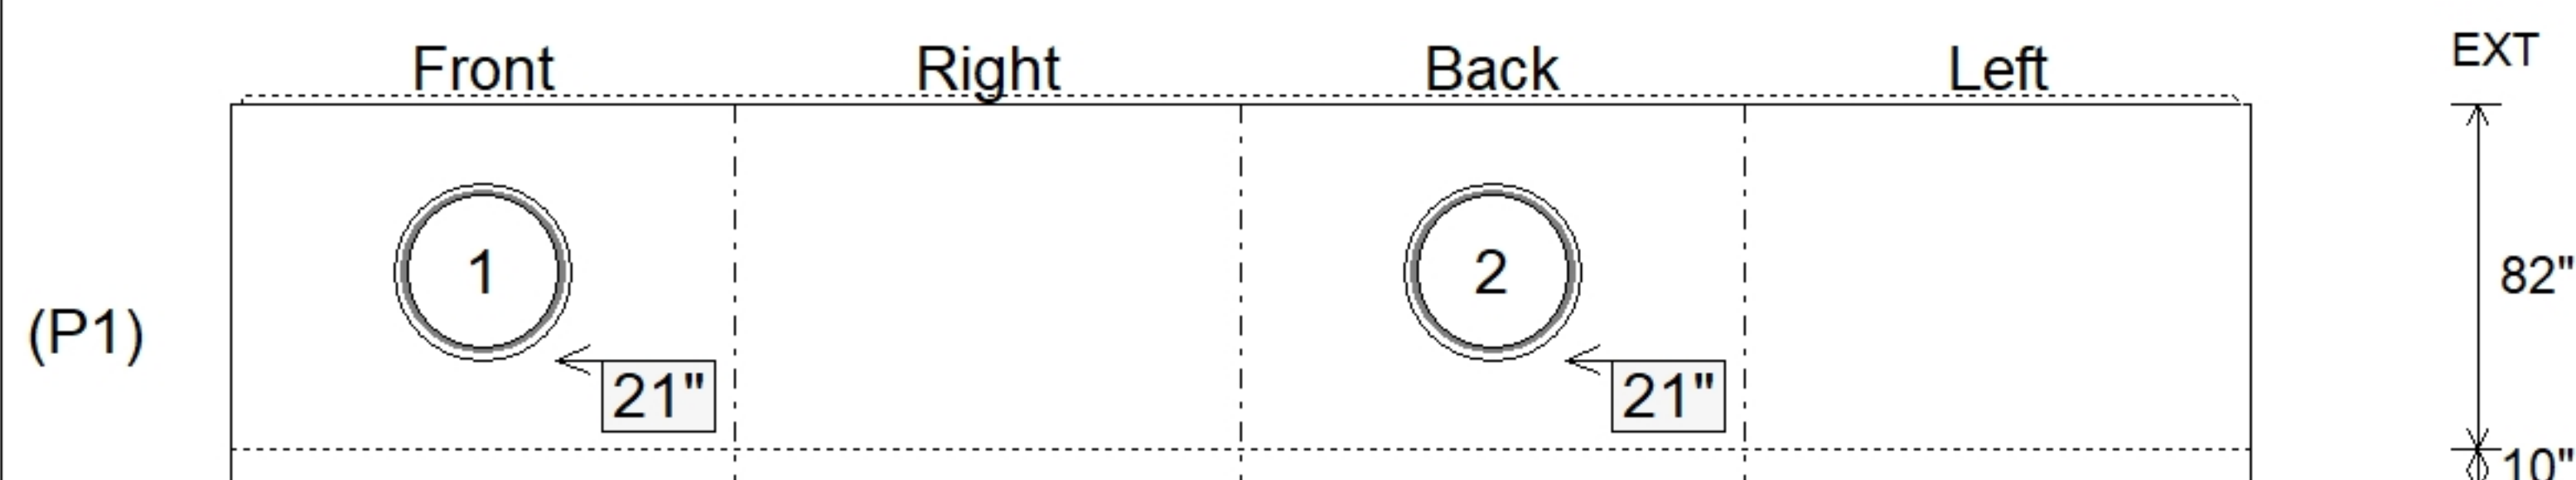

Submittal Drawing
7/9/2026 2:06:15 PM

SUBMITTAL
APPROVED BY:
