

Contractor: William & Charles Construction, LLC

Plant: 100



Slack: 2.02"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .12)
- FLOOR (As .62) #5 BARS AT 6" C.C.E.W.


P3) 24" x 46" CASTING HEIGHT - 8"
P2) 60" - MH FLAT TOP w/24"x46" Hole - 13"
P1) 60" - MH BASE Custom Ht - 60"
1) HOE R-3287-5 INDOT Type 5 FRAME & GRATE
2) Hole - 26
5) MH Step ML-10-TDS-NCR - 10"

0 lb
2313 lb
8274 lb
250 lb
0 lb
0 lb


Structure Total: 10837 lb

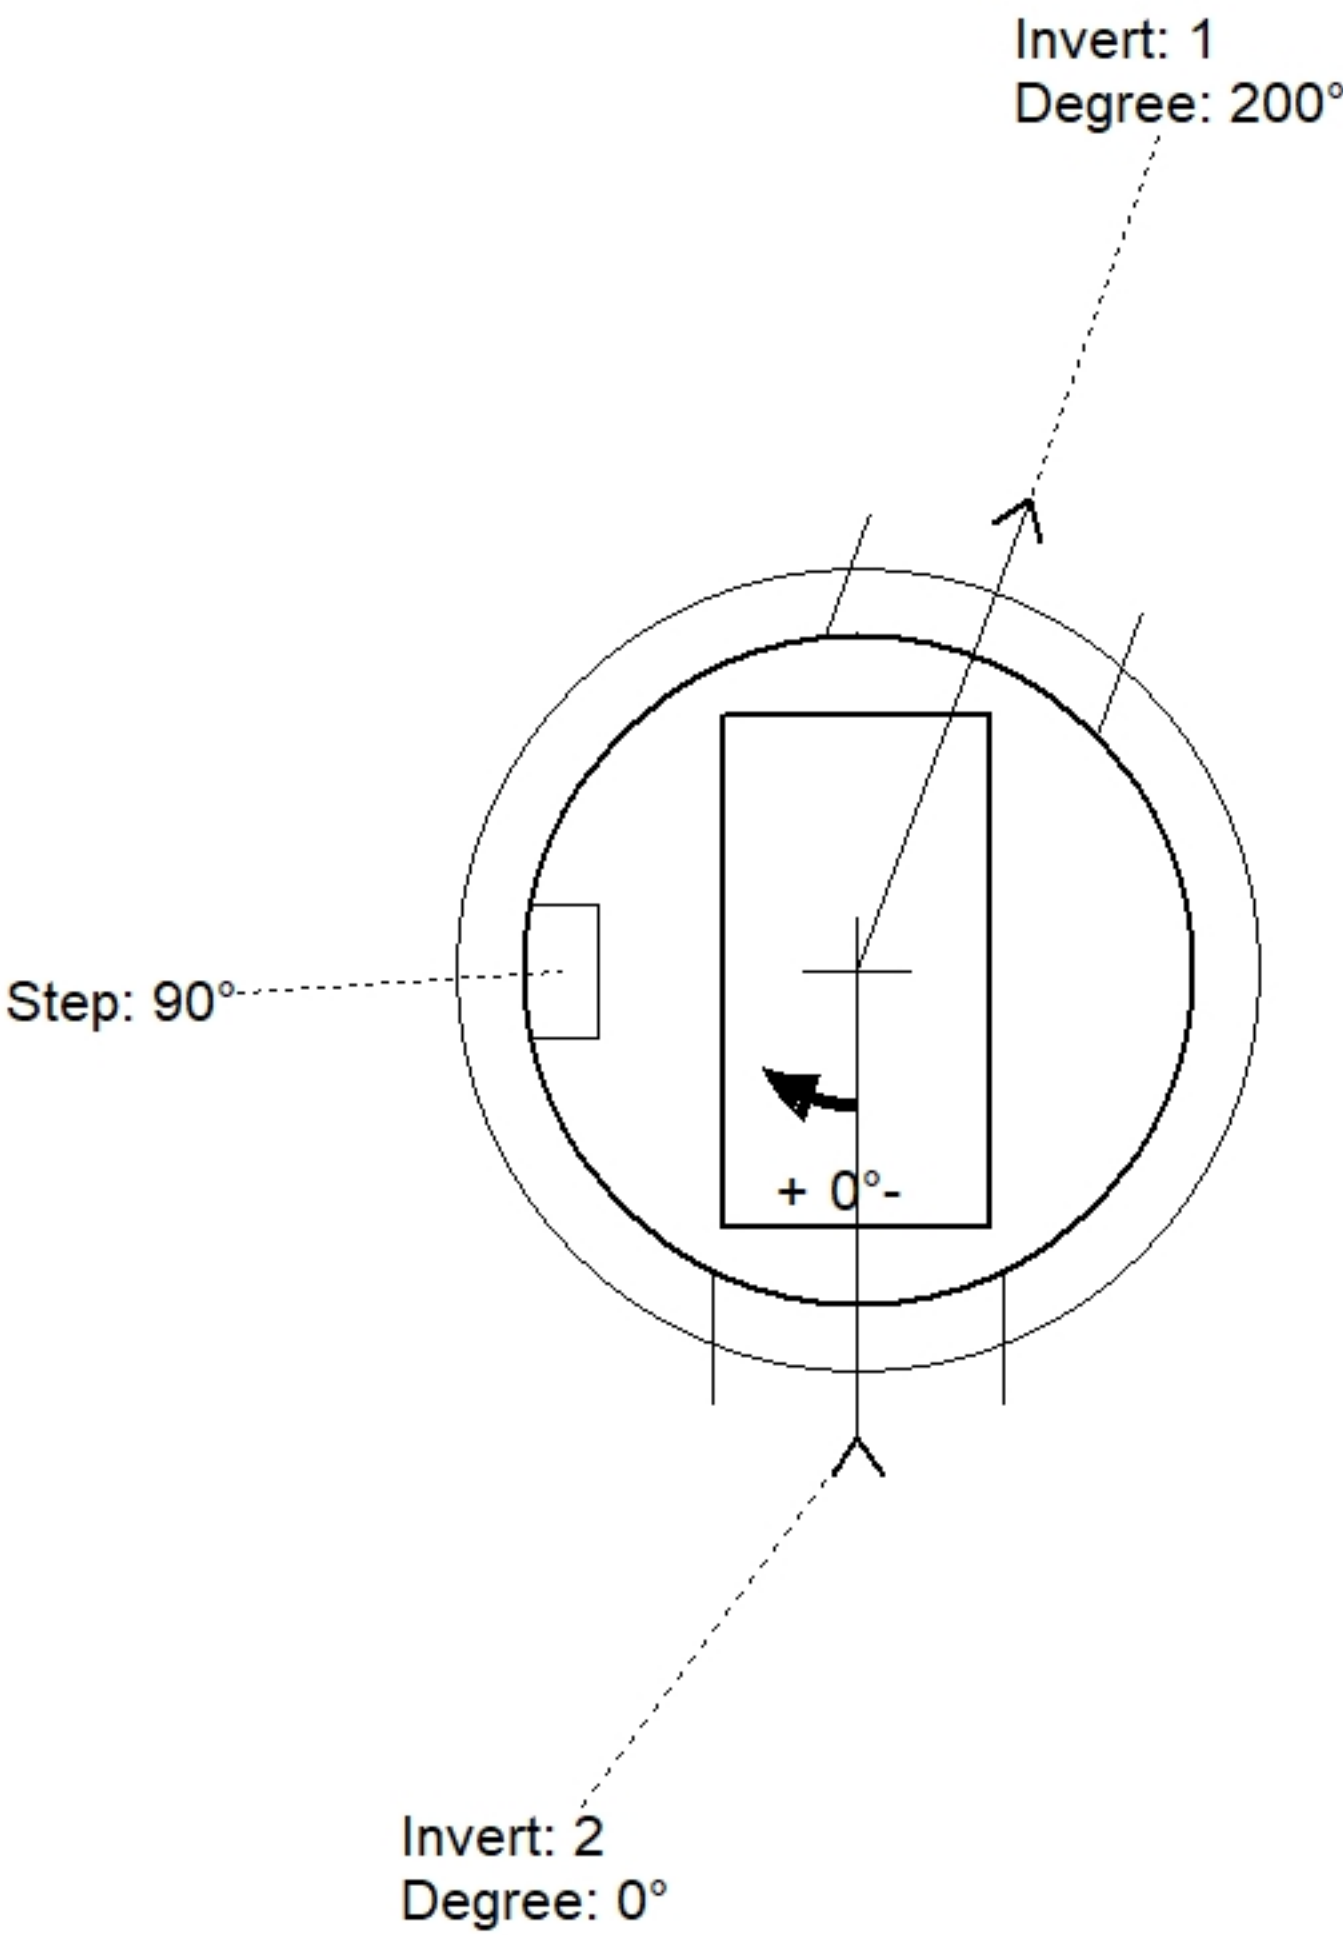

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	567.22'							
Reducer								
Invert 1	560.51'	200°	18" RCP B WALL	23"	26"	Hole 26	0"	P1
Invert 2	560.51'	0°	18" RCP B WALL	23"	26"	Hole 26	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

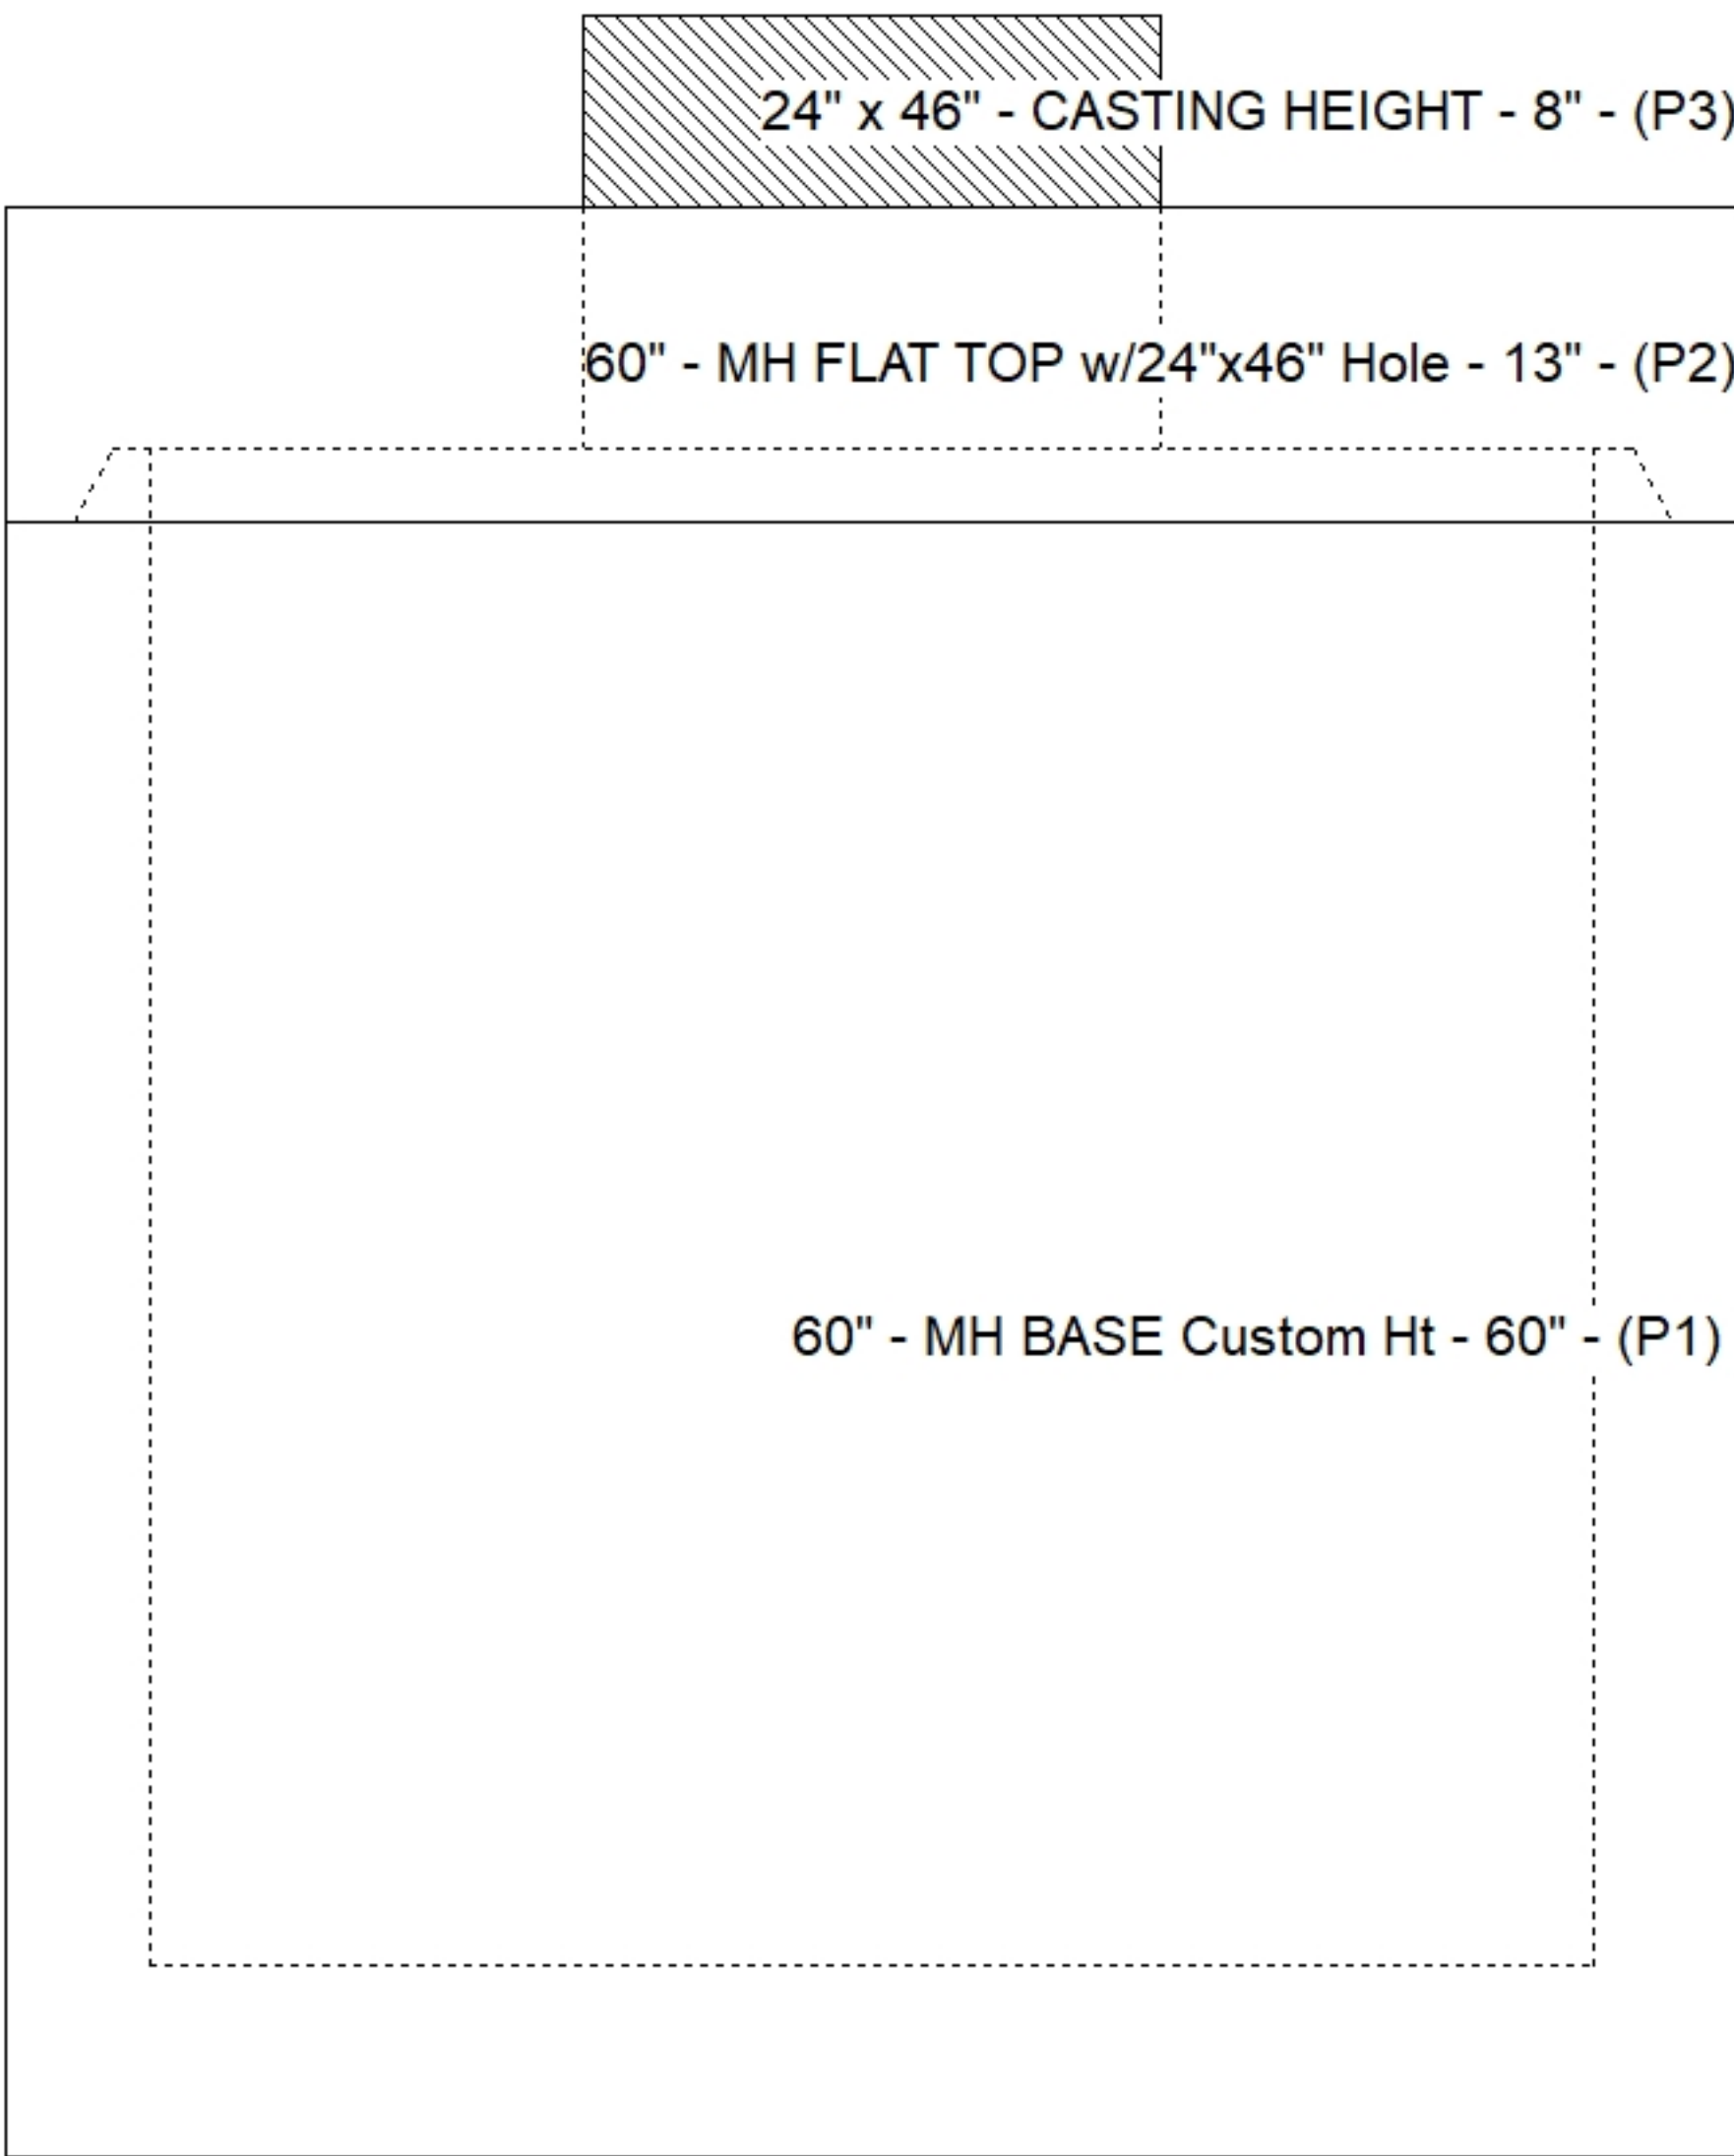

Default - Interior Dimensions

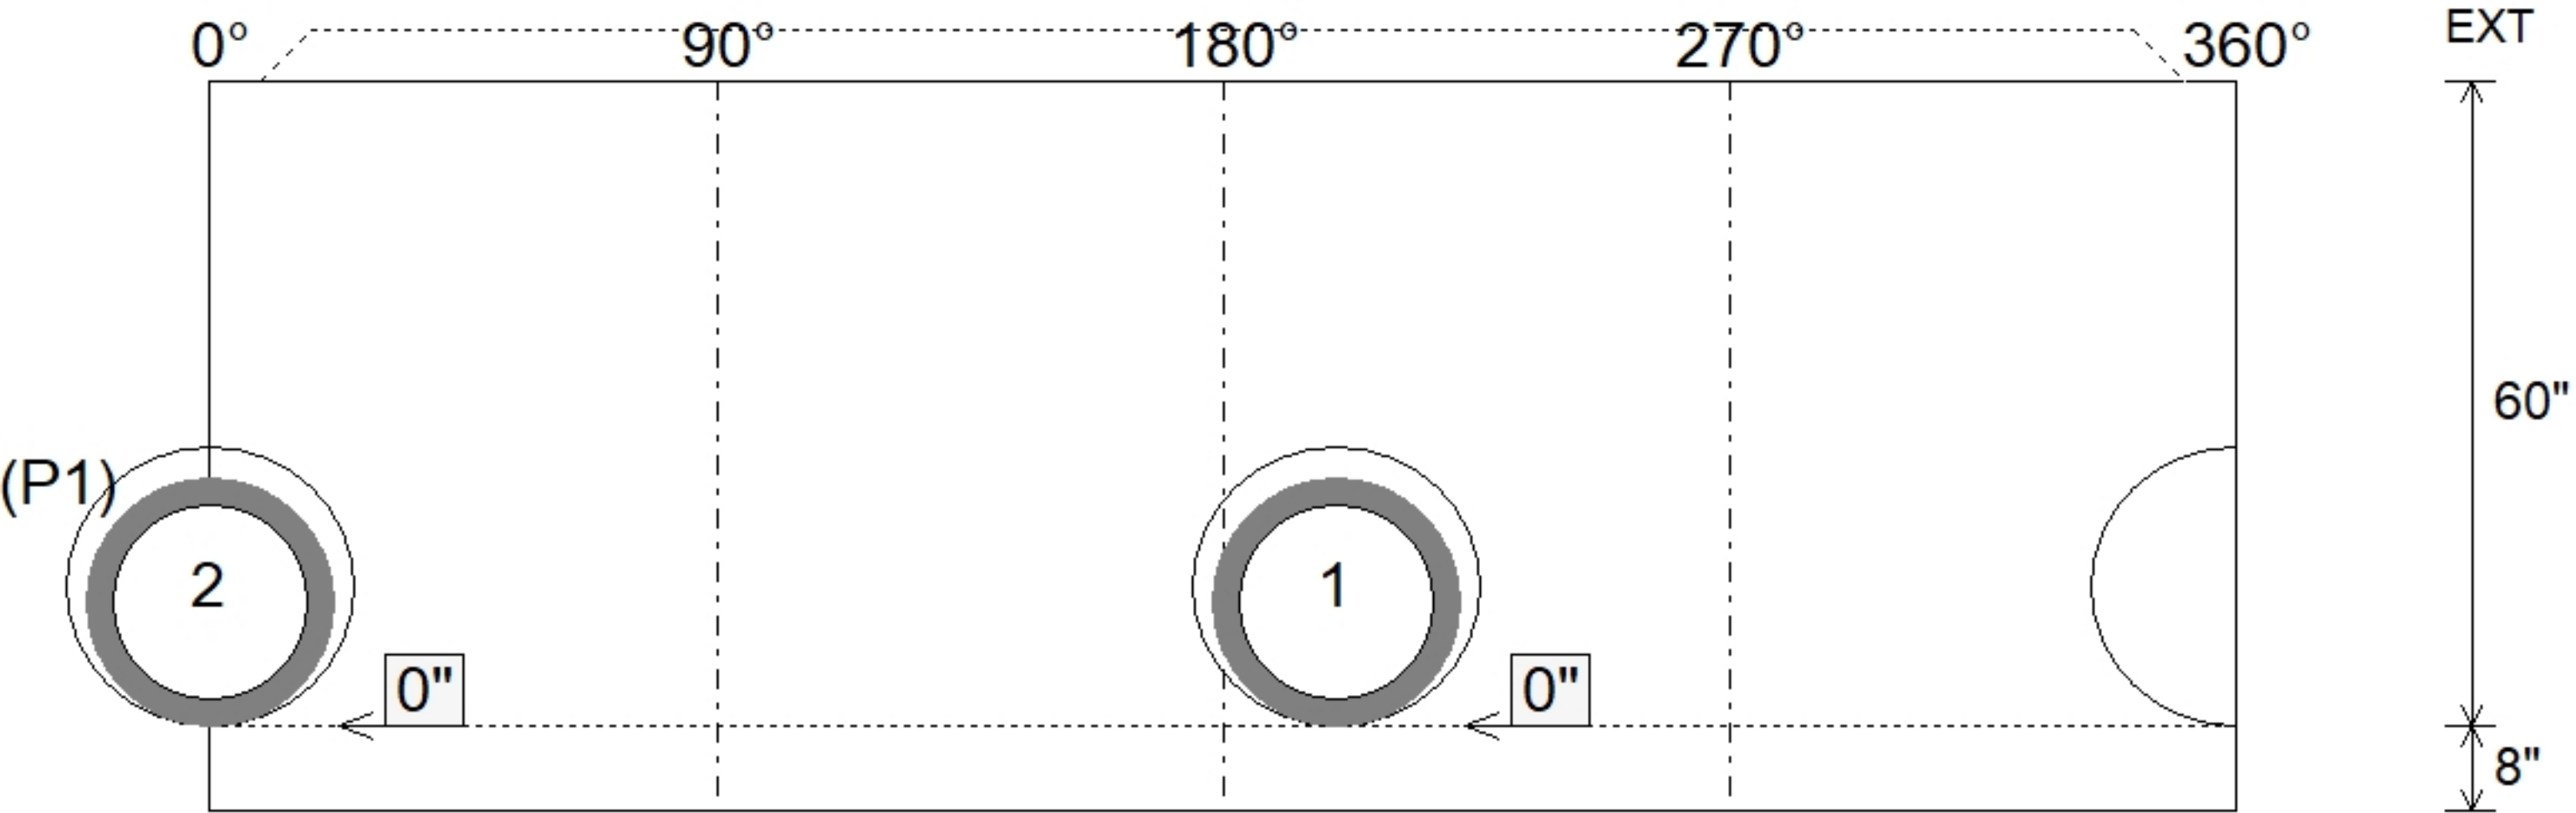

Submittal Drawing
9/24/2026 1:01:17 PM

SUBMITTAL
APPROVED BY:
