

Job Name: 25-4490P1 Heartland Meadows Subdivision  
Job Location: Elizabethtown, KY 40165  
Contractor: Kauffeld Brothers Construction

Plant: 100  
7/23/2026 12:04:56 PM

Tech: Jared - A  
PC: Celina Goff



Structure ID: MH 1-1 (8)



P3 MH048CN36

ECC CONE w/ 24" HOLE

- P5) 24" - CASTING HEIGHT - 7"  
P4) 24" - GRADE RING - 4"  
P3) 48" - ECC CONE w/ 24" HOLE - 36"  
P2) 48" - MH RISER - 36"  
P1) 48" - MH BASE - 30"  
1) 48" - MH INVERT CHANNEL - FULL HEIGHT  
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212  
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)  
1) CASTING - HOE MC-375 F/C Sanitary  
2) 48" - Conseal CS-102 1.00" (Double)  
2) 24" - Conseal CS-102 1.00" (Double)  
1) PSX - 12-08 NYLO  
2) PSX - 12-06 NYLO  
8) MH Step ML-10-TDS-NCR - 10"

- 0 lb  
270 lb  
3000 lb  
2515 lb  
3282 lb  
1440 lb  
0 lb  
0 lb  
271 lb  
0 lb  
0 lb  
8 lb  
16 lb  
0 lb
- Structure Notes: .  
1. HOE MC-375 F/C "SANITARY" PROVIDED BY ICAST.  
2. PER ASTM C478 SPECIFICATIONS.  
3. CONCRETE = 4,000 PSI AT 28 DAYS.  
4. REINFORCING PER ASTM A615 (GRADE 60).  
- CONE (As .12)  
- RISER/WALLS (As .12)  
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 10802 lb

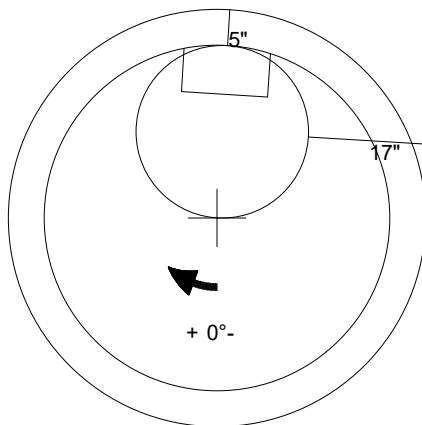

48" - ECC CONE w/ 24" HOLE - 36" - (P3)

Coating (Int):  
Coating (Ext):

Seam Up: Flat  
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 36"

Weight (Net): 3000 lb  
Volume (Net): 0.5cu.yd
